

MELBOURNE AIRPORT

Method of Working Plan

Airfield Pavement Maintenance

YMML 2023/4

AFO-AW-PLN-07-0012

Version 1.0

MOWP Approval date	03/08/2023
MOWP Commencement date	18/08/2023
MOWP Expiry	30/08/2025
Works Complete	30/08/2025

Document Number	AFO-AW-PLN-07-0012		
Version Number	Version 1.0		
Originator	Airfield Works Coordinator APAM	Date	20/07/2023
Approver	Head of Airfield, APAM	Date	03/08/2023

Contents

Definitions.....	10
Important Contacts.....	10
1. Works Information.....	11
1.1. Conditions of this method of working plan	11
1.2. Project Scope and affected aerodrome facilities.....	11
1.3. Works sequence.....	11
1.3.1. Runways.....	11
1.3.2. Taxiways.....	11
2. Restrictions to Aircraft Operations	14
2.1. Restrictions by works stages.....	14
2.1.1. Stage R1.....	14
2.1.2. Stage R2.....	15
2.1.3. Stage R3.....	16
2.1.4. Stage R4.....	17
2.1.5. Stage R5.....	18
2.1.6. Stage T1.....	19
2.1.7. Stage T2.....	19
2.1.8. Stage T3.....	20
2.1.9. Stage T4.....	21
2.1.10. Stage T5.....	22
2.1.11. Stage T6.....	23
2.1.12. Stage T7.....	23
2.1.13. Stage T8.....	24
2.1.14. Stage T9.....	25
2.1.15. Stage T10.....	26
2.1.16. Stage T11.....	27
2.1.17. Stage T12.....	28
2.1.18. Stage T13.....	28
2.1.19. Stage T14.....	29
2.1.20. Stage T15.....	30
2.1.21. Stage T16.....	31
2.1.22. Stage T17.....	31
2.1.23. Stage T18.....	32

2.1.24.	Stage T19.....	33
2.1.25.	Stage T20.....	34
2.1.26.	Stage T21.....	35
2.1.27.	Stage T22.....	36
2.1.28.	Stage T23.....	37
2.1.29.	Stage T24.....	37
2.1.30.	Stage T25.....	38
2.1.31.	Stage T26.....	39
2.1.32.	Stage T27.....	40
2.1.33.	Stage T28.....	40
2.1.34.	Stage T29.....	41
2.1.35.	Stage T30.....	42
2.1.36.	Stage T31.....	43
2.1.37.	Stage T32.....	43
2.1.38.	Stage T33.....	44
2.1.39.	Stage T34.....	45
2.1.40.	Stage T35.....	46
2.1.41.	Stage T36.....	46
2.1.42.	Stage T37.....	47
2.1.43.	Stage T38.....	48
2.1.44.	Stage T39.....	49
2.1.45.	Stage T40.....	49
2.1.46.	Stage T41.....	50
2.1.47.	Stage T42.....	51
2.1.48.	Stage T43.....	52
2.1.49.	Stage T44.....	52
2.1.50.	Stage T45.....	53
2.1.51.	Stage T46.....	54
2.1.52.	Stage T47.....	55
2.1.53.	Stage T48.....	55
2.1.54.	Stage T49.....	56
2.1.55.	Stage T50.....	57
2.1.56.	Stage T51.....	58
2.1.57.	Stage T52.....	59

2.1.58.	Stage T53.....	60
2.1.59.	Stage T54.....	60
2.1.60.	Stage T55.....	61
2.1.61.	Stage T56.....	62
2.1.62.	Stage T57.....	63
2.1.63.	Stage T58.....	64
2.1.64.	Stage T59.....	64
2.1.65.	Stage T60.....	65
2.1.66.	Stage T61.....	66
2.1.67.	Stage T62.....	67
2.1.68.	Stage T63.....	68
2.1.69.	Stage T64.....	69
2.1.70.	Stage T65.....	70
2.1.71.	Stage T66.....	70
2.1.72.	Stage T67.....	71
2.1.73.	Stage T68.....	72
2.1.74.	Stage T69.....	73
2.1.75.	Stage T70.....	74
2.1.76.	Stage T71.....	75
2.1.77.	Stage T72.....	75
2.1.78.	Stage T73.....	76
2.1.79.	Stage T74.....	77
2.1.80.	Stage T75.....	78
2.1.81.	Stage T76.....	79
2.1.82.	Stage T77.....	80
2.1.83.	Stage T78.....	80
2.1.84.	Stage T79.....	81
2.1.85.	Stage T80.....	82
2.1.86.	Stage T81.....	83
2.1.87.	Stage T82.....	83
2.1.88.	Stage T83.....	84
2.1.89.	Stage T84.....	85
2.1.90.	Stage T85.....	86
2.1.91.	Stage T86.....	86

2.1.92.	Stage T87	87
2.1.93.	Stage T88.....	88
2.1.94.	Stage T89.....	89
2.1.95.	Stage T90.....	90
2.2.	Weather conditions	90
2.3.	Airport emergencies	91
2.4.	NOTAM or other change to AIP	91
2.5.	Restoration of normal safety standards	91
2.6.	Restrictions on the organisation carrying out aerodrome works	91
3.	Personnel and Equipment.....	92
3.1.	Requirement to vacate the movement area	92
3.2.	Working hours on site.....	92
3.3.	Melbourne Airport operational policies	92
3.4.	Site restriction markings/lighting.....	92
3.5.	Access to the work site	92
3.6.	Traffic management plans	93
3.7.	Marking and lighting of vehicles	93
3.8.	Vehicle / equipment height limit	93
3.9.	Speed limits.....	94
3.10.	Parking of private vehicles	94
3.11.	Control of works personnel.....	94
3.12.	Personal protective equipment (PPE) for the airside environment	94
4.	Aerodromes Markers, Markings and Lights.....	95
4.1.	General.....	95
4.2.	Lights	95
4.3.	Procedure for protection of electrical services and control cables	95
5.	Special Requirements	95
5.1.	Airport security	95
5.2.	Permits	96
5.2.1.	Permit to commence works	96
5.2.2.	Hot works permit	96
5.2.3.	Excavation permit	97
5.2.4.	Crane permit	97
5.2.5.	Electrical isolation permit	97

5.3.	Critical obstacles	98
5.3.1.	General requirements.....	98
5.3.2.	Height and location of critical obstacles.....	98
5.4.	Pavement and cleanliness.....	98
5.5.	Waste disposal and environment protection	98
5.6.	Explosives.....	99
5.7.	Dust.....	99
5.8.	Dumping of fill.....	99
5.9.	Site sheds and locations.....	99
5.10.	Food consumption	99
5.11.	Smoking.....	99
5.12.	Wildlife hazards.....	99
5.13.	Lime and cement stabilisation	100
5.14.	Inspection at the completion of works.....	100
6.	Administration	101
6.1.	Contractors	101
6.2.	Project Manager.....	101
6.3.	Works Organiser	101
6.4.	Airfield Operations and Works Coordinator	101
6.5.	Works Safety Officer	101
6.6.	MOWP Author.....	102
7.	Authority.....	103
7.1.	Conduct of Works	103
7.2.	Expiry.....	103
7.3.	Variation.....	103
7.4.	Approval.....	103
8.	Drawings	104
8.1.	Stage R1.....	104
8.2.	Stage R2.....	105
8.3.	Stage R3.....	106
8.4.	Stage R4.....	107
8.5.	Stage R5.....	108
8.6.	Stage T1.....	109
8.7.	Stage T2.....	110

8.8.	Stage T3.....	111
8.9.	Stage T4.....	112
8.10.	Stage T5.....	113
8.11.	Stage T6.....	114
8.12.	Stage T7.....	115
8.13.	Stage T8.....	116
8.14.	Stage T9.....	117
8.15.	Stage T10.....	118
8.16.	Stage T11.....	119
8.17.	Stage T12.....	120
8.18.	Stage T13.....	121
8.19.	Stage T14.....	122
8.20.	Stage T15.....	123
8.21.	Stage T16.....	124
8.22.	Stage T17.....	125
8.23.	Stage T18.....	126
8.24.	Stage T19.....	127
8.25.	Stage T20.....	128
8.26.	Stage T21.....	129
8.27.	Stage T22.....	130
8.28.	Stage T23.....	131
8.29.	Stage T24.....	132
8.30.	Stage T25.....	133
8.31.	Stage T26.....	134
8.32.	Stage T27.....	135
8.33.	Stage T28.....	136
8.34.	Stage T29.....	137
8.35.	Stage T30.....	138
8.36.	Stage T31.....	139
8.37.	Stage T32.....	140
8.38.	Stage T33.....	141
8.39.	Stage T34.....	142
8.40.	Stage T35.....	143
8.41.	Stage T36.....	144

8.42.	Stage T37.....	145
8.43.	Stage T38.....	146
8.44.	Stage T39.....	147
8.45.	Stage T40.....	148
8.46.	Stage T41.....	149
8.47.	Stage T42.....	150
8.48.	Stage T43.....	151
8.49.	Stage T44.....	152
8.50.	Stage T45.....	153
8.51.	Stage T46.....	154
8.52.	Stage T47.....	155
8.53.	Stage T48.....	156
8.54.	Stage T49.....	157
8.55.	Stage T50.....	158
8.56.	Stage T51.....	159
8.57.	Stage T52.....	160
8.58.	Stage T53.....	161
8.59.	Stage T54.....	162
8.60.	Stage T55.....	163
8.61.	Stage T56.....	164
8.62.	Stage T57.....	165
8.63.	Stage T58.....	166
8.64.	Stage T59.....	167
8.65.	Stage T60.....	168
8.66.	Stage T61.....	169
8.67.	Stage T62.....	170
8.68.	Stage T63.....	171
8.69.	Stage T64.....	172
8.70.	Stage T65.....	173
8.71.	Stage T66.....	174
8.72.	Stage T67.....	175
8.73.	Stage T68.....	176
8.74.	Stage T69.....	177
8.75.	Stage T70.....	178

8.76.	Stage T71.....	179
8.77.	Stage T72.....	180
8.78.	Stage T73.....	181
8.79.	Stage T74.....	182
8.80.	Stage T75.....	183
8.81.	Stage T76.....	184
8.82.	Stage T77.....	185
8.83.	Stage T78.....	186
8.84.	Stage T79.....	187
8.85.	Stage T80.....	188
8.86.	Stage T81.....	189
8.87.	Stage T82.....	190
8.88.	Stage T83.....	191
8.89.	Stage T84.....	192
8.90.	Stage T85.....	193
8.91.	Stage T86.....	194
8.92.	Stage T87.....	195
8.93.	Stage T88.....	196
8.94.	Stage T89.....	197
8.95.	Stage T90.....	198
9.	Distribution List.....	199
9.1.	Further Information	199

Definitions

Please refer to the [Aeronautical Information Package](#) and the [CASA Website](#) for commonly used Aviation terms and abbreviations.

For additional definitions specific to Melbourne Airport, please visit www.melbourneairport.com.au/glossary.

Important Contacts

Title	Contact phone number	Contact email
Airfield Operations & Works Coordinators	+61 (03) 9297 1839	airfieldworkscoordinator@melair.com.au
Melbourne Airport Buildings Approvals Officer	+61 (03) 9297 1310	building.approval@melair.com.au
Fire & Life Safety Leader	n/a	FireImpairments@melair.com.au
Melbourne Airport – Airfield Lighting	n/a	airsidepermits@melair.com.au
Airfield Support	+61 (03) 8326 2525	cranepermits@melair.com.au
Car2	+61 418 335 985	n/a
Leanne Carroll	+61 (03) 9297 1839	Leanne.carroll@melair.com.au
Ron Butterworth	+61 (03) 9297 1165	Ronald.butterworth@melair.com.au
Project Manager	+61 437 533 152	Scott.erturk@melair.com.au
Works Organiser – Civil	+61 416 094 689	Tony.epenian@melair.com.au
Works Organiser - Lighting	+61 418 775 788	Gavan.saker@melair.com.au

1. Works Information

1.1. Conditions of this method of working plan

No changes to the conditions outlined in this Method of Working Plan (MOWP) can be made without the approval of the Airfield Operations and Works Coordinators.

1.2. Project Scope and affected aerodrome facilities.

The works undertaken as part of this MOWP are to ensure all parts of the airport are in a safe, serviceable, and compliant condition.

The actual date and time of the commencement of the work will be advised by a Notice to Airmen (NOTAM), and Local Works Plan (LWP) to be issued not less than 48 hours before works commence.

1.3. Works sequence

Due to the nature of the works being completed under this MOWP being reactive in nature there is no set sequence for these works. All stages may commence from the 18/08/2023 and be completed by 30/08/2025. Duration of each stage will vary depending on the works required to be completed. Works will be conducted at dates and times to best reduce impact to aircraft operations.

The actual date and time of commencement will be advised by a NOTAM, to be issued not less than 48 hours before work commences.

Actual dates and times will also be advised via the release of a Local Works Plan to affected stakeholders and will be updated to aircraft operators via the Aeronautical Information Publication including AIP-SUP, AIC, and NOTAM.

1.3.1. Runways

Stage R1 Runway 09/27
Stage R2 Runway 09/27 including the intersection of Taxiway Alpha
Stage R3 Runway 09/27 including the intersection of Taxiway Victor
Stage R4 Runway 16/34 including Taxiway's Alpha and Victor north of Runway 09/27
Stage R5 Runway 16/34 including Taxiway Charlie and Taxiway Victor north of Runway 09/27 (Bravo and Kilo Run-up Bay available)

1.3.2. Taxiways

Stage T1 Taxiway Alpha between Taxiway Juliet and Taxiway Whiskey
Stage T2 Taxiway Alpha between Taxiway Yankee and Taxiway Juliet
Stage T3 Taxiway Alpha between Taxiway Yankee and Taxiway Golf
Stage T4 Taxiway Alpha between Taxiway Uniform and Taxiway Golf
Stage T5 Taxiway Alpha between Taxiway Uniform and Taxiway Tango
Stage T6 Taxiway Alpha between Taxiway Tango and Taxiway Echo

Stage T7 Taxiway Alpha north of Taxiway Echo
Stage T8 Taxiway Alpha between Bravo Run Up Bay and Runway 09/27
Stage T9 Taxiway Bravo and Taxiway Alpha north of Taxiway Charlie
Stage T10 Taxiway Alpha between Runway 09/27 and Taxiway Charlie
Stage T11 Taxiway Sierra between Taxiway Juliet and Taxiway Whiskey
Stage T12 Taxiway Sierra between Taxiway Juliet and Taxiway Yankee
Stage T13 Taxiway Sierra between Taxiway Uniform and Taxiway Golf
Stage T14 Taxiway Sierra between Taxiway Echo and Taxiway Tango
Stage T15 Taxiway Victor south of Taxiway Yankee
Stage T16 Taxiway Victor between Taxiway Yankee and Taxiway Golf
Stage T17 Taxiway Victor between Taxiway Foxtrot and Taxiway Uniform
Stage T18 Taxiway Victor between Taxiway Foxtrot and Taxiway Golf and Taxiway Uniform between Taxiway Alpha and Taxiway Victor
Stage T19 Taxiway Kilo between Taxiway Alpha and Taxiway Kilo stop bar (westbound)
Stage T20 Taxiway Kilo between Taxiway Alpha and Taxiway Kilo Run-up Bay
Stage T21 Taxiway Whiskey between Taxiway Sierra and Taxiway Alpha
Stage T22 Taxiway Whiskey east of Taxiway Sierra
Stage T23 Taxiway Whiskey east of Whiskey 1
Stage T24 Taxiway Whiskey east of Whiskey 2
Stage T25 Taxiway Whiskey east of Whiskey 3
Stage T26 Whiskey 1 Taxilane
Stage T27 Whiskey 2 Taxilane
Stage T28 Whiskey 3 Taxilane
Stage T29 Taxiway Juliet west of Taxiway Victor
Stage T30 Taxiway Juliet between Taxiway Alpha and Taxiway Victor
Stage T31 Taxiway Juliet between Taxiway Alpha and Taxiway Sierra
Stage T32 Taxiway Yankee between Taxiway Alpha and Taxiway Victor
Stage T33 Taxiway Yankee between Taxiway Alpha and Taxiway Sierra
Stage T34 Taxiway Golf between Taxiway Alpha and Taxiway Victor
Stage T35 Taxiway Golf between Taxiway Sierra and Taxiway Alpha
Stage T36 Taxiway Uniform between Taxiway Alpha and Taxiway Victor
Stage T37 Taxiway Uniform between Taxiway Sierra and Taxiway Alpha
Stage T38 Taxiway Foxtrot between Taxiway Tango and Taxiway Echo and Taxiway Victor between Taxiway Tango and Taxiway Echo
Stage T39 Taxiway Tango between Taxiway Quebec and Taxiway Romeo
Stage T40 Taxiway Tango between Taxiway Quebec and Taxiway Papa
Stage T41 Taxiway Tango between Taxiway Sierra and Taxiway Papa
Stage T42 Taxiway Tango between Taxiway Sierra and Taxiway Alpha
Stage T43 Taxiway Tango between Taxiway Alpha and Taxiway Foxtrot
Stage T44 Taxiway Papa between Runway 09/27 and Taxiway Echo
Stage T45 Taxiway Papa between Taxiway Tango and Taxiway Echo
Stage T46 Taxiway Quebec north of Taxiway Echo
Stage T47 Taxiway November
Stage T48 Taxiway Mike and Taxiway Echo west of Taxiway November
Stage T49 Taxiway Echo between Taxiway Echo Stop bar (eastbound) and Taxiway Mike, Taxiway Mike between the Taxiway Mike stop bar (northbound) and Taxiway Echo and Taxiway November between the Taxiway November stop bar (northbound) and Taxiway Echo

Stage T50 Taxiway Echo between Runway 16/34 and Taxiway Foxtrot, Taxiway Victor between Taxiway Foxtrot and Taxiway Charlie
Stage T51 Taxiway Echo between Taxiway Sierra and Taxiway Alpha
Stage T52 Taxiway Echo between Taxiway Sierra and Taxiway Papa
Stage T53 Taxiway Echo between Taxiway Papa and Taxiway Quebec
Stage T54 Taxiway Echo between Taxiway Quebec and Taxiway Romeo
Stage T55 Intersection of Taxiway Alpha, Echo, and Foxtrot
Stage T56 Intersection of Taxiway Alpha and Taxiway Tango
Stage T57 Intersection of Taxiway Alpha and Taxiway Uniform
Stage T58 Intersection of Taxiway Golf and Taxiway Alpha
Stage T59 Intersection of Taxiway Alpha and Taxiway Yankee
Stage T60 Intersection of Taxiway Alpha and Taxiway Juliet
Stage T61 Intersections of Taxiway Alpha and Taxiway Whiskey
Stage T62 Intersection of Taxiway Whiskey and Taxiway Sierra
Stage T63 Intersection of Taxiway Sierra and Taxiway Juliet
Stage T64 Intersection of Taxiway Sierra and Taxiway Yankee
Stage T65 Intersection of Taxiway Sierra and Taxiway Golf
Stage T66 Intersection of Taxiway Sierra and Taxiway Uniform
Stage T67 Intersection of Taxiway Tango and Taxiway Sierra
Stage T68 Intersection of Taxiway Victor and Taxiway Juliet
Stage T69 Intersection of Taxiway Victor and Taxiway Yankee
Stage T70 Intersection of Taxiway Victor and Taxiway Golf
Stage T71 Intersection of Taxiway Victor, Taxiway Foxtrot and Taxiway Tango
Stage T72 Intersection of Taxiway Quebec and Taxiway Echo
Stage T73 Intersection of Taxiway Romeo and Taxiway Tango
Stage T74 Intersection of Taxiway Echo and Taxiway Papa
Stage T75 Intersection of Taxiway Echo and Taxiway Sierra
Stage T76 Intersection of Taxiway Tango and Taxiway Quebec
Stage T77 Intersection of Taxiway Tango and Taxiway Papa
Stage T78 Taxilane Romeo
Stage T79 Taxilane Quebec
Stage T80 Taxilane Papa
Stage T81 Taxilane Uniform
Stage T82 Taxilane Golf
Stage T83 Taxilane Yankee
Stage T84 Taxilane Juliet
Stage T85 Taxiway Golf between Runway 16/34 and Taxiway Victor
Stage T86 Taxiway Foxtrot between Runway 16/34 and Taxiway Victor
Stage T87 Taxiway Charlie and Taxiway Victor between Runway 09/27 and Taxiway Charlie
Stage T88 Intersection of Taxiway Foxtrot and Taxiway Echo
Stage T89 Taxiway Victor between Taxiway Echo and Taxiway Charlie
Stage T90 Taxiway Victor between Runway 09/27 and Taxiway Charlie

2. Restrictions to Aircraft Operations

2.1. Restrictions by works stages.

2.1.1. Stage R1

Stage R1	
Description of works	Runway 09/27 involves manoeuvring area maintenance, visual aid maintenance and electrical works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Runway 09/27 not available
Taxiways	Taxiway Papa north of Taxiway Echo not available Taxiway Quebec north of Taxiway Echo not available Taxiway Mike not available Taxiway November not available Taxiway Echo west of Runway 16/34 not available
Aircraft type restrictions	Not applicable
RWY NOTAM	(A) MELBOURNE (B) (START DATE) (C) (FINISH DATE) MOWP YMML 2023/4 STAGE R1 RWY 09/27 CLSD DUE WIP
TWY NOTAM	(A) MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE R1 TWY M AND TWY N CLSD DUE WIP TWY P NORTH OF TWY E CLSD TWY Q NORTH OF TWY E CLSD TWY E WEST OF RWY 16/34 CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Works on this stage will only be undertaken when the prevailing wind conditions do not dictate the essential use of Runway 09/27.
Drawing	Stage R1

2.1.2. Stage R2

Stage R2	
Description of works	Runway 09/27 involves manoeuvring area maintenance, visual aid maintenance and electrical works
Scheduled start date	18/08/2023
Scheduled end date	30/06/2025
Restrictions: Manoeuvring Area	
Runways	Runway 09/27 not available
Taxiways	Taxiway Papa north of Taxiway Echo not available Taxiway Quebec north of Taxiway Echo not available Taxiway Alpha between Taxiway Echo and Taxiway Charlie not available Taxiway Mike not available Taxiway November not available Taxiway Echo west of Runway16/34 not available
Aircraft type restrictions	Not applicable
RWY NOTAM	(A) MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE R2 RWY 09/27 CLSD DUE WIP
TWY NOTAM	(A) MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE R2 TWY M AND TWY N CLSD DUE WIP TWY P NORTH OF TWY E CLSD TWY Q NORTH OF TWY E CLSD TWY A BTN TWY E AND TWY C CLSD TWY E WEST OF RWY 16/34 CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Works on this stage will only be undertaken when the prevailing wind conditions do not dictate the essential use of Runway 09/27
Drawing	Stage R2

2.1.3. Stage R3

Stage R3	
Description of works	Runway 09/27 involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Runway 09/27 will not be available
Taxiways	Taxiway Papa north of Taxiway Echo not available Taxiway Quebec north of Taxiway Echo not available Taxiway Victor between Taxiway Echo and Taxiway Charlie not available Taxiway Mike not available Taxiway November not available Taxiway Echo west of Runway 16/34 not available
Aircraft type restrictions	Not applicable
RWY NOTAM	(A) MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE R3 RWY 09/27 CLSD DUE WIP
TWY NOTAM	(A) MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE R3 TWY M AND TWY N CLSD DUE WIP TWY P NORTH OF TWY E CLSD TWY Q NORTH OF TWY E CLSD TWY V BTN TWY E AND TWY C CLSD TWY E WEST OF RWY 16/34 CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Works on this stage will only be undertaken when the prevailing wind conditions do not dictate the essential use of Runway 09/27
Drawing	Stage R3

2.1.4. Stage R4

Stage R4	
Description of works	Runway 16/34 involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Runway 16/34 will not be available
Taxiways	Taxiway Alpha north of Runway 09/27 not available Taxiway Bravo not available Taxiway Victor north of Runway 09/27 not available Taxiway Charlie not available Taxiway Foxtrot (RET) west of Taxiway Victor not available Taxiway Golf (RET) west of Taxiway Victor not available Taxiway Juliet west of Taxiway Victor not available Taxiway Kilo west of Taxiway Alpha not available
Aircraft type restrictions	Not applicable
RWY NOTAM	A) MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE R4 RWY 16/34 CLSD DUE WIP.
TWY NOTAM	A) MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE R4 TWY B, TWY C AND TWY K CLSD DUE WIP TWY A NORTH OF RWY 09/27 CLSD TWY V NORTH OF RWY 09/27 CLSD TWY F WEST OF TWY V CLSD TWY G WEST OF TWY V CLSD TWY J WEST OF TWY V CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Engine Ground Runs at Taxiway Bravo and Taxiway Kilo are not available during these works. Works on this stage will only be undertaken when the prevailing wind conditions do not dictate the essential use of Runway 16/34.
Drawing	Stage R4

2.1.5. Stage R5

Stage R5	
Description of works	Runway 16/34 involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Runway 16/34 not available
Taxiways	Taxiway Charlie not available Taxiway Victor north of Runway 09/27 not available Taxiway Foxtrot (RET) west of Taxiway Victor not available Taxiway Golf (RET) west of Taxiway Victor not available Taxiway Juliet west of Taxiway Victor not available. Taxiway Kilo west of Taxiway Alpha not available
Aircraft type restrictions	Not applicable
RWY NOTAM	(A) MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE R5 RWY 16/34 CLSD DUE WIP
TWY NOTAM	(A) MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE R5 TWY C AND TWY K CLSD DUE WIP TWY V NORTH OF RWY 09/27 CLSD TWY F WEST OF TWY V CLSD TWY G WEST OF TWY V CLSD TWY J WEST OF TWY V CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Engine Ground Runs at Taxiway Kilo are not available during these works however the Taxiway Bravo site remains available. Works on this stage will only be undertaken when the prevailing wind conditions do not dictate the essential use of Runway 16/34.
Drawing	Stage R5

2.1.6. Stage T1

Stage T1	
Description of works	Taxiway Alpha between Taxiway Juliet and Taxiway Whiskey involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Alpha between Taxiway Juliet and Taxiway Whiskey not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T1 TWY A BTN TWY J AND TWY W CLSD DUE WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T1

2.1.7. Stage T2

Stage T2	
Description of works	Taxiway Alpha between Taxiway Yankee and Taxiway Juliet involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	

Stage T2	
Runways	Not applicable
Taxiways	Taxiway Alpha between Taxiway Yankee and Taxiway Juliet not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T2 TWY A BTN TWY Y AND TWY J CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: G54, G54A, G56, G57, G57A, G57B, G57C, G57D, G57E, G57F, G57G, G58, G59, G60, G60A, G60B, G60C, G60D, G60E, G60F and G60G. Remote parking positions RPA 20 – RPA 22 also not available.
Drawing	Stage T2

2.1.8. Stage T3

Stage T3	
Description of works	Taxiway Alpha between Taxiway Yankee and Taxiway Golf involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Alpha between Taxiway Yankee and Taxiway Golf not available
Aircraft type restrictions	Not applicable

Stage T3	
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T3 TWY A BTN TWY Y AND TWY G CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: F25, F25A, F25B, F24, F24A and F24B
Drawing	Stage T3

2.1.9. Stage T4

Stage T4	
Description of works	Taxiway Alpha between Taxiway Uniform and Taxiway Golf involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	NOT APPLICABLE
Taxiways	Taxiway Alpha between Taxiway Uniform and Taxiway Golf involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T4 TWY A BTN TWY U AND TWY G CLSD DUE TO WIP

Stage T4	
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T4

2.1.10. Stage T5

Stage T5	
Description of works	Taxiway Alpha between Taxiway Uniform and Taxiway Tango involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Alpha between Taxiway Uniform and Taxiway Tango not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T5 TWY A BTN TWY U AND TWY T CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: D20, D20A, D18, D18A, D18B, D18C, D16, D16A, D16B, D14 and D14A
Drawing	Stage T5

2.1.11. Stage T6

Stage T6	
Description of works	Taxiway Alpha between Taxiway Tango and Taxiway Echo involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Alpha between Taxiway Tango and Taxiway Echo not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T6 TWY A BTN TWY T AND TWY E CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T6

2.1.12. Stage T7

Stage T7	
Description of works	Taxiway Alpha north of Taxiway Echo involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	

Stage T7	
Runways	Not applicable
Taxiways	Taxiway Alpha between Taxiway Echo and Taxiway Charlie not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T7 TWY A BTN TWY E AND TWY C CLSD DUE WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T7

2.1.13. Stage T8

Stage T8	
Description of works	Taxiway Alpha between Bravo Run Up Bay and Runway 09/27 involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Alpha between Taxiway Bravo Run Up Bay and Runway 09/27 Taxiway Charlie between Taxiway Victor and Taxiway Alpha
Aircraft type restrictions	Not applicable

Stage T8	
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T8 TWY A BTN TWY B RUN UP BAY AND RWY 09/27 CLSD DUE WIP TWY C BTN TWY V AND TWY A TWY B CLSD FOR CAT II/III DEP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Due to Taxiway Alpha (north of Runway 09/27 being closed) aircraft requiring a full-length take-off for Runway 16 must enter Runway 16/34 via Taxiway Charlie and backtrack using Taxiway Bravo for turnaround. Similarly, aircraft that pass Taxiway Charlie during the Runway 34 landing roll must back track Runway 16/34 using Taxiway Bravo for turnaround. Taxiway Bravo unavailable for Cat II/III
Drawing	Stage T8

2.1.14. Stage T9

Stage T9	
Description of works	Taxiway Bravo and Taxiway Alpha north of Taxiway Charlie involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Alpha north of Taxiway Charlie not available Taxiway Bravo not available
Aircraft type restrictions	Not applicable

Stage T9																	
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T9 RWY 16/34 OPR LEN REDUCED BY 304 M TWY B CLSD TWY A NORTH OF TWY C CLSD DECLARED DISTANCE AND GRADIENT CHANGES DECLARED DISTANCES <table border="0"> <tr> <td>RWY TORA</td> <td>TODA</td> <td>ASDA</td> <td>LDA</td> </tr> <tr> <td>16</td> <td>3353</td> <td>3473 (2.02%)</td> <td>3413 3657</td> </tr> <tr> <td>34</td> <td>3657</td> <td>3837 (2.02%)</td> <td>3717 3353</td> </tr> <tr> <td>RWY 16 STODA</td> <td>3363 (1.6%)</td> <td>3448 (1.9%)</td> <td></td> </tr> </table>	RWY TORA	TODA	ASDA	LDA	16	3353	3473 (2.02%)	3413 3657	34	3657	3837 (2.02%)	3717 3353	RWY 16 STODA	3363 (1.6%)	3448 (1.9%)	
RWY TORA	TODA	ASDA	LDA														
16	3353	3473 (2.02%)	3413 3657														
34	3657	3837 (2.02%)	3717 3353														
RWY 16 STODA	3363 (1.6%)	3448 (1.9%)															
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Due to Taxiway Bravo being closed runway 16 full length departures are not available. Taxiway Bravo Run Up Bay not available																
Drawing	Stage T9																

2.1.15. Stage T10

Stage T10	
Description of works	Taxiway Alpha between Runway 09/27 and Taxiway Charlie involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Alpha between Runway 09/27 and Taxiway Charlie not available
Aircraft type restrictions	Not applicable

Stage T10	
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T10 TWY A BTN RWY 09/27 AND TWY C CLSD DUE WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T10

2.1.16. Stage T11

Stage T11	
Description of works	Taxiway Sierra between Taxiway Juliet and Taxiway Whiskey involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Sierra between Taxiway Juliet and Taxiway Whiskey not available
Aircraft type restrictions	Not applicable
NOTAM	A) MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T11 TWY S BTN TWY J AND TWY W CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable

Stage T11	
Drawing	Stage T11

2.1.17. Stage T12

Stage T12	
Description of works	Taxiway Sierra between Taxiway Juliet and Taxiway Yankee involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Sierra between Taxiway Juliet and Taxiway Yankee not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T12 TWY S BTN TWY J AND TWY Y CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: G50, G51, and G52
Drawing	Stage T12

2.1.18. Stage T13

Stage T13	
Description of works	Taxiway Sierra between Taxiway Uniform and Taxiway Golf involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.

Stage T13	
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Sierra between Taxiway Uniform and Taxiway Golf not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T13 TWY S BTN U AND TWY G CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T13

2.1.19. Stage T14

Stage T14	
Description of works	Taxiway Sierra between Taxiway Echo and Taxiway Tango involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Sierra between Taxiway Echo and Taxiway Tango not available

Stage T14	
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T14 TWY S BTN TWY E AND TWY T CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T14

2.1.20. Stage T15

Stage T15	
Description of works	Taxiway Victor south of Taxiway Yankee involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Victor between Taxiway Yankee and Taxiway Juliet not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T15 TWY V BTW TWY Y AND TWY J CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable

Stage T15	
Drawing	Stage T15

2.1.21. Stage T16

Stage T16	
Description of works	Taxiway Victor between Taxiway Yankee and Taxiway Golf involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Victor between Taxiway Yankee and Taxiway Golf
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T16 TWY V BTN TWY Y AND TWY G CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T16

2.1.22. Stage T17

Stage T17	
Description of works	Taxiway Victor between Taxiway Foxtrot and Taxiway Uniform involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023

Stage T17	
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Victor between Taxiway Foxtrot and Taxiway Uniform not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T17 TWY V BTN TWY F AND TWY U CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T17

2.1.23. Stage T18

Stage T18	
Description of works	Taxiway Victor between Taxiway Foxtrot and Taxiway Golf and Taxiway Uniform between Taxiway Alpha and Taxiway Victor involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Victor between Taxiway Foxtrot and Taxiway Golf, Taxiway Uniform between Taxiway Alpha, and Taxiway Victor not available
Aircraft type restrictions	Not applicable

Stage T18	
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T18 TWY V BTN TWY F AND TWY G CLSD DUE TO WIP TWY U BTN TWY A AND TWY V CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T18

2.1.24. Stage T19

Stage T19	
Description of works	Taxiway Kilo between Taxiway Alpha and Taxiway Kilo stop bar (westbound) involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Due to Taxiway Kilo (east of Runway 16/34) being closed full length departure on Runway 34 not available.
Taxiways	Taxiway Kilo between Taxiway Alpha and the Taxiway Kilo stop bar (westbound) not available
Aircraft type restrictions	Not applicable

Stage T19																	
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T19 RWY 16/34 OPR LEN REDUCED BY 754M AT SOUTHERN END DUE WIP SOUTHERN MOST ACCESS TO RWY 16/34 VIA TWY J LANDING RWY 34 FULL LEN AVBL DUE TWY K CLSD DECLARED DISTANCE AND GRADIENT CHANGES DECLARED DISTANCES <table border="0"> <tr> <td>RWY TORA</td> <td>TODA</td> <td>ASDA</td> <td>LDA</td> </tr> <tr> <td>16 3657</td> <td>3777 (2.02%)</td> <td>3717</td> <td>2903</td> </tr> <tr> <td>34 2903</td> <td>3083 (2.02%)</td> <td>2963</td> <td>3657</td> </tr> <tr> <td>RWY 34 STODA</td> <td>2652 (1.6%)</td> <td>2996</td> <td>(1.9)</td> </tr> </table>	RWY TORA	TODA	ASDA	LDA	16 3657	3777 (2.02%)	3717	2903	34 2903	3083 (2.02%)	2963	3657	RWY 34 STODA	2652 (1.6%)	2996	(1.9)
RWY TORA	TODA	ASDA	LDA														
16 3657	3777 (2.02%)	3717	2903														
34 2903	3083 (2.02%)	2963	3657														
RWY 34 STODA	2652 (1.6%)	2996	(1.9)														
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Due to Taxiway Kilo (east of Runway 16/34) being closed, full length departure on Runway 34 not available. Similarly, aircraft landing on Runway 16 MUST vacate onto/or prior to Taxiway Juliet Kilo Run-Up Bay Not Available.																
Drawing	Stage T19																

2.1.25. Stage T20

Stage T20	
Description of works	Taxiway Kilo between Taxiway Alpha and Taxiway Kilo Run-up Bay involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Kilo between Taxiway Alpha and Taxiway Kilo Run-up Bay not available
Aircraft type restrictions	Not applicable

Stage T20	
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T20 TWY K BTN TWY A AND K RUN UP BAY CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Due to Taxiway Kilo between the Kilo Run-up Bay and Taxiway Alpha being closed, aircraft requiring a full-length take-off for Runway 34 must enter Runway 16/34 via Taxiway Juliet and backtrack using Taxiway Kilo Run-up Bay for turnaround. Similarly, aircraft that pass Taxiway Juliet during the Runway 16 landing roll must back track Runway 16/34 using Taxiway Kilo Run-up Bay for turnaround. Clearance available in the Taxiway Kilo Holding (Run Up) Bay
Drawing	Stage T20

2.1.26. Stage T21

Stage T21	
Description of works	Taxiway Whiskey between Taxiway Sierra and Taxiway Alpha involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Whiskey between Taxiway Sierra and Taxiway Alpha not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T21 TWY W BTN TWY S AND TWY A CLSD DUE TO WIP

Stage T21	
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T21

2.1.27. Stage T22

Stage T22	
Description of works	Taxiway Whiskey east of Taxiway Sierra involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Whiskey east of Taxiway Sierra not available
Taxilanes	Whiskey 1, Whiskey 2, Whiskey 3 and Whiskey 4 not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T22 TWY W EAST OF TWY S CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T22

2.1.28. Stage T23

Stage T23	
Description of works	Taxiway Whiskey east of Whiskey 1 involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Whiskey east of Whiskey 1 not available
Taxilanes	Whiskey 2, Whiskey 3, and Whiskey 4 not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T23 TWY W EAST OF W1 CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T23

2.1.29. Stage T24

Stage T24	
Description of works	Taxiway Whiskey east of Whiskey 2 involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	

Stage T24	
Runways	Not applicable
Taxiways	Taxiway Whiskey east of Whiskey 2 not available
Taxilane	Whiskey 3 and Whiskey 4 not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T24 TWY W EAST OF W2 CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T24

2.1.30. Stage T25

Stage T25	
Description of works	Taxiway Whiskey east of Whiskey 3 involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Whiskey east of Whiskey 3 not available
Taxilane	Whiskey 4 not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T25 TWY W EAST OF W3 CLSD DUE TO WIP

Stage T25	
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T25

2.1.31. Stage T26

Stage T26	
Description of works	Whiskey 1 Taxilane involves Movement Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Not applicable
Taxilane	Taxilane Whiskey 1 not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T26 TAXILANE W1 CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T26

2.1.32. Stage T27

Stage T27	
Description of works	Whiskey 2 Taxilane involves Movement Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Not applicable
Taxilane	Taxilane Whiskey 2 not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T27 TAXILANE W2 CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T27

2.1.33. Stage T28

Stage T28	
Description of works	Whiskey 3 Taxilane involves Movement Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	

Stage T28	
Runways	Not applicable
Taxiways	Not applicable
Taxilane	Taxilane Whiskey 3 not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T28 TAXILANE W3 CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T28

2.1.34. Stage T29

Stage T29	
Description of works	Taxiway Juliet west of Taxiway Victor involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Juliet west of Taxiway Victor not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T29 TWY J WEST OF TWY V CLSD DUE TO WIP

Stage T29	
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T29

2.1.35. Stage T30

Stage T30	
Description of works	Taxiway Juliet between Taxiway Alpha and Taxiway Victor involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Juliet between Taxiway Alpha and Taxiway Victor not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T30 TWY J BTN TWY A AND TWY V CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T30

2.1.36. Stage T31

Stage T31	
Description of works	Taxiway Juliet between Taxiway Alpha and Taxiway Sierra involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Juliet between Taxiway Alpha and Taxiway Sierra not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T31 TWY J BTN TWY A AND TWY S CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: G54A
Drawing	Stage T31

2.1.37. Stage T32

Stage T32	
Description of works	Taxiway Yankee between Taxiway Alpha and Taxiway Victor involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025

Stage T32	
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Yankee between Taxiway Alpha and Taxiway Victor
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T32 TWY Y BTN TWY A AND TWY V CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T32

2.1.38. Stage T33

Stage T33	
Description of works	Taxiway Yankee between Taxiway Alpha and Taxiway Sierra involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Yankee between Taxiway Alpha and Taxiway Sierra not available
Aircraft type restrictions	Not applicable

Stage T33	
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T33 TWY Y BTN TWY A AND TWY S CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: F22B, F24 and F24B
Drawing	Stage T33

2.1.39. Stage T34

Stage T34	
Description of works	Taxiway Golf between Taxiway Alpha and Taxiway Victor involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Golf between Taxiway Alpha and Taxiway Victor not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T34 TWY G BTN TWY A AND TWY V CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T34

2.1.40. Stage T35

Stage T35	
Description of works	Taxiway Golf between Taxiway Sierra and Taxiway Alpha involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not Applicable
Taxiways	Taxiway Golf between Taxiway Sierra and Taxiway Alpha not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T35 TWY G BTN TWY S AND TWY A CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: F25 and F25A not available
Drawing	Stage T35

2.1.41. Stage T36

Stage T36	
Description of works	Taxiway Uniform between Taxiway Alpha and Taxiway Victor involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	

Stage T36	
Runways	Not applicable
Taxiways	Taxiway Uniform between Taxiway Alpha and Taxiway Victor not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T36 TWY U BTN TWY A AND TWY V CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T36

2.1.42. Stage T37

Stage T37	
Description of works	Taxiway Uniform between Taxiway Sierra and Taxiway Alpha involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Uniform between Taxiway Sierra and Taxiway Alpha not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T37 TWY U BTN TWY S AND TWY A CLSD DUE TO WIP

Stage T37	
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: D14 and D14A
Drawing	Stage T37

2.1.43. Stage T38

Stage T38	
Description of works	Taxiway Foxtrot between Taxiway Tango and Taxiway Echo and Taxiway Victor between Taxiway Tango and Taxiway Echo involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Foxtrot between Taxiway Tango and Taxiway Echo and Taxiway Victor between Taxiway Tango and Taxiway Echo not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T38 TWY F BTN TWY T AND TWY E CLSD DUE TO WIP TWY V BTN TWY T AND TWY E CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T38

2.1.44. Stage T39

Stage T39	
Description of works	Taxiway Tango between Taxiway Quebec and Taxiway Romeo involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Tango between Taxiway Quebec and Taxiway Romeo not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T39 TWY T BTN TWY Q AND TWY R CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: B29
Drawing	Stage T39

2.1.45. Stage T40

Stage T40	
Description of works	Taxiway Tango between Taxiway Quebec and Taxiway Papa involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	

Stage T40	
Runways	Not applicable
Taxiways	Taxiway Tango between Taxiway Quebec and Taxiway Papa not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T40 TWY T BTN TWY Q AND TWY P CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: C11, C11A and C12
Drawing	Stage T40

2.1.46. Stage T41

Stage T41	
Description of works	Taxiway Tango between Taxiway Sierra and Taxiway Papa involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Tango between Taxiway Sierra and Taxiway Papa not available
Aircraft type restrictions	Not applicable

Stage T41	
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T41 TWY T BTN TWY S AND TWY P CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: D7, D9, D9A, D9B, D10, D11, D11A, D11B, D13, 13A, D13B, D15, D15A, D15B, D17 and D19
Drawing	Stage T41

2.1.47. Stage T42

Stage T42	
Description of works	Taxiway Tango between Taxiway Sierra and Taxiway Alpha involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Tango between Taxiway Sierra and Taxiway Alpha not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T42 TWY T BTN TWY S AND TWY A CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T42

2.1.48. Stage T43

Stage T43	
Description of works	Taxiway Tango between Taxiway Alpha and Taxiway Foxtrot involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Tango between Taxiway Alpha and Taxiway Foxtrot not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T43 TWY T BTN TWY A AND TWY F CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T43

2.1.49. Stage T44

Stage T44	
Description of works	Taxiway Papa between Runway 09/27 and Taxiway Echo involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025

Stage T44	
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Papa between Runway 09/27 and Taxiway Echo not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T44 TWY P BTN RWY 09/27 AND TWY E CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T44

2.1.50. Stage T45

Stage T45	
Description of works	Taxiway Papa between Taxiway Tango and Taxiway Echo involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Papa between Taxiway Tango and Taxiway Echo not available
Aircraft type restrictions	Not applicable

Stage T45	
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T45 TWY P BTN TWY T AND TWY E CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T45

2.1.51. Stage T46

Stage T46	
Description of works	Taxiway Quebec north of Taxiway Echo involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Quebec north of Taxiway Echo not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T46 TWY Q NORTH OF TWY E CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T46

2.1.52. Stage T47

Stage T47	
Description of works	Taxiway November involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway November not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T76 TWY N CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T47

2.1.53. Stage T48

Stage T48	
Description of works	Taxiway Mike and Taxiway Echo west of Taxiway November involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	

Stage T48																
Runways	Not applicable															
Taxiways	Taxiway Mike between Taxiway Mike Stop bar (northbound) and Taxiway Echo not available Taxiway Echo west of Taxiway November not available															
Aircraft type restrictions	Not applicable															
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4STAGE T48 RWY 09/27 OPR LEN REDUCED BY 638 M TWY M NOT AVBL TWY E WEST OF TWY N NOT AVBL DECLARED DISTANCE AND GRADIENT CHANGES DECLARED DISTANCES <table border="1"> <thead> <tr> <th>RWY</th> <th>TORA</th> <th>TODA</th> <th>ASDA</th> <th>LDA</th> </tr> </thead> <tbody> <tr> <td>09</td> <td>1648</td> <td>1798 (2.08%)</td> <td>1708</td> <td>2286</td> </tr> <tr> <td>27</td> <td>2286</td> <td>2436 (1.52%)</td> <td>2346</td> <td>1648</td> </tr> </tbody> </table> RWY 09 STODA 1664 (1.6%) 1755 (1.9%)	RWY	TORA	TODA	ASDA	LDA	09	1648	1798 (2.08%)	1708	2286	27	2286	2436 (1.52%)	2346	1648
RWY	TORA	TODA	ASDA	LDA												
09	1648	1798 (2.08%)	1708	2286												
27	2286	2436 (1.52%)	2346	1648												
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Due to Taxiway Mike being closed, full length departure on Runway 09 is not available. Aircraft landing Runway27 MUST vacate the Runway via Taxiway November															
Drawing	Stage T48															

2.1.54. Stage T49

Stage T49	
Description of works	Taxiway Echo between Taxiway Echo Stop bar (eastbound) and Taxiway Mike, Taxiway Mike between the Taxiway Mike stop bar (northbound) and Taxiway Echo and Taxiway November between the Taxiway November stop bar (northbound) and Taxiway Echo involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025

Stage T49	
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Echo from Taxiway Echo Stop bar (westbound) to Taxiway Mike, Taxiway November between RWY 09/27 and Taxiway Echo, Taxiway Mike between Runway 09/27, and Taxiway Echo not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T49 RWY 09 NOT AVBL FOR DEP RWY 27 NOT AVBL FOR ARV DUE TWY E WEST OF RWY 16/34 CLSD TWY M AND TWY N CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Due to Taxiway Echo (east of Runway 16) Runway 09 departures and Runway 27 arrivals unavailable
Drawing	Stage T49

2.1.55. Stage T50

Stage T50	
Description of works	Taxiway Echo between Runway 16/34 and Taxiway Foxtrot, Taxiway Victor between Taxiway Foxtrot and Taxiway Charlie involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable

Stage T50	
Taxiways	Taxiway Echo between Runway 16/34 and Taxiway Foxtrot and Taxiway Victor between Taxiway Foxtrot and Taxiway Charlie not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T50 TWY E BTN RWY 16/34 AND TWY F CLSD DUE TO WIP TWY V BTN TWY F AND TWY C CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Due to Taxiway Echo (east of RUNWAY 16/34) being closed, aircraft arrivals on Runway 27 must enter Runway 16 via Taxiway Echo southbound to vacate the Runway at Taxiway Golf
Drawing	Stage T50

2.1.56. Stage T51

Stage T51	
Description of works	Taxiway Echo between Taxiway Sierra and Taxiway Alpha involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Echo between Taxiway Sierra and Taxiway Alpha not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T51 TWY E BTN TWY S AND TWY A CLSD DUE TO WIP

Stage T51	
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T51

2.1.57. Stage T52

Stage T52	
Description of works	Taxiway Echo between Taxiway Sierra and Taxiway Papa involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Echo between Taxiway Sierra and Taxiway Papa not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T52 TWY E BTN TWY S AND TWY P CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T52

2.1.58. Stage T53

Stage T53	
Description of works	Taxiway Echo between Taxiway Papa and Taxiway Quebec involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Echo between Taxiway Papa and Taxiway Quebec not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T53 TWY E BTN TWY P AND TWY Q CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T53

2.1.59. Stage T54

Stage T54	
Description of works	Taxiway Echo between Taxiway Quebec and Taxiway Romeo involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025

Stage T54	
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Echo between Taxiway Quebec and Taxiway Romeo not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T54 TWY E BTN TWY Q AND TWY R CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T54

2.1.60. Stage T55

Stage T55	
Description of works	Intersection of Taxiway Alpha, Echo and Foxtrot involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Intersection of Taxiway Alpha, Echo and Foxtrot resulting in Taxiway Echo between Taxiway Victor and Taxiway Sierra Taxiway Foxtrot between Taxiway Tango and Taxiway Echo Taxiway Alpha between Taxiway Tango and Taxiway Charlie not available

Stage T55	
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T55 TWY E BTN TWY V AND TWY S CLSD DUE TO WIP TWY F BTN TWY T AND TWY E CLSD TWY A BTN TWY T AND TWY C CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T55

2.1.61. Stage T56

Stage T56	
Description of works	Intersection of Taxiway Alpha and Taxiway Tango involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Alpha between Taxiway Echo and Taxiway Tango, Taxiway Tango between Taxiway Sierra, and Taxiway Foxtrot not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T56 TWY A BTN TWY E AND TWY T CLSD DUE TO WIP TWY T BTN TWY S AND TWY F CLSD

Stage T56	
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: D20 and D20A
Drawing	Stage T56

2.1.62. Stage T57

Stage T57	
Description of works	Intersection of Taxiway Alpha and Taxiway Uniform involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Alpha between Taxiway Uniform and Taxiway Golf, Taxiway Uniform between Taxiway Sierra, and Taxiway Victor not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T57 TWY A BTN TWY U AND TWY G CLSD DUE TO WIP TWY U BTN TWY S AND TWY V CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: D14 and D14A (D4, D6 and D8 restricted to max D Aircraft)
Drawing	Stage T57

2.1.63. Stage T58

Stage T58	
Description of works	Intersection of Taxiway Golf and Taxiway Alpha involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Alpha between Taxiway Uniform and Taxiway Golf and Taxiway Golf between Taxiway Sierra, and Taxiway Victor not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T58 TWY A BTN TWY U AND TWY G CLSD DUE TO WIP TWY G BTN TWY S AND TWY V CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: F25, F25A and F25B
Drawing	Stage T58

2.1.64. Stage T59

Stage T59	
Description of works	Intersection of Taxiway Alpha and Taxiway Yankee involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025

Stage T59	
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Yankee between Taxiway Sierra and Taxiway Victor not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T59 TWY Y BTN TWY S AND TWY V CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: F24, F24B, G57, G57A, G57D and G57E
Drawing	Stage T59

2.1.65. Stage T60

Stage T60	
Description of works	Intersection of Taxiway Alpha and Taxiway Juliet involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Alpha between Taxiway Juliet and Taxiway Whiskey, Taxiway Juliet between Taxiway Sierra, and Taxiway Victor not available
Aircraft type restrictions	Not applicable

Stage T60	
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T60 TWY A BTN TWY J AND TWY W CLSD DUE TO WIP TWY J BTN TWY S AND TWY V CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Due to Taxiway Juliet between Taxiway Sierra and Taxiway Victor and Taxiway Alpha between Taxiway Juliet and Taxiway Whiskey being closed, all Code F aircraft requiring a full-length take-off for Runway 34 must enter Runway 16/34 via Taxiway Juliet and backtrack using Taxiway Kilo for turnaround. Similarly, all aircraft that pass Taxiway Juliet during the Runway 16 landing roll must back track Runway 16/34 using Taxiway Kilo Run-up Bay for turnaround. Kilo Run-up Bay available for an A380 turnaround. Follow me service available upon request. Bays impacted: G54 and G54A
Drawing	Stage T60

2.1.66. Stage T61

Stage T61	
Description of works	Intersections of Taxiway Alpha and Taxiway Whiskey involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Alpha between Taxiway Juliet and Taxiway Whiskey, Taxiway Whiskey between Taxiway Sierra, and Taxiway Kilo not available
Aircraft type restrictions	Not applicable

Stage T61	
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T61 TWY A BTN TWY J AND TWY W CLSD DUE TO WIP TWY W BTN TWY S AND TWY K CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Due to Taxiway Alpha between Taxiway Juliet and Taxiway Whiskey and Taxiway Whiskey between Taxiway Sierra and Taxiway Kilo being closed, all aircraft requiring a full-length take-off for Runway 34 must enter Runway 16/34 via Taxiway Juliet and backtrack using Taxiway Kilo for turnaround. Similarly, aircraft that pass Taxiway Juliet during the Runway 16 landing roll must back track Runway 16/34 using Taxiway Kilo Run-up Bay for turnaround. Kilo Run-up Bay clear for an A380 Turnaround
Drawing	Stage T61

2.1.67. Stage T62

Stage T62	
Description of works	Intersection of Taxiway Whiskey and Taxiway Sierra involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Sierra between Taxiway Juliet and Taxiway Whiskey, Taxiway Whiskey between Taxiway Alpha, and Whiskey 4 Taxilane not available
Taxilanes	Whiskey 1,2,3 and 4 not available to aircraft operation
Aircraft type restrictions	Not applicable

Stage T62	
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T62 TWY S BTN TWY J AND TWY W CLSD DUE TO WIP TWY W BTN TWY A AND W4 CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T62

2.1.68. Stage T63

Stage T63	
Description of works	Intersection of Taxiway Sierra and Taxiway Juliet involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Sierra between Taxiway Juliet and Taxiway Whiskey, Taxiway Juliet between Taxiway Alpha, and Taxiway Sierra not available
Taxilanes	Juliet Taxilane not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T63 TWY S BTN intermediate holding points north of TWY J AND TWY W CLSD DUE TO WIP TWY J BTN TWY A AND TWY S CLSD

Stage T63	
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: G54A, G50, G42, G44, G46, G46A G48, H1, H1A, H1B, H2, H2A, H3, H3A and H3B.
Drawing	Stage T63

2.1.69. Stage T64

Stage T64	
Description of works	Intersection of Taxiway Sierra and Taxiway Yankee involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Yankee between Taxiway Alpha and Taxilane Yankee, not available
Taxilanes	Yankee Taxilane not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) MOWP YMML 2023/4 STAGE T64 TWY Y BTN TWY A AND TAXILANE Y CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: F12, F14, F16, F18, F20, F22, F22A, F22B, G41, G41A G43, G45, G45A, G47 and G49
Drawing	Stage T64

2.1.70. Stage T65

Stage T65	
Description of works	Intersection of Taxiway Sierra and Taxiway Golf involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Sierra between Taxiway Uniform and Taxiway Golf, and Taxiway Golf between Taxiway Alpha, and Taxiway Sierra not available
Taxilanes	Golf Taxilane not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T65 TWY S BTN TWY U AND TWY G CLSD DUE TO WIP TWY G BTN TWY A AND TAXILANE G CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: E2, E4, E6, E8, E10, F11, F13, F15, F17, F19 F21, F21A, F23, F25 and F25A
Drawing	Stage T65

2.1.71. Stage T66

Stage T66	
Description of works	Intersection of Taxiway Sierra and Taxiway Uniform involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023

Stage T66	
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Sierra between Taxiway Uniform and Taxiway Golf, Taxiway Uniform between Taxiway Alpha, and Taxiway Sierra not available
Taxilanes	Uniform Taxilane not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T66 TWY S BTN TWY U AND TWY G CLSD DUE TO WIP TWY U BTN TWY A AND TAXILANE U CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: D2, D4, D4A D6, D8, D12, D12A, D14, D14A, E1, E3, E5, E7 and E9
Drawing	Stage T66

2.1.72. Stage T67

Stage T67	
Description of works	Intersection of Taxiway Tango and Taxiway Sierra involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable

Stage T67	
Taxiways	Taxiway Sierra between Taxiway Echo and Taxiway Tango, and Taxiway Tango between Taxiway Alpha, and Taxiway Sierra not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T67 TWY S BTN TWY E AND TWY T CLSD DUE TO WIP TWY T BTN TWY A AND INTERMEDIATE HOLDING POINT EAST OF TWY S CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: D10, D11, D11B, D13 and D13A not available
Drawing	Stage T67

2.1.73. Stage T68

Stage T68	
Description of works	Intersection of Taxiway Victor and Taxiway Juliet involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Victor between Taxiway Yankee and Taxiway Juliet, Taxiway Juliet between Runway 16/34, and Taxiway Alpha not available
Aircraft type restrictions	Not applicable

Stage T68	
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T68 TWY V BTN TWY Y AND TWY J CLSD DUE TO WIP TWY J BTN RWY 16/34 AND TWY A CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T68

2.1.74. Stage T69

Stage T69	
Description of works	Intersection of Taxiway Victor and Taxiway Yankee involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Victor between Taxiway Golf and Taxiway Juliet and Taxiway Yankee between Taxiway Alpha, and Taxiway Victor not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T69 TWY V BTN TWY G AND TWY J CLSD DUE TO WIP TWY Y BTN TWY A AND TWY V CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable

Stage T69	
Drawing	Stage T69

2.1.75. Stage T70

Stage T70	
Description of works	Intersection of Taxiway Victor and Taxiway Golf involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Victor between Taxiway Uniform and Taxiway Yankee, Taxiway Golf between Runway 16/34, and Taxiway Alpha not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T70 TWY V BTN TWY U AND TWY Y CLSD DUE TO WIP TWY G BTN RWY 16/34 AND TWY A CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T70

2.1.76. Stage T71

Stage T71	
Description of works	Intersection of Taxiway Victor, Taxiway Foxtrot and Taxiway Tango involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Victor between Taxiway Uniform and Taxiway Echo, Taxiway Foxtrot between Runway 16/34 and Taxiway Echo and Taxiway Tango between Taxiway Foxtrot and Taxiway Alpha not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T71 TWY V BTN TWY U AND TWY E CLSD DUE TO WIP TWY F BTN RWY 16/34 AND TWY E CLSD TWY T BTN TWY A AND TWY F CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T71

2.1.77. Stage T72

Stage T72	
Description of works	Intersection of Taxiway Quebec and Taxiway Echo involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023

Stage T72	
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Quebec between Runway 09/27 and Taxiway Tango, Taxiway Echo between Taxiway Papa and Taxiway Romeo not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T72 TWY Q BTN RWY 09/27 AND TWY T CLSD DUE TO WIP TWY E BTN TWY P AND TWY R CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Taxiway Tango east of Taxiway Papa not available to aircraft greater than Code E
Drawing	Stage T72

2.1.78. Stage T73

Stage T73	
Description of works	Intersection of Taxiway Romeo and Taxiway Tango involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Echo between Taxiway Quebec and Taxilane Romeo, Taxiway Tango between Taxiway Quebec and Taxiway Romeo not available

Stage T73	
Taxilane	Romeo Taxilane not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T73 TWY E BTN TWY Q AND TAXILANE R CLSD DUE TO WIP TWY T BTN TWY R AND TWY Q CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: B21, B23, B25, B25A, B27, and B29
Drawing	Stage T73

2.1.79. Stage T74

Stage T74	
Description of works	Intersection of Taxiway Echo and Taxiway Papa involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Runway 27 departures and Runway 09 arrivals are not available for Code F aircraft.
Taxiways	Taxiway Echo between Taxiway Sierra and Taxiway Quebec, Taxiway Papa between Taxiway Tango, and Runway 09/27 not available
Aircraft type restrictions	Due to Taxiway Echo between Taxiway Sierra and Taxiway Quebec and Taxiway Papa between Runway 09/27 and Taxiway Tango being closed, Runway 27 departures and Runway 09 arrivals are not available for Code F aircraft.

Stage T74	
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T74 TWY E BTN TWY S AND TWY Q CLSD DUE TO WIP TWY P BTN TWY T AND RWY 09/27 CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T74

2.1.80. Stage T75

Stage T75	
Description of works	Intersection of Taxiway Echo and Taxiway Sierra involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Echo between Taxiway Alpha and Taxiway Papa, Taxiway Sierra between Taxiway Echo, and Taxiway Tango not available
Aircraft type restrictions	Due to Taxiway Echo between Taxiway Alpha and Taxiway Papa and Taxiway Sierra between Taxiway Echo and Taxiway Tango being closed, Runway 27 departures and Runway 09 arrivals are not available for Code F aircraft
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T75 TWY E BTN TWY A AND TWY P CLSD DUE TO WIP TWY S BTN TWY E AND TWY T CLSD

Stage T75	
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T75

2.1.81. Stage T76

Stage T76	
Description of works	Intersection of Taxiway Tango and Taxiway Quebec involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Tango between Taxiway Romeo and Taxiway Papa, Taxiway Quebec between Taxiway Echo, and Taxiway Tango not available
Taxilane	Quebec Taxilane not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T76 TWY T BTN TWY R AND TWY P CLSD DUE TO WIP TWY Q BTN TWY E AND TWY T CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: B22, B24, B26, B26A, B30, C1, C3, C5, C7, C9, C11, C11A and C12
Drawing	Stage T76

2.1.82. Stage T77

Stage T77	
Description of works	Intersection of Taxiway Tango and Taxiway Papa involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Tango between Taxiway Papa and Taxiway Quebec, Taxiway Papa between Taxiway Echo, and Taxiway Tango not available
Taxilane	Papa Taxilane not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T77 TWY T BTN TWY P AND TWY Q CLSD DUE TO WIP TWY P BTN TWY E AND TWY T CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: D3, D5, D7, D9, C4, C6, C8, C10, C12, C11 and C11A
Drawing	Stage T77

2.1.83. Stage T78

Stage T78	
Description of works	Taxilane Romeo involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025

Stage T78	
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Not applicable
Taxilane	Taxilane Romeo not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T78 TAXILANE R CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: B21, B23, B25, B25A and B27
Drawing	Stage T78

2.1.84. Stage T79

Stage T79	
Description of works	Quebec Taxilane involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Not applicable
Taxilane	Taxilane Quebec not available
Aircraft type restrictions	Not applicable

Stage T79	
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T79 TAXILANE Q CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: B22, B24, B26, B26A, B28, B30, C1, C3, C5, C7 and C9
Drawing	Stage T79

2.1.85. Stage T80

Stage T80	
Description of works	Papa Taxilane involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Not applicable
Taxilane	Taxilane Papa not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T80 TAXILANE P CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: C4, C6, C8, C10, D3, D5 and D7
Drawing	Stage T80

2.1.86. Stage T81

Stage T81	
Description of works	Uniform Taxilane involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Not applicable
Taxilane	Uniform Taxilane not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T81 TAXILANE U CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: D2, D4, D4A, D6, D8, D12, D12A, E1, E3, E5, E7 and E9
Drawing	Stage T81

2.1.87. Stage T82

Stage T82	
Description of works	Golf Taxilane involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	

Stage T82	
Runways	Not applicable
Taxiways	Not applicable
Taxilane	Taxilane Golf not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T82 TAXILANE G CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: E2, E4, E6, E8, E8A, E10, F11, F13, F15, F17, F19, F21, F21A and F23
Drawing	Stage T82

2.1.88. Stage T83

Stage T83	
Description of works	Yankee Taxilane involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Not applicable
Taxilane	Taxilane Yankee not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T83 TAXILANE Y CLSD DUE TO WIP

Stage T83	
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: F12, F14, F16, F18, F20, F22, F22A, F22B, G41, G41A, G43, G45, G45A, G47 and G49
Drawing	Stage T83

2.1.89. Stage T84

Stage T84	
Description of works	Juliet Taxilane involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Not applicable
Taxilane	Taxilane Juliet not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T84 TAXILANE J CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Bays impacted: G42, G44, G46, G46A, G48, G50, H1, H1A, H1B, H2, H2A, H3, H3A and H3B
Drawing	Stage T84

2.1.90. Stage T85

Stage T85	
Description of works	Taxiway Golf between Runway 16/34 and Taxiway Victor involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Golf between Runway 16/34 and Taxiway Victor not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T85 TWY G BTN RWY 16/34 AND TWY V CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T85

2.1.91. Stage T86

Stage T86	
Description of works	Taxiway Foxtrot between Runway 16/34 and Taxiway Victor involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025

Stage T86	
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Foxtrot between Runway 16/34 and Taxiway Victor not available
Aircraft type restrictions	Not applicable
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T86 TWY F BTN RWY 16/34 AND TWY V CLSD DUE TO WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T86

2.1.92. Stage T87

Stage T87	
Description of works	Taxiway Charlie and Taxiway Victor between Runway 09/27 and Taxiway Charlie involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Charlie and Taxiway Victor between Runway 09/27 and Taxiway Charlie not available
Aircraft type restrictions	Not applicable

Stage T87	
NOTAM	(A)MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T87 TWY C CLSD DUE WIP TWY V BTN RWY 09/27 AND TWY C CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T87

2.1.93. Stage T88

Stage T88	
Description of works	Intersection of Taxiway Foxtrot and Taxiway Echo involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Echo between Taxiway Victor and Taxiway Alpha, Taxiway Foxtrot between Taxiway Tango, and Taxiway Echo not available
Aircraft type restrictions	Not applicable
NOTAM	A) MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T88 TWY E BTN TWY V AND TWY A CLSD DUE TO WIP TWY F BTN TWY T AND TWY E CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable

Stage T88	
Drawing	Stage T88

2.1.94. Stage T89

Stage T89	
Description of works	Taxiway Victor between Taxiway Echo and Taxiway Charlie involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Victor between Taxiway Echo and Runway 09/27 and Taxiway Victor between Runway 09/27 and Taxiway Charlie
Aircraft type restrictions	Not applicable
NOTAM	A) MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T89 TWY V BTN TWY E AND RWY 09/27 CLSD DUE TO WIP TWY V BTN RWY 09/27 AND TWY C CLSD
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T89

2.1.95. Stage T90

Stage T90	
Description of works	Taxiway Victor between Runway 09/27 and Taxiway Charlie involves Manoeuvring Area Maintenance, Visual Aid Maintenance and Electrical Works.
Scheduled start date	18/08/2023
Scheduled end date	30/08/2025
Restrictions: Manoeuvring Area	
Runways	Not applicable
Taxiways	Taxiway Victor between Runway 09/27 and Taxiway Charlie will not be available
Aircraft type restrictions	Not applicable
NOTAM	A) MELBOURNE (B) (START DATE) (C) (FINISH DATE) (E)MOWP YMML 2023/4 STAGE T89 TWY V BTN RWY 09/27 AND TWY C CLSD DUE WIP
Remarks (details of any special restrictions and the requirements for the issue of NOTAMs)	Not applicable
Drawing	Stage T90

2.2. Weather conditions

Works will not be permitted on the manoeuvring area or in areas where the Senior Airside Safety Officer (Car2) believes is unsafe in:

1. Low visibility conditions; or
2. Weather conditions that Car2 in conjunction with ATC believe are unsafe or may affect airport operations.

Low Visibility Operations must be in force when:

- a) The cloud ceiling is at or below the CAT I minima for the runway being used: or
- b) Runway Visual Range (RVR) is at or below 550m (visibility at or below 800m when RVR not available).

When implementing LVP, Melbourne Tower will notify.

- a) The Senior Airside Safety Officer
- b) Service Desk Airway: and
- c) Operations Manager (OM) Systems Supervisor (SS)

ATC will then declare “Low Visibility Procedures in Force” on the Automated Terminal Information Service (ATIS).

Works may be postponed, limited, or cancelled subject to the prevailing weather conditions.

Once a NOTAM has been issued and there are unfavourable weather conditions, and the NOTAM is required to be cancelled or amended a new NOTAM may be issued at short notice to activate another stage of the MOWP to minimise impact to aircraft operations.

2.3. Airport emergencies

Under certain emergency situations, access to the airside of the airport including the work site will not be allowed.

Because of the unpredictable nature of emergency situations, it is not possible to give advance warning of these occurrences. Local Standby situations do not require the works party to vacate the airside.

2.4. NOTAM or other change to AIP

Melbourne Airport will issue a NOTAM or other required change to the AIP (i.e. AIP-SUP or AIC) prior to the commencement of the works. Refer to the [Restrictions by works stages](#) section for the draft wording.

Note: For works affecting the Instrument Landing System (ILS), Airservices are responsible for issuing a NOTAM to activate/deactivate the ILS.

2.5. Restoration of normal safety standards

All works undertaken in the stages of this MOWP specified in subsection [2.1](#) will require the partial closure of the Manoeuvring area. These closed areas will not be available for aircraft operations until works have been completed, inspected and declared serviceable as specified in subsection [5.14](#).

2.6. Restrictions on the organisation carrying out aerodrome works

Organisations carrying out aerodrome works must do so in accordance with this MOWP including sections [Personnel and Equipment](#) and [Aerodromes Markers, Markings and Lights](#).

3. Personnel and Equipment

3.1. Requirement to vacate the movement area

Personnel and equipment will be required to vacate the movement area during certain weather conditions (refer [Section 2.1.3](#)) and in the event of an airport emergency (refer [Section 2.3](#)).

3.2. Working hours on site

Works will be conducted at all hours of the day as agreed by Melbourne Airport to minimise the disruption to operations.

3.3. Melbourne Airport operational policies

At all times the contractor must abide by Melbourne Airport's operational policies which include but are not limited to:

- Airside Works Safety.
- Drug and Alcohol Management Plan
- Airside Vehicle Control Handbook

All operational policies are available on the [Melbourne Airport website](#).

3.4. Site restriction markings/lighting

Melbourne Airport may request the contractor to define the Site Restricted area (SRA).

The SRA is to be defined by either:

- 900mm or 300mm high red/white-water barriers
- A continuous line of witches' hat, or
- Other visual aids (markers, or lights) as approved by the Airfield Operations Works Coordinator or delegate.

Yellow warning lights may be requested to be used to define the area during night works. Red lights may also be requested to be placed around hazards within the work area.

The works party, including all works vehicles that are not appropriately lit or approved under the Melbourne Airport Standard Blanket Clearance are not permitted to move outside the works area without the approval of the Works Safety Officer.

3.5. Access to the work site

Access to the work sites for all vehicles and deliveries will be via the access gates as shown on the attached plans. No vehicle will be allowed access or egress through any other gate except as approved by the Airfield Operations and Works Coordinators.

Vehicles and plant moving between the access gate and the work site must follow the route specified on the attached plan under the escort of an escort vehicle unless otherwise approved by Airfield Operations.

Delivery vehicles moving to and from the work site will be issued with a temporary pass at the access gate.

Vehicles that frequently gain access to airside must apply for a permanent Airside Vehicle Permit (Authority to Use Airside).

3.6. Traffic management plans

A Traffic Management Plan (TMP) must be submitted to the Airfield Operations and Works Coordinator in the event any works have an impact on any airside roads including Apron Service Road, Airside Road or Perimeter Road.

Access from access gate to the worksite for all contractors who do not have an Airside Drivers Authority (ADA) will be by escort only.

3.7. Marking and lighting of vehicles

Vehicles accessing the site will be required to have signs that clearly identify the vehicle as belonging to that company (an A4 size sign should be taken as a guide) and be issued with an Authority to Use Airside (AUA).

Additionally, all vehicles while operating airside will be required to have fitted an amber beacon which is visible 360 degrees of the vehicle and must be visible up to 200 meters from the vehicle in normal daylight conditions.

Please refer to the [Airside Vehicle Control Handbook](#) on the Melbourne Airport website for more information.

3.8. Vehicle / equipment height limit

No vehicle or other item of plant over 5 metres high may be used at the works site without authority from the Airfield Operations and Works Coordinator. Works parties must comply with any other associated requirements in the Melbourne Airport Manual, including the associated Obstacle Restriction Area instrument as detailed in [Height and location of critical obstacles](#).

The western track between Gates 11 and 8 will remain usable in all conditions except LVO with the two following restrictions:

- vehicle heights on this section of roadway **are not to exceed 4m**, and
- vehicles **are not permitted to stop** on this roadway section at any time.

If either of the two conditions cannot be achieved, this section of road cannot be used without tower approval as the integrity of the ILS may be affected.

3.9. Speed limits

Maximum speed limits apply as follows:

A 10km/h speed limit applies:

- Around or under buildings (Airside Road, Concourse Road, Freight Service Road)
- Apron area within 15 metres of an aircraft

A 15km/h speed limit applies:

- Apron area not within 15 metres of an aircraft and not under or around buildings

A speed limit of 15km/h for tugs and 25km/h for all other vehicles applies to:

- Roadway from Gate 27 to south of Bay H2 (Airside Access Road)
- Roadway from maintenance bases and the rest of the airfield (Maintenance Road)
- Roadway from Gate 27 to G.S.E maintenance precinct (Airside Access Road)

A 40 km/h speed limit applies:

- On taxiways

A 60km/h speed limit applies:

- On the Perimeter Road unless otherwise signposted

Breaches of the speed limit will result in a Penalty Infringement Notice (PIN) being issued or refusal of access to the driver and vehicle involved.

3.10. Parking of private vehicles

Only vehicles and plant engaged in the works will be permitted at the works site. All other vehicles must be parked at a site pre-arranged with the Project Manager.

All vehicles must be returned to the nominated compound at the completion of each day/night works.

3.11. Control of works personnel

All personnel associated with the work will always be bound by the directions of the Works Safety Officer with respect to operational safety matters.

3.12. Personal protective equipment (PPE) for the airside environment

The following PPE must be worn by all personnel airside:

- Hearing Protection
- Dayglow yellow High-Vis clothing or dayglow yellow vest that meet the Australian Standards
- Eye and Skin protection is to be worn in reference to the prevailing weather conditions
- Safety shoes must always be worn on works sites
- Hard Hats are required to be worn on work sites

Refer to the Melbourne Airport [Pedestrian Safety Policy](#) for further information.

4. Aerodromes Markers, Markings and Lights

4.1. General

Melbourne Airport shall mark the unserviceable operational area and install unserviceability markers and markings during the works as per the attached plans.

Closed portions of the manoeuvring area will be marked by red and white unserviceability markers during the day, and red unserviceability lights at night, in accordance with the CASR Part 139 Manual of Standards (MOS).

4.2. Lights

All Lighting within and directly leading into the closed portion of Manoeuvring area will be obscured or extinguished.

The closed taxiway is marked with unserviceability cones placed across the taxiway at 3m spacing. This is supplemented by red lights at 3m spacing across the taxiway at night or in poor visibility. The taxiway centreline lights within the closed portion of the taxiway and taxiway lights leading into the closed portion are extinguished or covered during the works. Where possible MAG signs are maintained to assist pilots and works parties in situational awareness.

4.3. Procedure for protection of electrical services and control cables

The contractor, before the commencement of any works, will confirm the location of all underground services. This check is usually done in conjunction with the issuing of a Permit to Commence Works (PERCOW) and prevents damage to any airport services.

An excavation permit must also be obtained prior to the commencement of any excavation works that penetrate the ground surface. Refer [Excavation permit](#).

5. Special Requirements

5.1. Airport security

Aviation Security Identification Cards (ASIC) must be obtained for all personnel associated with airside works. Melbourne Airport will issue an ASIC on application by the contractor. Applications must be made at least **6 weeks** in advance.

Once issued the ASIC must be worn and displayed at all times on the outside of their clothing, waist height or above, at the front or side of the person's body and with the front face of the card clearly visible by all staff whilst working on the airside of the airport.

Where contractors have applied, and the ASIC check is not complete:

- Visitor Passes may be used - restricted to 28 days within a 12-month period.
- Escort drivers and Works Safety Officers will act as the sponsor.

Delivery personnel with legitimate business on the airside may operate with a Visitor Pass under the supervision and escort of an ASIC holder.

5.2. Permits

5.2.1. Permit to commence works.

This MOWP is **not** an approval to commence works.

Before any works may commence the contractor must obtain a PERCOW from the [Melbourne Airport Buildings Approvals Officer](#). Please email the Building Approvals Officer should you require any further information.

5.2.2. Hot works permit

The contractor must obtain a Hot Works Permit from the Works Safety Officer prior to undertaking any oxy cutting, welding, or grinding on the airside of the airport.

A Hot Works Permit will be issued only when all Melbourne Airport safety requirements are met. For example, including but not limited to:

- the site is clean and free of all combustible material within 10m of works.
- a spark resistant solid hoarding is placed around the site.
- 2 x nine litre fire extinguishers are on site.
- A fire blanket (size of 3m square minimum) is on site.
- A "spotter" is in attendance for the duration of hot works.
- There are no refuelling aircraft or aircraft fuel vents in the vicinity of at least 50m for the duration of the permit.

When satisfied that all these conditions are being met a permit will be issued.

The permit is valid for a period of a maximum of one day and if works are to resume the next day a new permit is required.

Note: The permit only covers the location specified in the application. If the works move to another location a new permit is required.

Applications for Hot Works Permits within 5m of the building drip line will require approval from the [Fire & Life Safety Leader](#).

Permits will not be issued on days of a total fire ban.

5.2.3. Excavation permit

The contractor, before the commencement of any works, will lodge a dial before you dig (DBYD) job through the DBYD website. Once the Melbourne Airport drawing is received, the excavation area is to be highlighted clearly with a description of works. The contractor will confirm the location of all underground services by an independent service locator.

An excavation permit must be obtained from [Melbourne Airport – Airfield Lighting](#) at least 5 business days prior to any excavation works that penetrate the ground surface with the documents below included in the application:

- Copy of the PERCOW
- Independent Service locators Certificate
- DBYD service drawings of the works area with the works area clearly marked.

5.2.4. Crane permit

A permit must be obtained prior to the erection of any crane on the airport

Applications for approval must be sent to [Airfield Support](#) a minimum of **5 working days prior** to the crane lift including the following information:

- The proposed location of the lift activity (street address, MGA or AMG co-ordinates)
- A site locality plan (i.e. Aerial Photo Extract)
- Crane maximum height (AHD or m above ground level)
- Date, time, and duration of activity
- Work description and
- Contact details of Site supervisor and applicant

An email confirming approval will be sent to the applicant prior to the crane lift.

For equipment that are likely to penetrate Melbourne Airport Airspace, **12 weeks** notification is required.

5.2.5. Electrical isolation permit

Any works on or near electrical cables will require an electrical isolation permit. Requests are to be emailed through to [Melbourne Airport – Airfield Lighting](#) at least **24 hours prior** to the commencement of the activity with a list of the circuits required for isolation.

The contractor must supply a licensed electrician to carry out isolations (Lock out Tag out) with a Melbourne Airport Airfield Lighting Officer. Upon completion of the isolation procedures an isolation permit will be issued.

5.3. Critical obstacles

5.3.1. General requirements

Melbourne Airport's Prescribed Airspace cannot be penetrated without the relevant approvals. Refer [Crane permit](#).

Unless specifically approved, plant/vehicle or equipment cannot exceed a maximum height of **5 metres** within the closed area.

Note: This limit is only applicable in locations where the Melbourne Airport's Prescribed Airspace will **not** be penetrated.

5.3.2. Height and location of critical obstacles

For works within the Obstacle Restricted Area (ORA), works activities will comply with the Instrument of Approval number: CASA.ANAA.0101.2 issued from CASA on 19 February 2019. This instrument is maintained in the Melbourne Airport Manual.

These conditions will be communicated to the Works Safety Officer via the Airfield Operations Manager and to works parties via a contractor instruction.

5.4. Pavement and cleanliness

The contractor is to ensure that runways and taxiways used or crossed during the works are kept clean and free of debris.

A sweeper (no steel brushes), approved by the Airfield Operations and Works Coordinator, is always to be kept on call whilst works are in progress.

Areas within the works site must also be free of Foreign Object Debris (FOD).

No trench within the runway or taxiway strip may be left open, unattended or unprotected at the completion of each day/night works without prior approval of the Airfield Operations and Works Coordinator.

Any approved open excavations within the works area must be covered with heavy duty steel plates and defined by either 900mm or 300mm red and white half-filled water barriers and/or red lights.

5.5. Waste disposal and environment protection

Any putrescible waste generated at the site is to be placed in secure, covered rubbish bins and removed from the airport at the end of each working day.

The contractor must ensure that all other waste is contained within the site and not free to blow around the airport. Builder's waste must be removed well clear of the movement area to a site directed by the Works Safety Officer and the Melbourne Airport Environment Manager.

The contractor must comply with all environmental controls as specified in the Construction Environment Management Plan provided by the contractor and endorsed by the Melbourne Airport Environment Manager or delegate.

Please refer to the Melbourne Airport Environmental Management Plan which can be found on the Melbourne Airport [website](#).

5.6. Explosives

No explosives or explosive power tools may be used on the airport without prior approval of the Airfield Operations and Works Coordinators.

5.7. Dust

Dust must be kept to a minimum and excavated areas must be constantly watered in windy conditions.

5.8. Dumping of fill

Fill must be transported from the site to landside and dumped in an area approved by the Melbourne Airport Environment Team and the Airfield Operations and Works Coordinators.

Fill must not be dumped or stored airside without the express approval of the Airfield Operations and Works Coordinator.

5.9. Site sheds and locations

Site shed locations that have any impact on the airlines staging or storage area must be approved by the Airfield Operations and Works Coordinators.

5.10. Food consumption

Due to wildlife the consumption of any food whilst airside should be contained within a vehicle, or an approved sealed site shed (at no stage should food be consumed outside in open areas).

5.11. Smoking

All the airside is a designated NO SMOKING area.

Smoking is not permitted within the works site, the building area or in any vehicle whilst airside.

5.12. Wildlife hazards

The contractor is to monitor all work sites for increased wildlife activity. In the event of an increase in wildlife activity, the contractor is to notify Car2 and the Airfield Operations Manager immediately. All precautions are to be taken to minimise this risk.

To limit the risk of wildlife activity on the airfield, restrictions apply to eating airside. Eating is restricted to inside enclosed areas only. Any food scraps must be disposed of correctly in suitable bins to prevent attracting wildlife. Any bins used to dispose of food scraps must be emptied daily. Food vans are not permitted on the airfield.

Wildlife hazards must be reported immediately to the WSO assigned to the site or if unavailable, to the [Car2](#). Wildlife hazard management is to be handled in accordance with the Melbourne Airport Airside Operational Safety Policy –Wildlife Hazard Management. This document is available on the [Melbourne Airport website](#).

5.13. Lime and cement stabilisation

Lime and cement spreading is not allowed to take place during the following conditions:

- in winds greater than 5 knots
- if the wind is blowing towards the terminal
- if the wind is blowing towards critical operational areas such as an active apron, TWY or RWY system

The contractor will employ additional measures to minimise the escape of dust from the site. It is preferable that contractors undertake the spreading of lime and cement dust at early morning/dusk hours to minimize impacts on airfield operations. An approval must be obtained prior to any spreading from [Car2](#).

5.14. Inspection at the completion of works

On completion of the works (if applicable) the contractor is to return the area to a serviceable and compliant standard and to the satisfaction of the Car2.

Car2 must conduct a thorough inspection prior to reopening the area to ensure that the area is serviceable and compliant.

All facilities, markers and markings are to be carefully checked to ensure that they comply with the CASA standards. Special attention must be paid to markers and/or markings/lighting that may have been obliterated or obscured by the works party.

On completion of each stage of the works, the contractor is to:

- clean up the area to the satisfaction of the Airfield Operations and Works Coordinator and/or Car2
- rectify any pavement damage to the satisfaction of the Airfield Civil Maintenance Manager
- remove all building rubbish, excess materials and construction plant from the site

A joint inspection involving the Airfield Lighting Maintenance Manager, Airfield Facilities and Technical Manager, Airfield Civil Maintenance Manager, Airfield Operations and Works Coordinator, and the Airfield Operations Manager may be conducted before the works area is deemed to be completed.

6. Administration

6.1. Contractors

The work is being carried out by Melbourne Airport staff and contractors employed by Melbourne Airport.

6.2. Project Manager

The Project Manager will be the Airfield Facilities and Technical Manager Mr. Scott Bailey-Erturk +61 437 533 152.

All questions relating to the technical aspect of this project should be directed to the Project Manager.

Note: The Project Manager may change throughout these stages of works, changes will be advised within the Local Works Plan

6.3. Works Organiser

The Works Organisers will be the Airfield Civil Maintenance Manager Mr Tony Epenian 0416 094 689 and the Airfield Lighting Maintenance Manager Mr Gavan Saker 0418 775 788.

All questions relating to the practical aspect of this project should be directed to the Works Organisers

Note: The Works Organisers may change throughout these stages of works, changes will be advised within the Local Works Plan.

Nominated Senior Works Safety Officer Car 2 +61 418 335 985

The Nominated Senior Works Safety Officer Car 2 will be contactable 24/7.

All questions relating to the practical aspect of this project should be directed to the [Works Organiser](#).

6.4. Airfield Operations and Works Coordinator

The Melbourne Airport [Airfield Operations and Works Coordinator](#) will be either Mrs Leanne Carroll or Mr Ron Butterworth.

Any queries about the conditions contained in this MOWP or the effect of the works on aircraft operations should be directed to the Airfield Operations and Works Coordinator.

6.5. Works Safety Officer

The Senior Airside Safety Officer (Car2) will be the nominated Senior Works Safety Officer to look after the works. [Car2](#) will be contactable 24/7.

The Senior Works Safety Officer may be supported by one or a team of Works Safety Officers which may delegate some or all the specified responsibilities.

The Senior Works Safety Officer will be responsible for the operational safety of the works including the opening and closing of the works areas.

The Works Safety Officer performs the responsibilities as specified in the CASR Part 139 MOS and as required for these works.

6.6. MOWP Author

This MOWP has been written by:

Leanne Carroll

**Airfield Operations and Works Coordinator
Melbourne Airport**

7. Authority

7.1. Conduct of Works

All works must be carried out in accordance with the MOWP.

7.2. Expiry

This MOWP will expire on 30/08/2025 unless otherwise amended or extended.

7.3. Variation

The approval of the Airfield Operations and Works Coordinator must be obtained before any variation is made to this MOWP or associated NOTAM. Verbal approvals are to be confirmed in writing at the earliest opportunity.

7.4. Approval

This MOWP has been checked and concurred with by Airservices Australia, major airline operators and internally within Melbourne Airport.

The MOWP is issued by Melbourne Airport in accordance with the CASR Part 139 MOS – Aerodrome Chapter 16 Method of Working Plans issued by the Civil Aviation Safety Authority.


The Head of Airfield has authorised this MOWP as delegated in writing by the Accountable Manager for Melbourne Airport, as identified in the Melbourne Airport Manual



Mark Wilson
Head of Airfield


8. Drawings

8.1. Stage R1

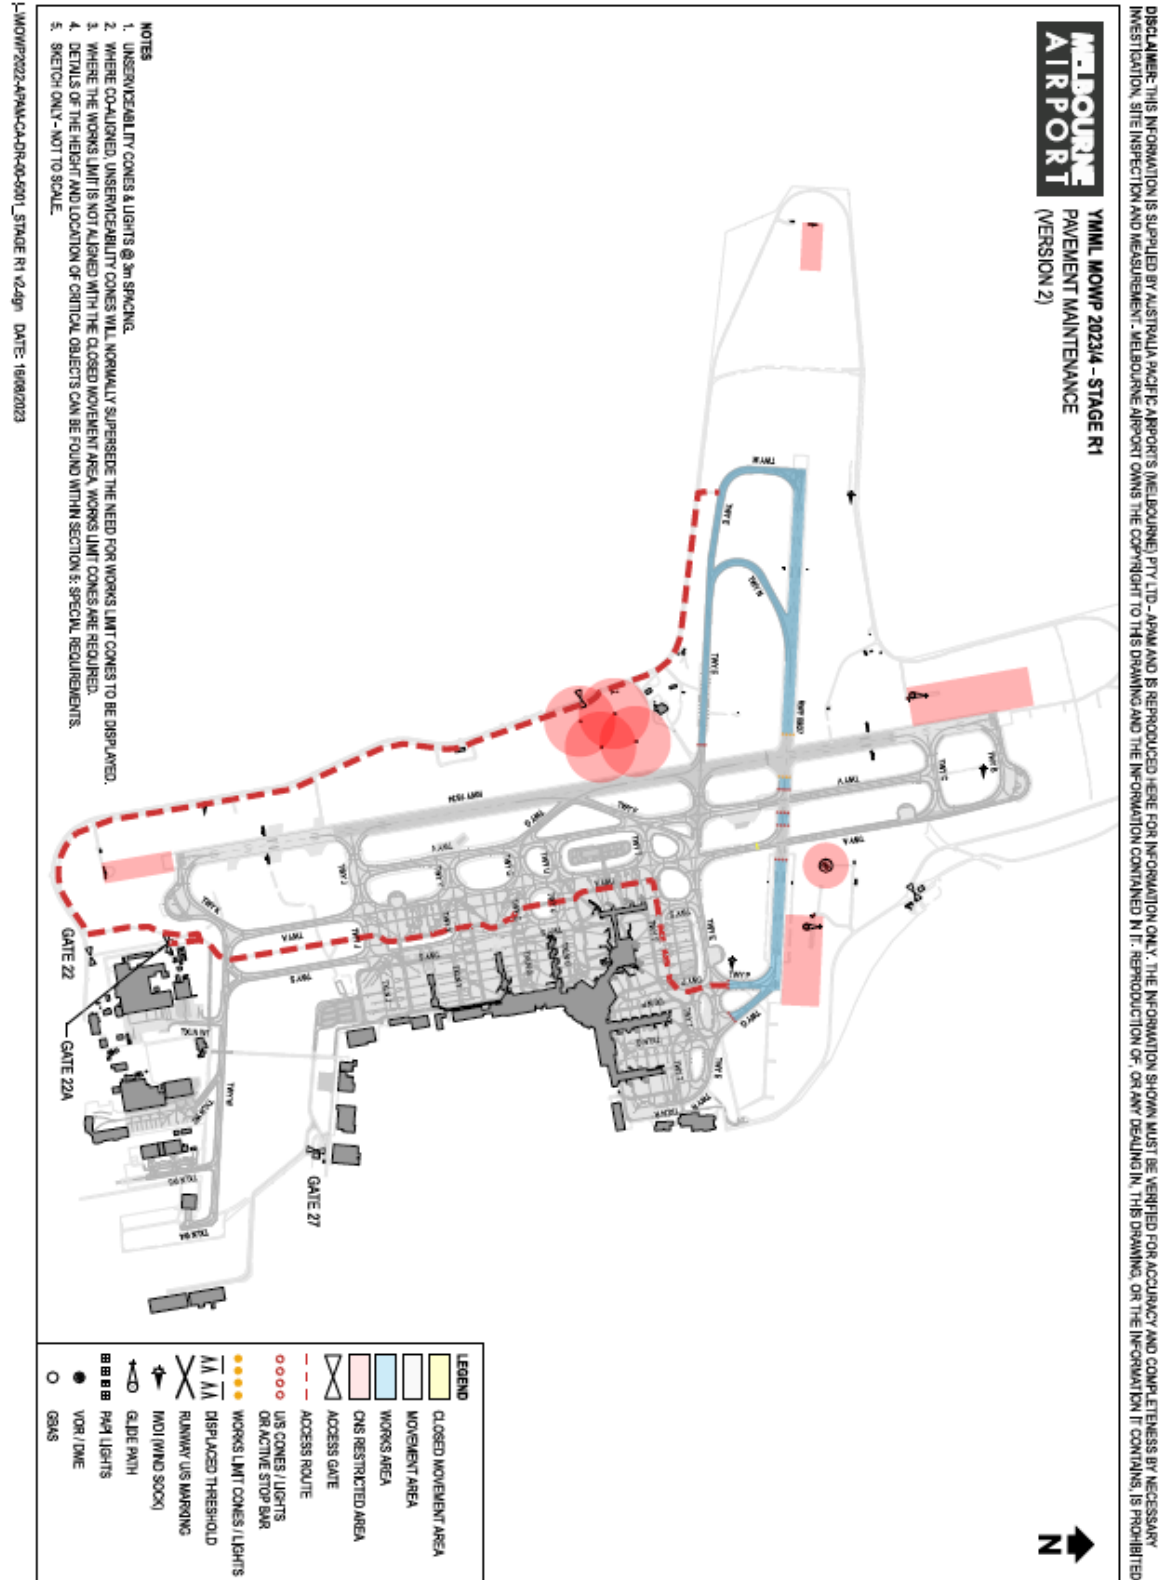


DISCLAIMER: THIS INFORMATION IS SUPPLIED BY AUSTRALIA PACIFIC AIRPORTS (MELBOURNE) PTY LTD. (APM) AND IS REPRODUCED HERE FOR INFORMATION ONLY. THE INFORMATION SHOWN MUST BE VERIFIED FOR ACCURACY AND COMPLETENESS BY NECESSARY INVESTIGATION, SITE INSPECTION AND MEASUREMENT. MELBOURNE AIRPORT OWNS THE COPYRIGHT TO THIS DRAWING AND THE INFORMATION CONTAINED IN IT. REPRODUCTION OF OR ANY DEALING IN THIS DRAWING, OR THE INFORMATION IT CONTAINS, IS PROHIBITED.

8.2. Stage R2

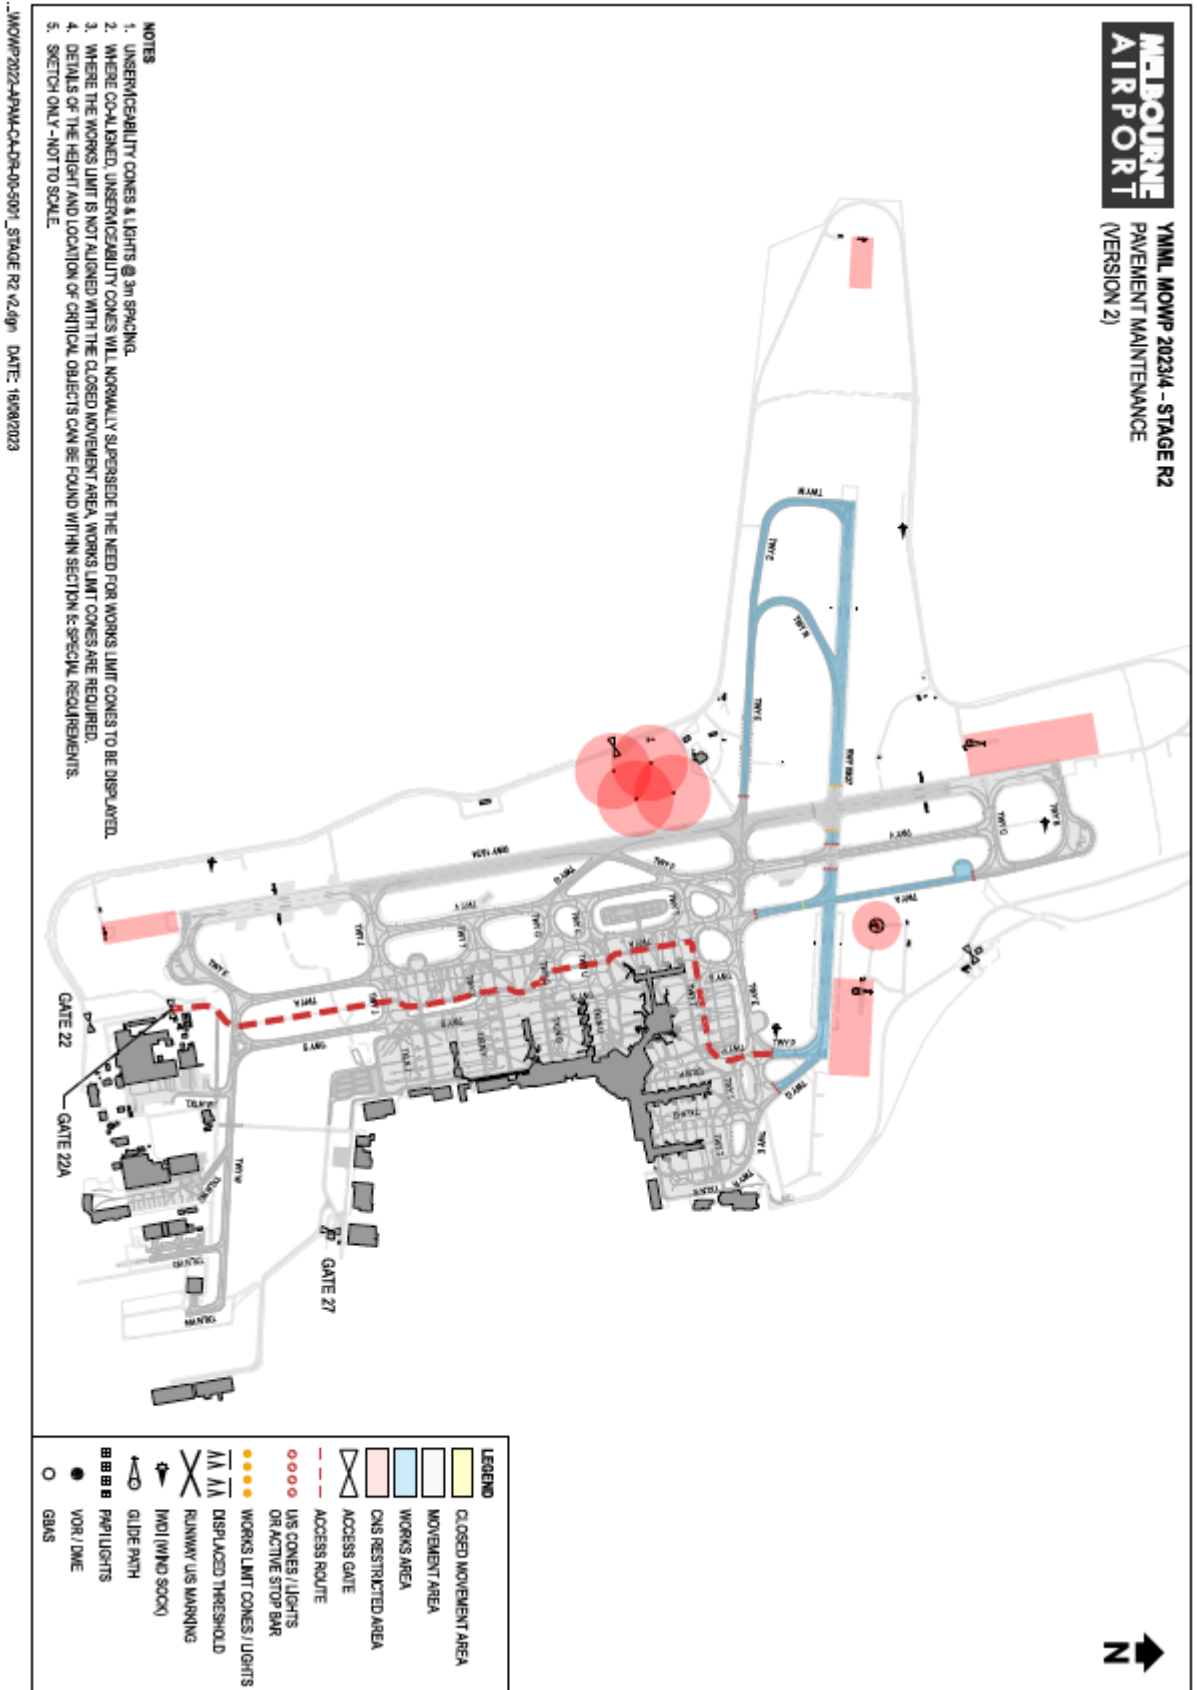


DISCLAIMER: THIS INFORMATION IS SUPPLIED BY AUSTRALIA PACIFIC AIRPORTS (MELBOURNE) PTY LTD. APAM AND IS REPRODUCED HERE FOR INFORMATION ONLY. THE INFORMATION SHOWN MUST BE VERIFIED FOR ACCURACY AND COMPLETENESS BY NECESSARY INVESTIGATION, SITE INSPECTION AND MEASUREMENT. MELBOURNE AIRPORT OWNS THE COPYRIGHT TO THIS DRAWING AND THE INFORMATION CONTAINED IN IT. REPRODUCTION OF, OR ANY DEALING IN, THIS DRAWING, OR THE INFORMATION IT CONTAINS, IS PROHIBITED.


8.3. Stage R3

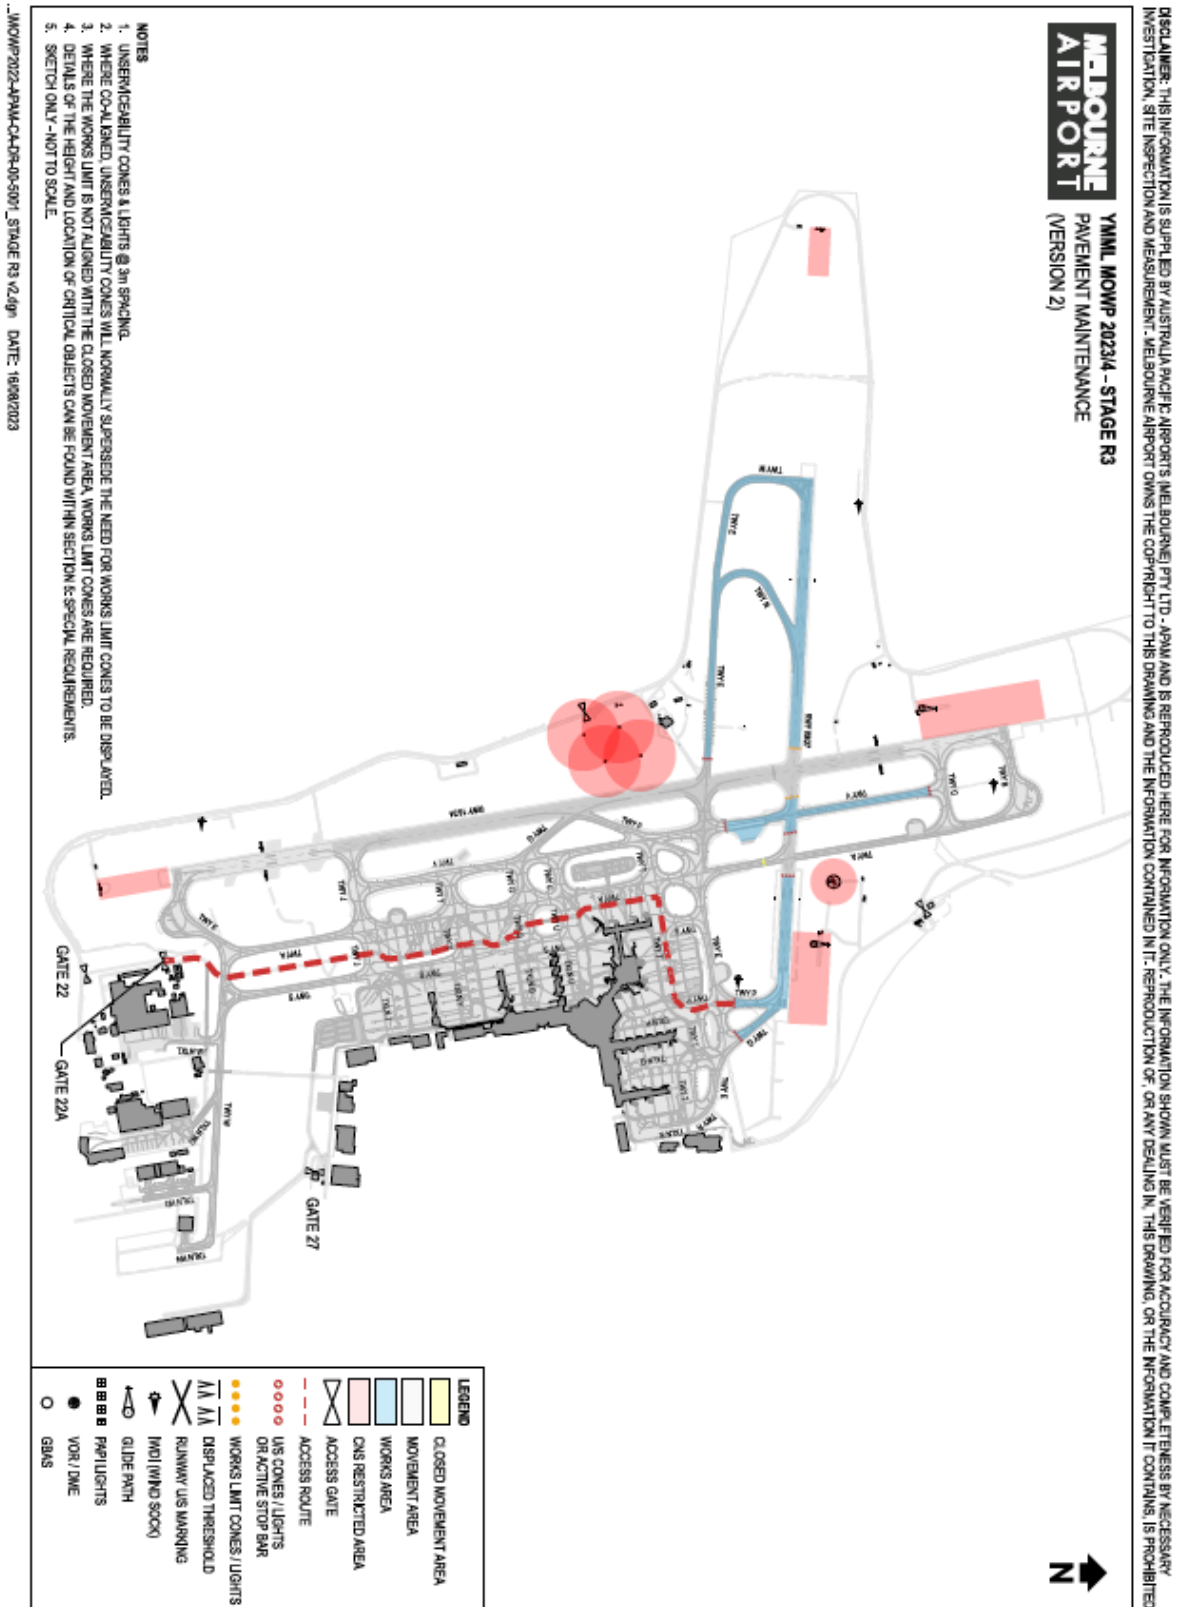


8.4. Stage R4

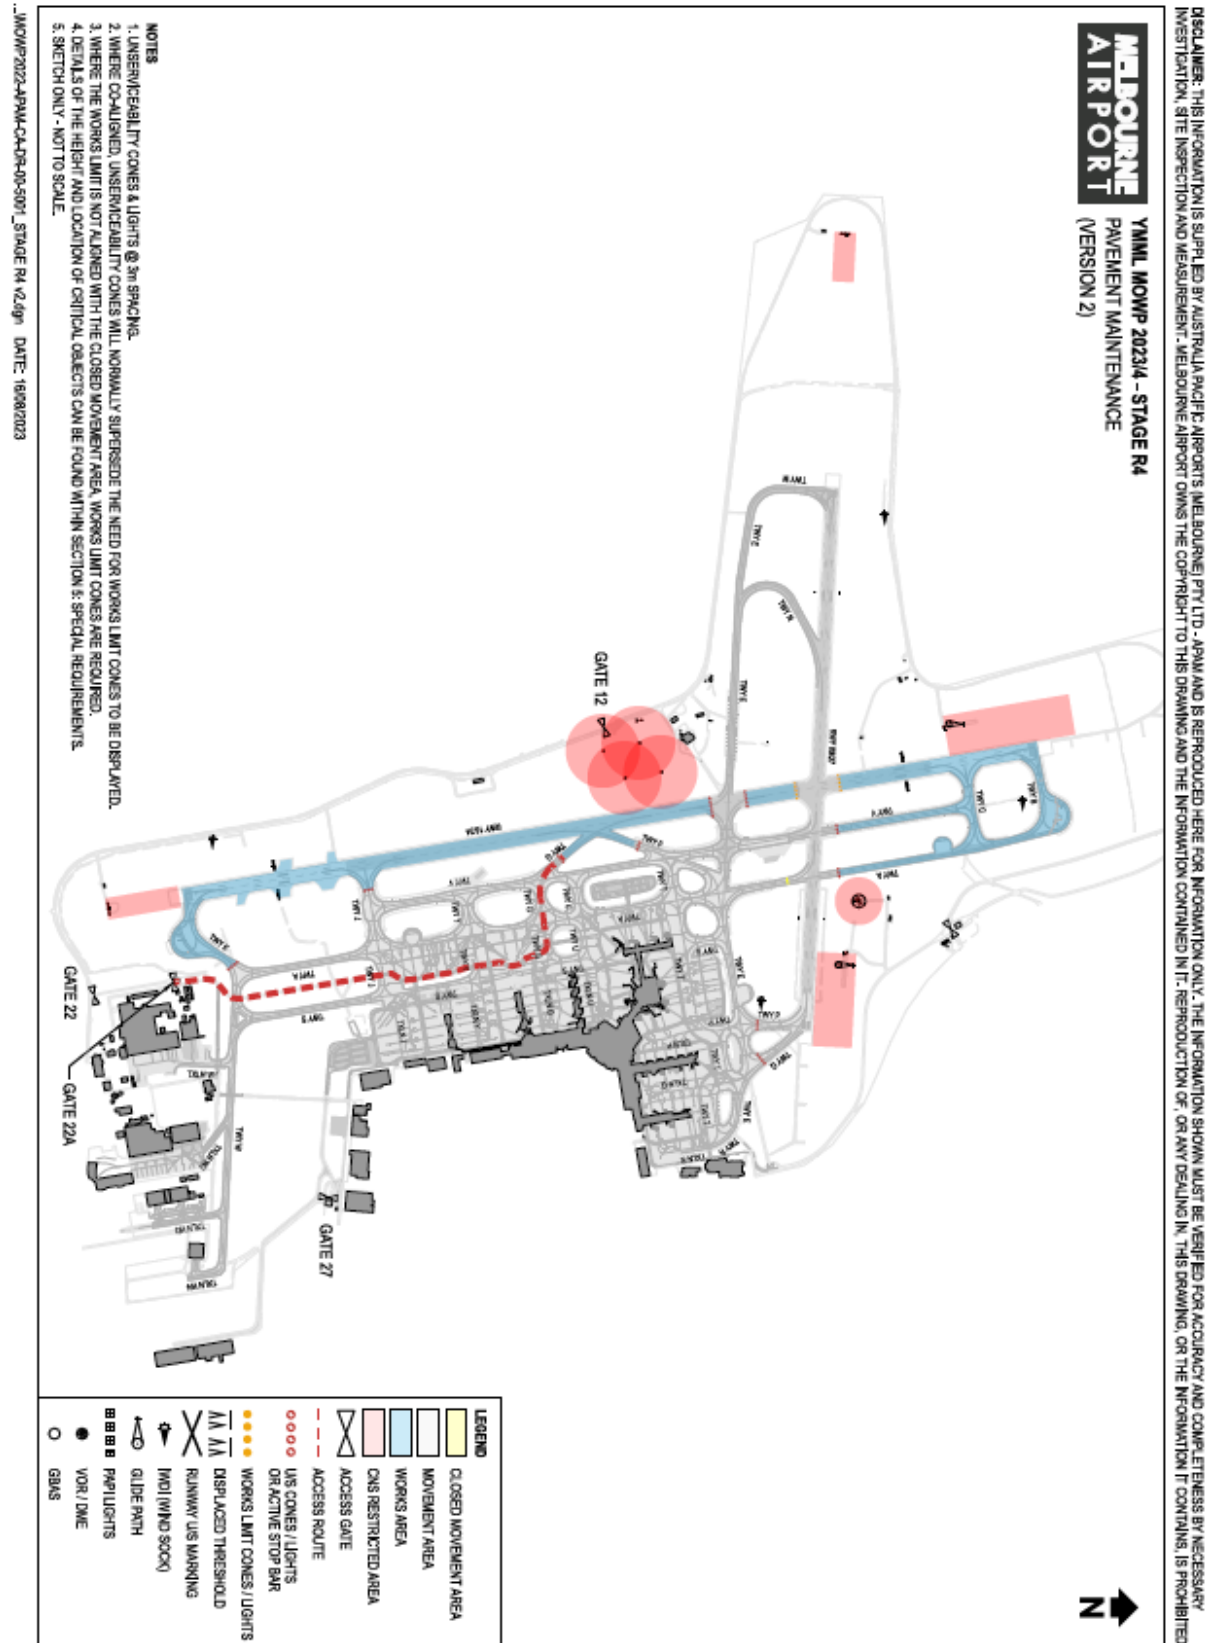


8.5. Stage R5

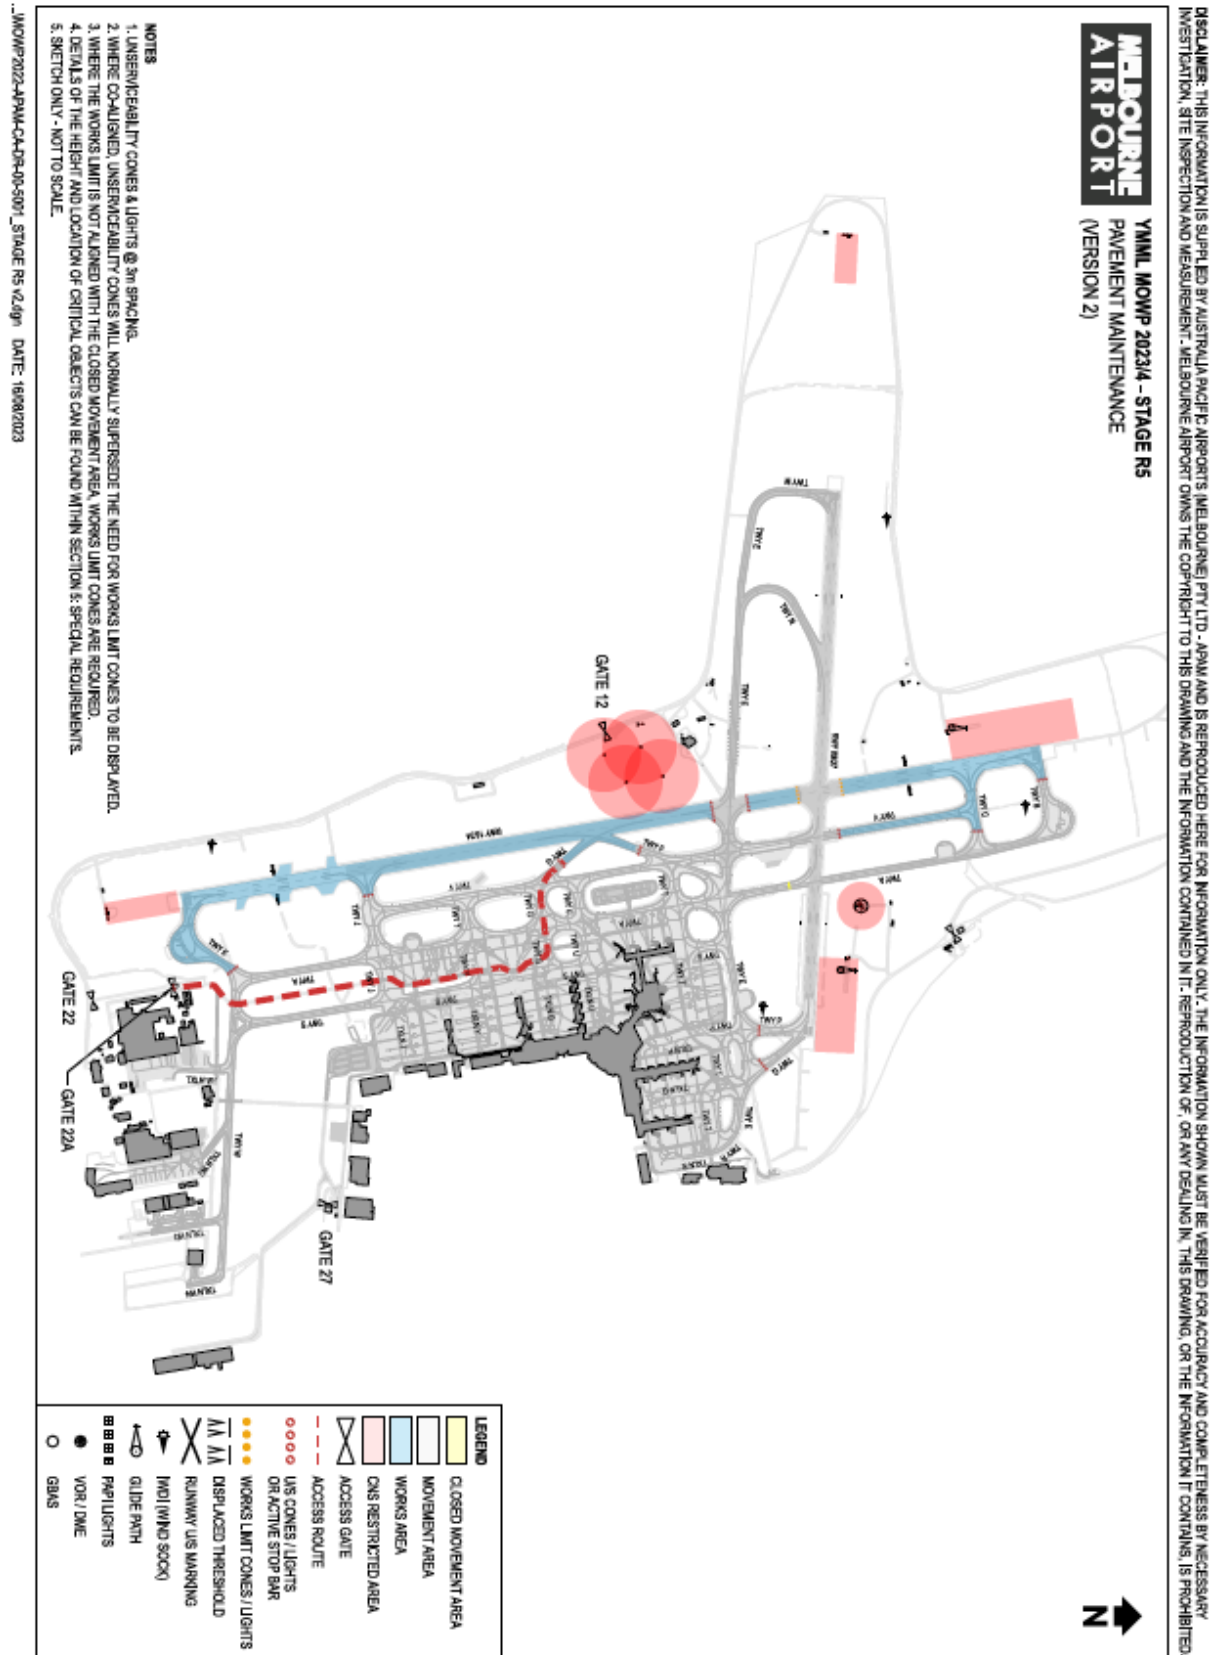


8.6. Stage T1

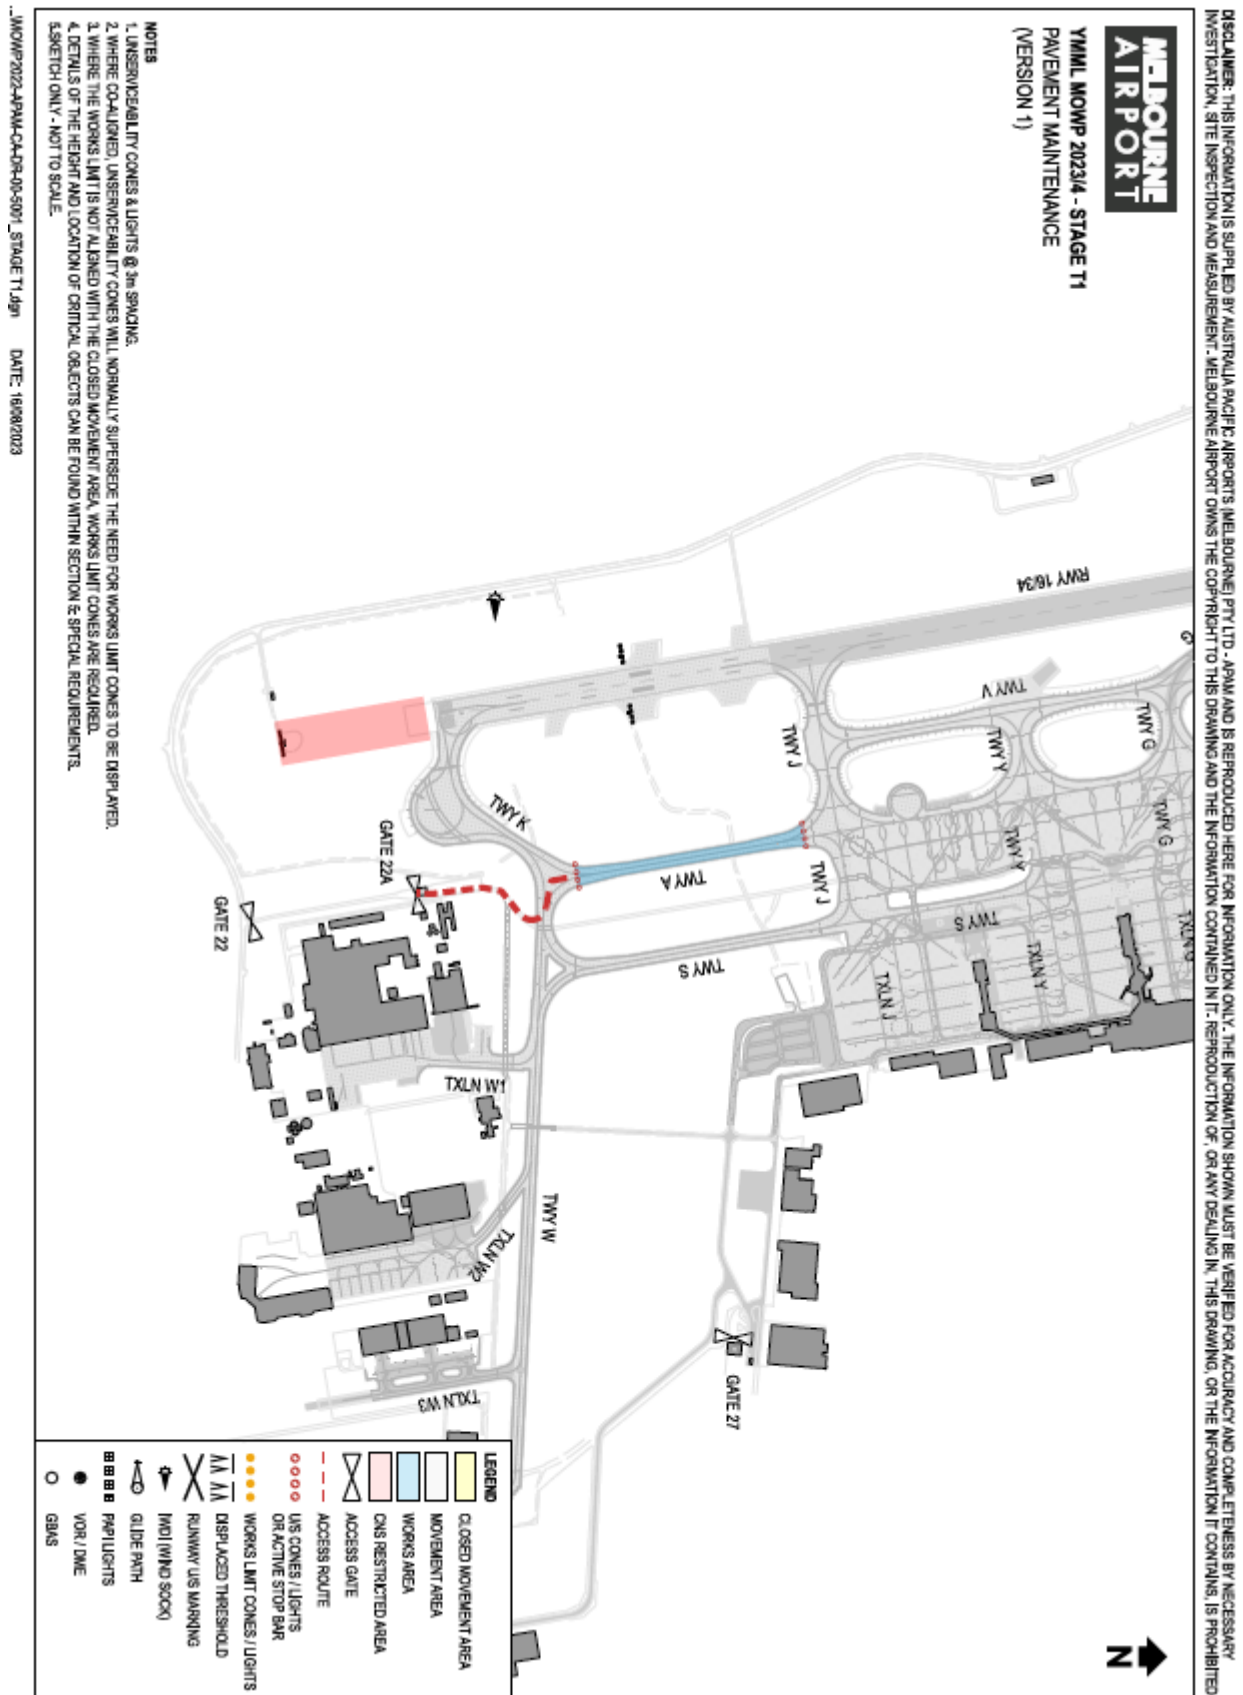


8.7. Stage T2

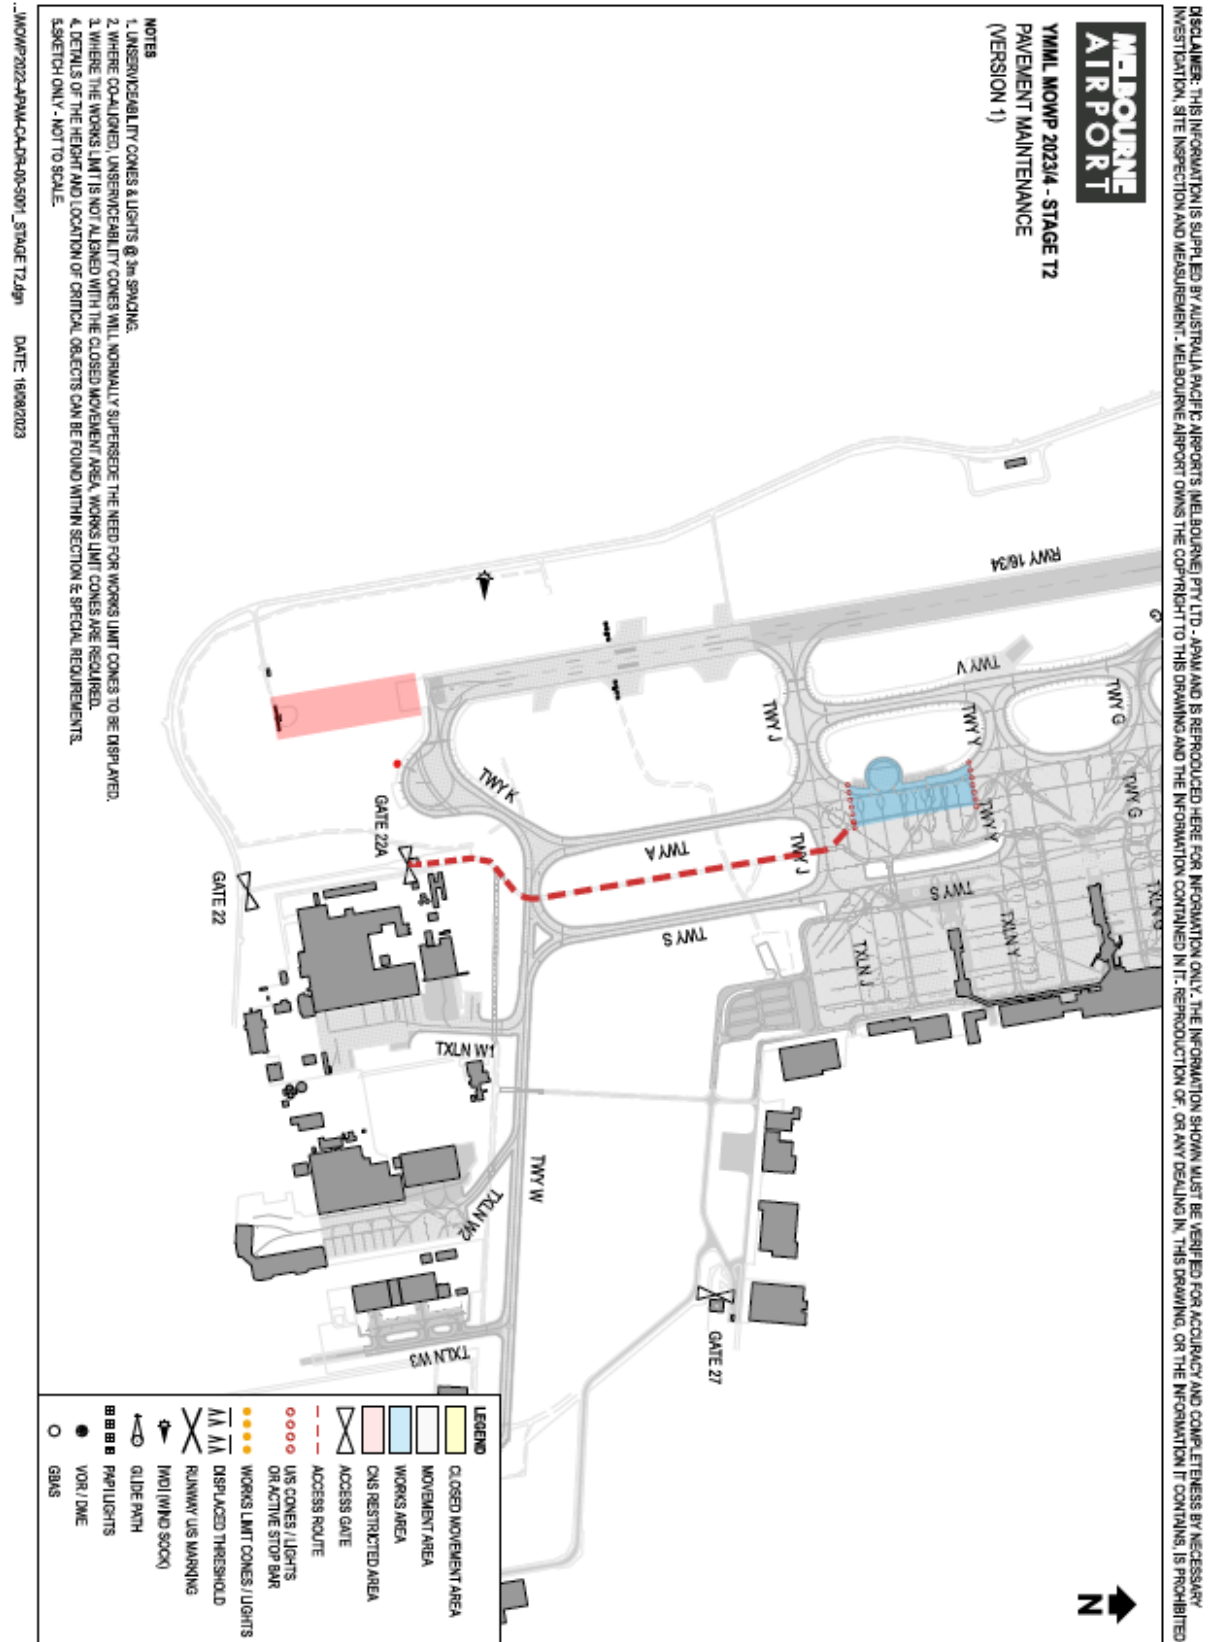


8.8. Stage T3

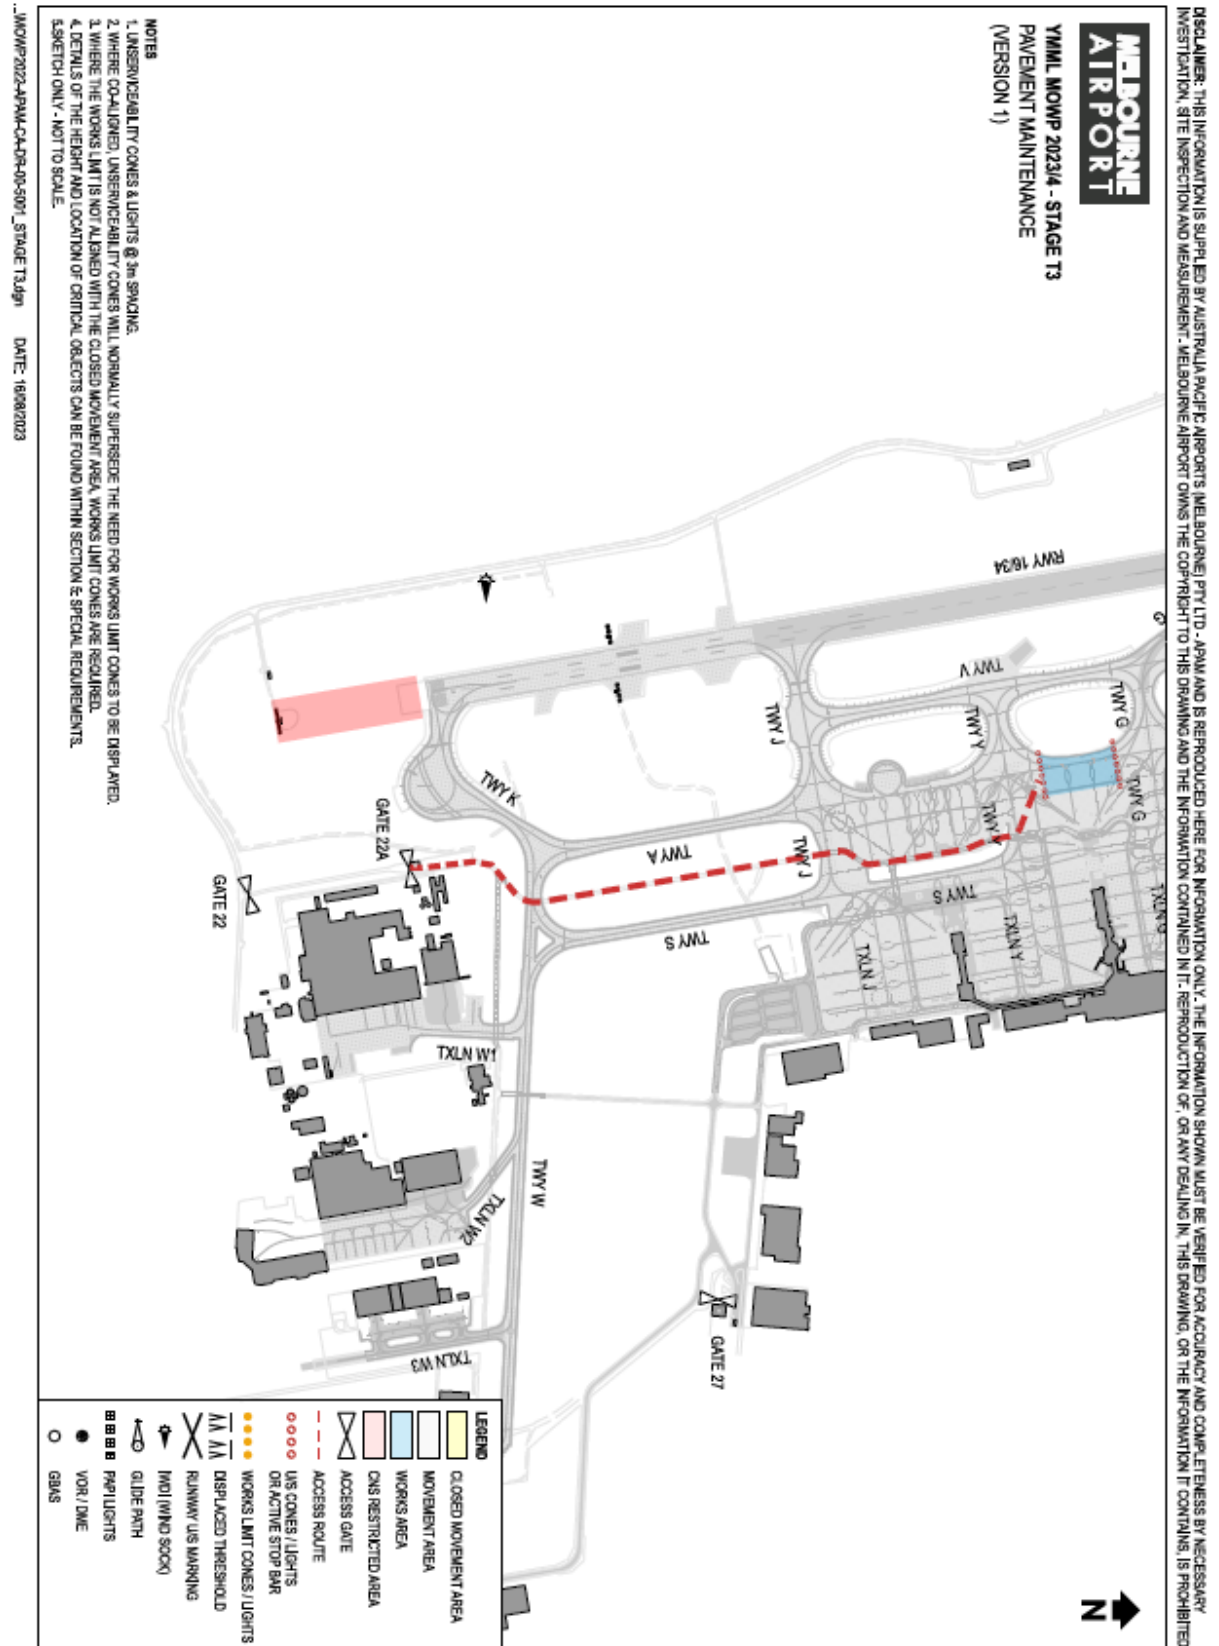


8.9. Stage T4

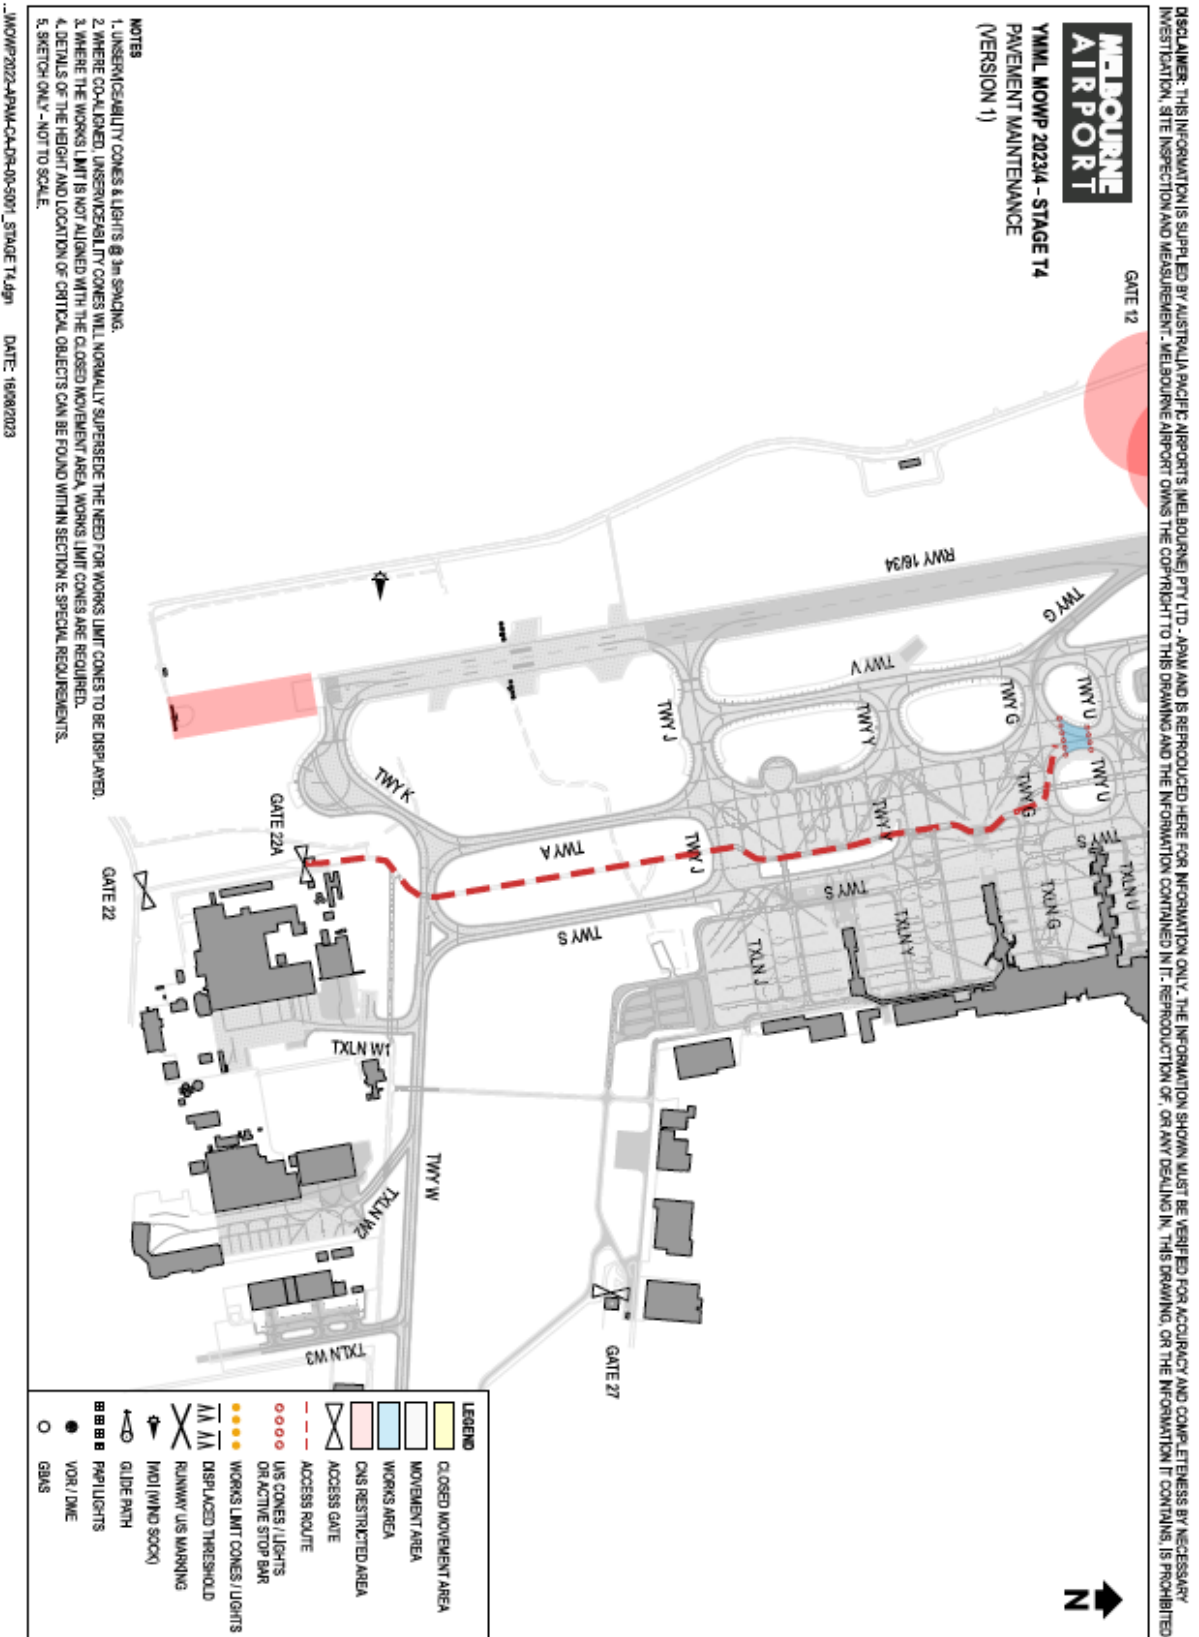


8.10. Stage T5

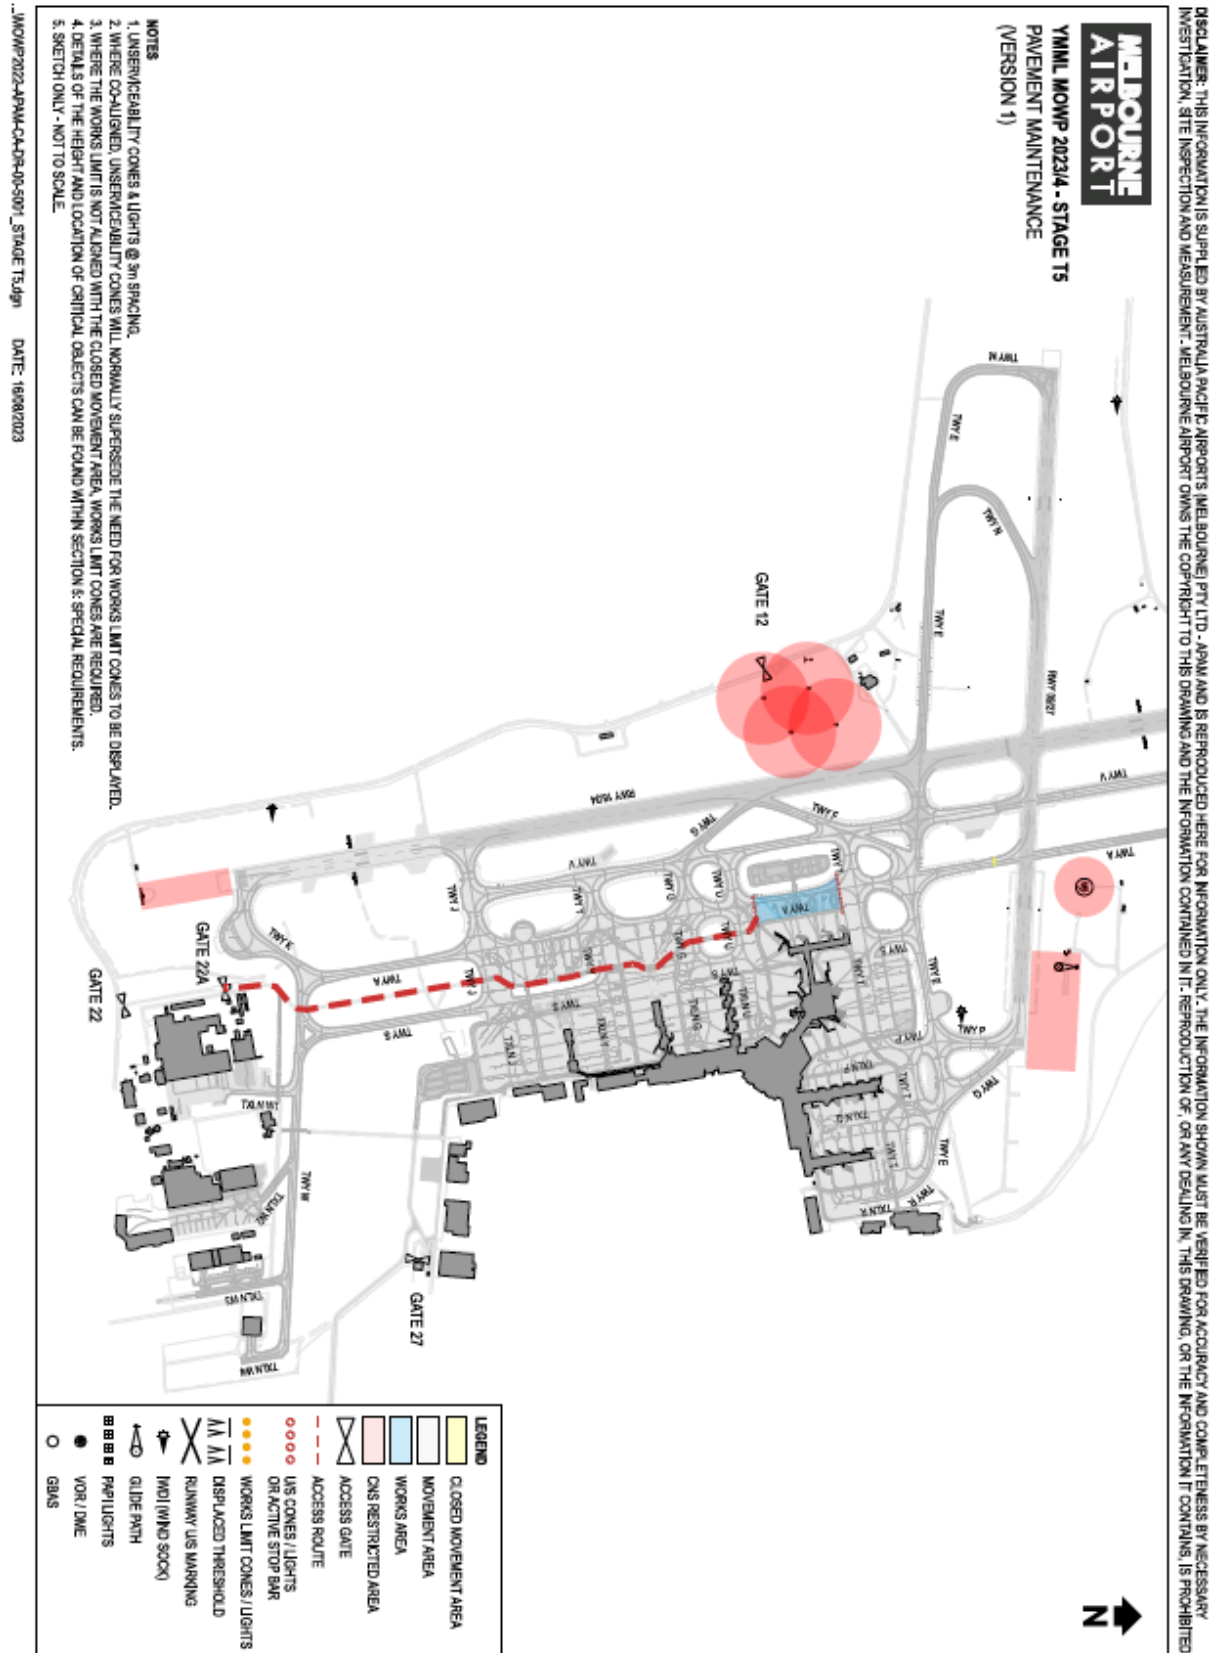


8.11. Stage T6

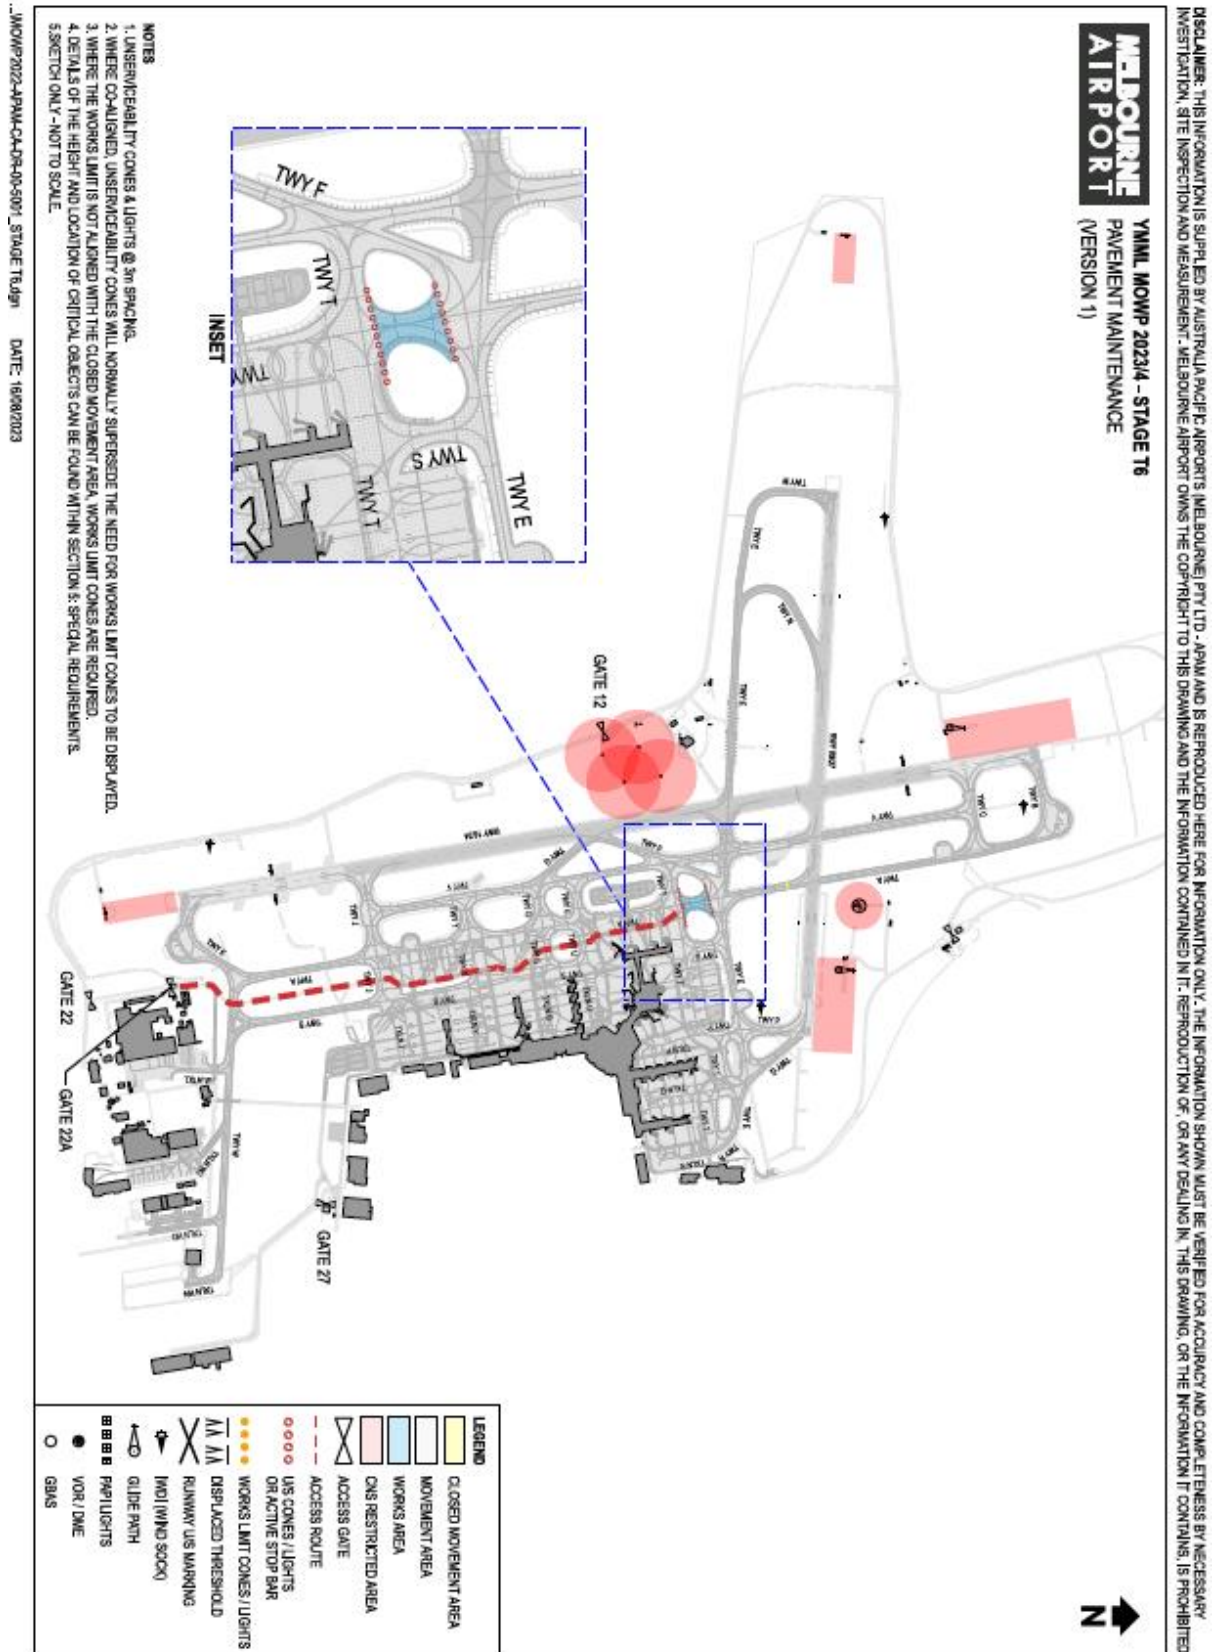


8.12. Stage T7

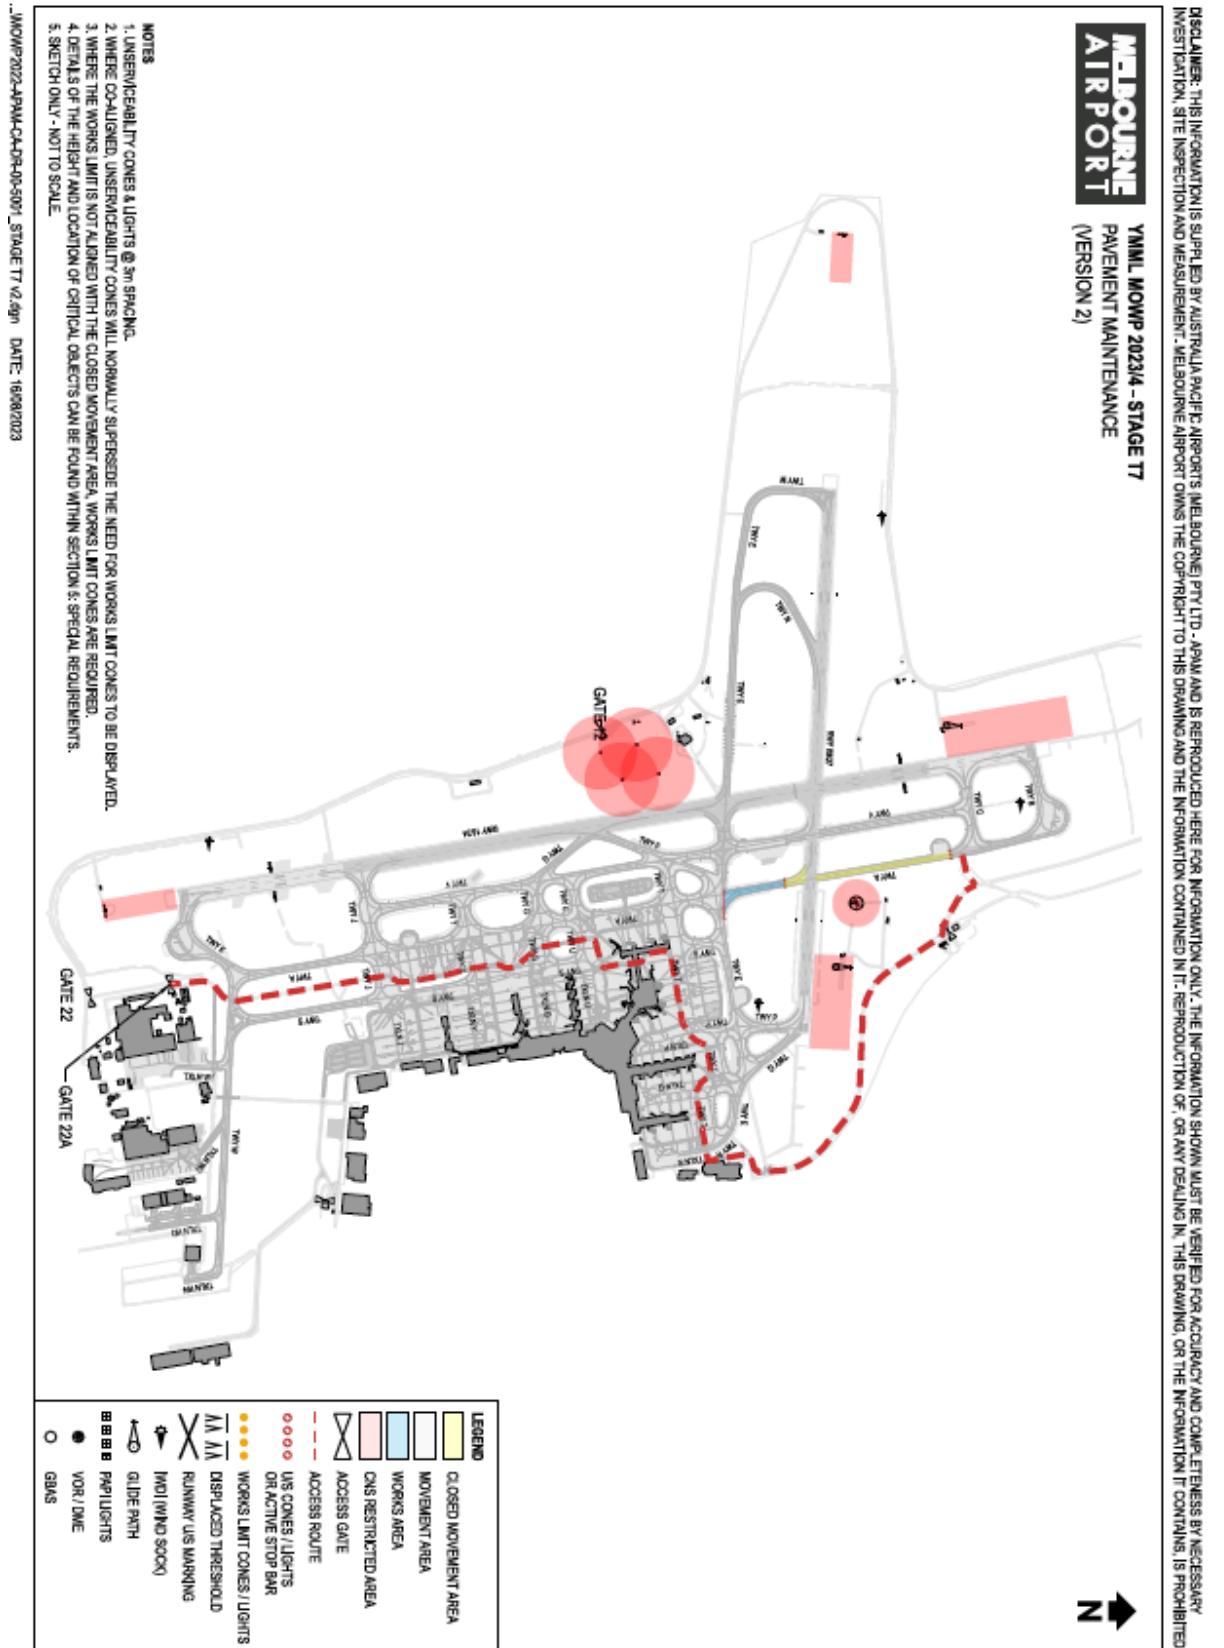


8.13. Stage T8

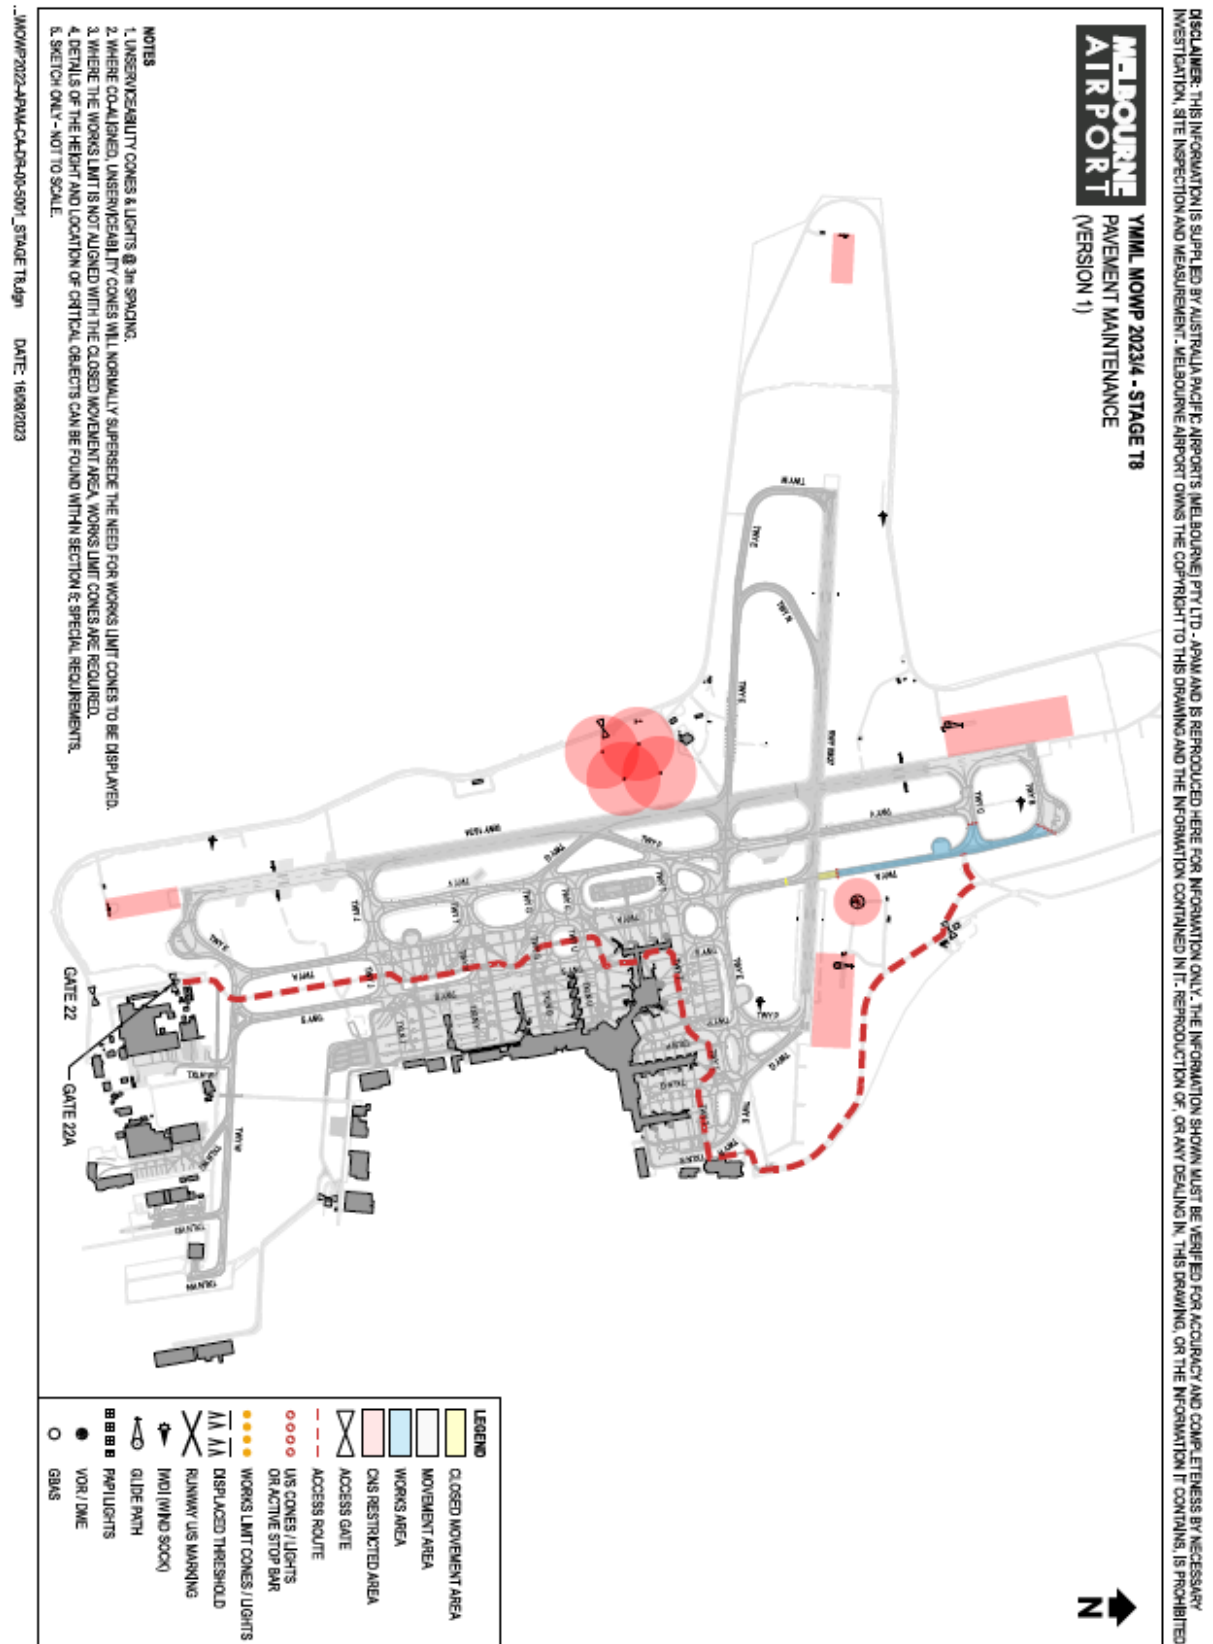


8.14. Stage T9

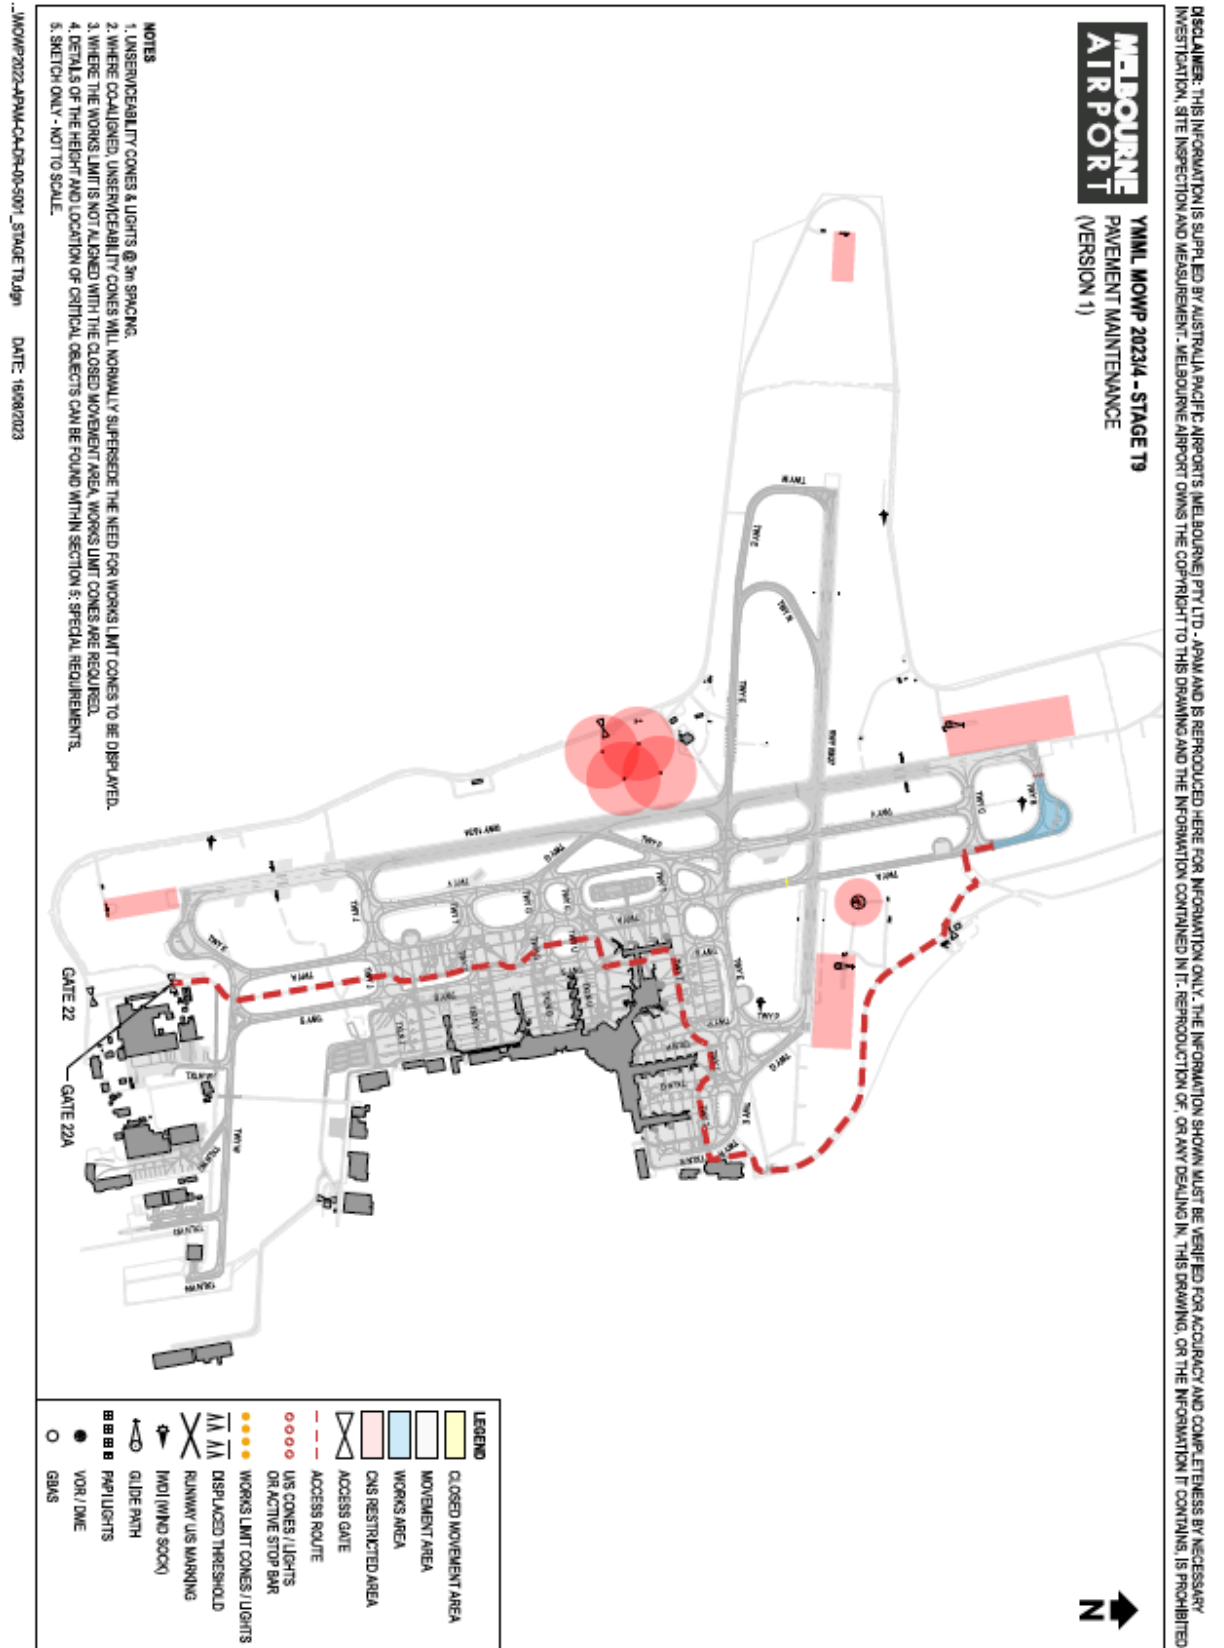


8.15. Stage T10

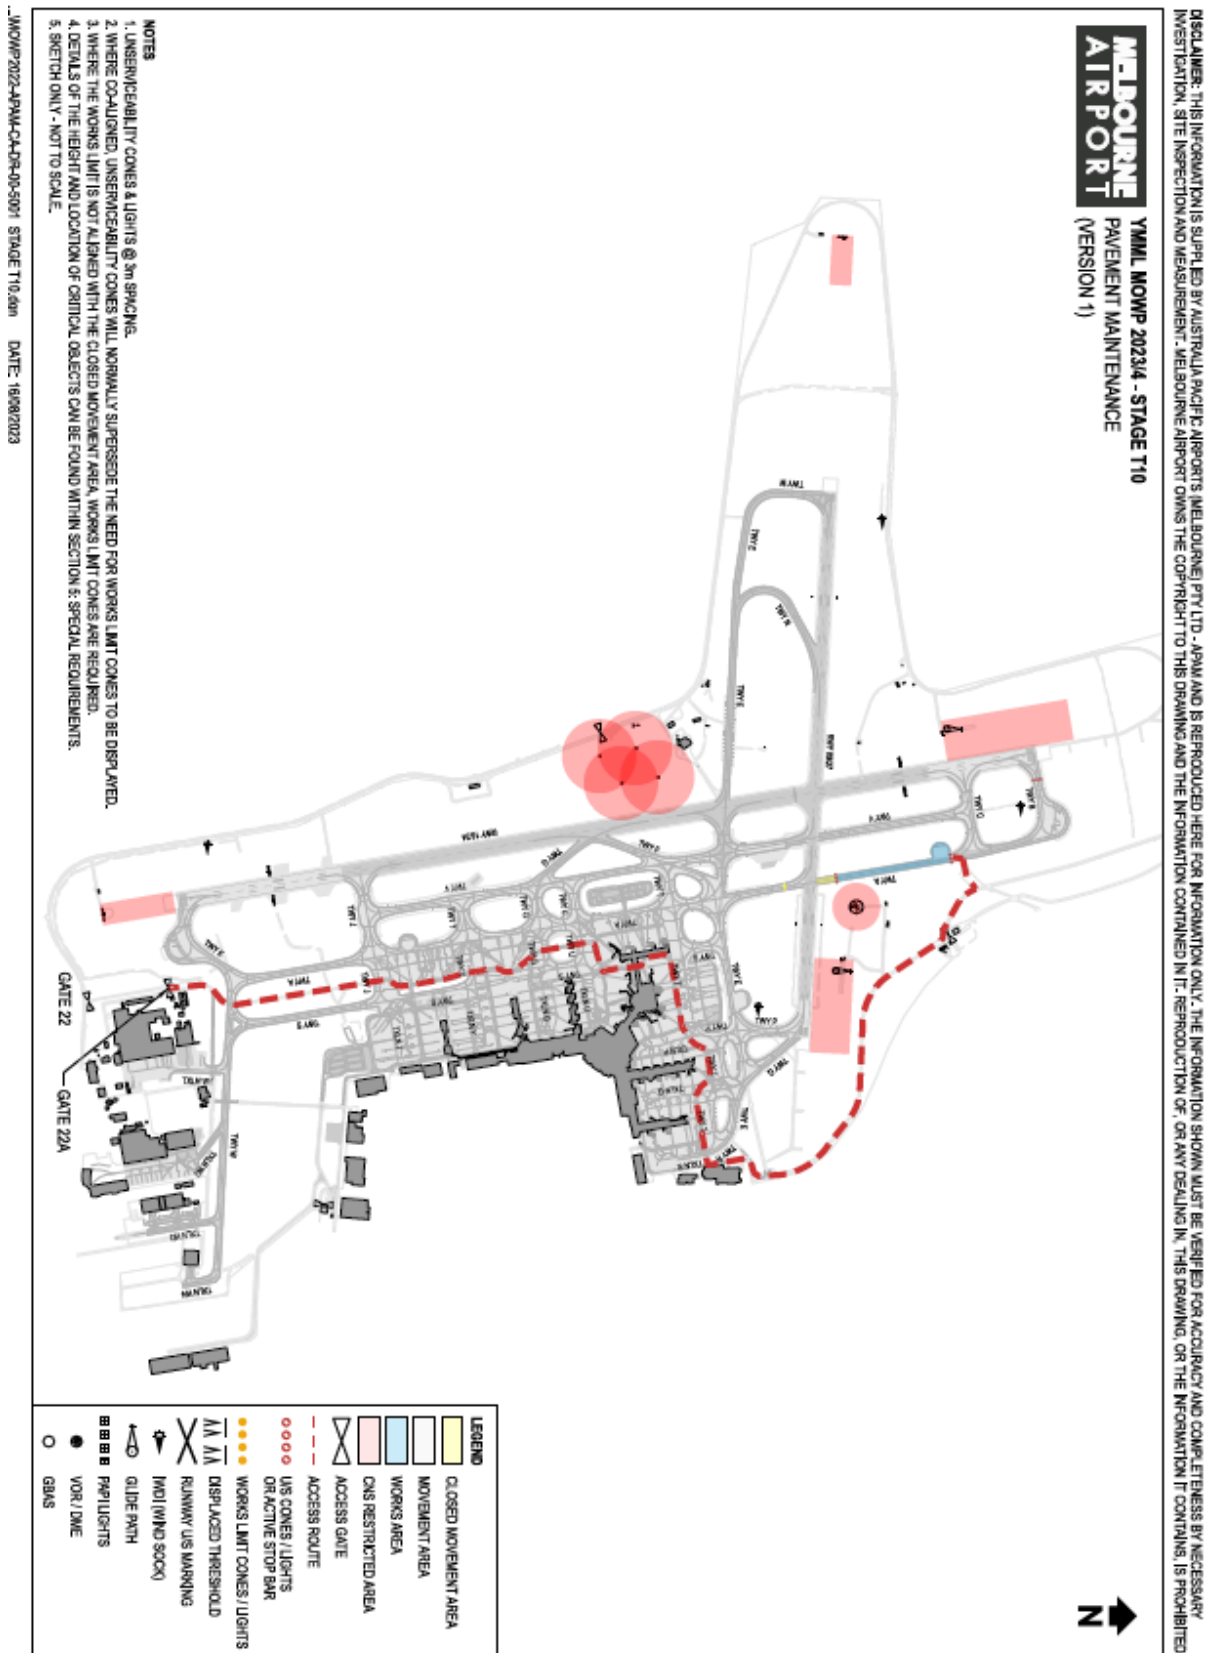


8.16. Stage T11

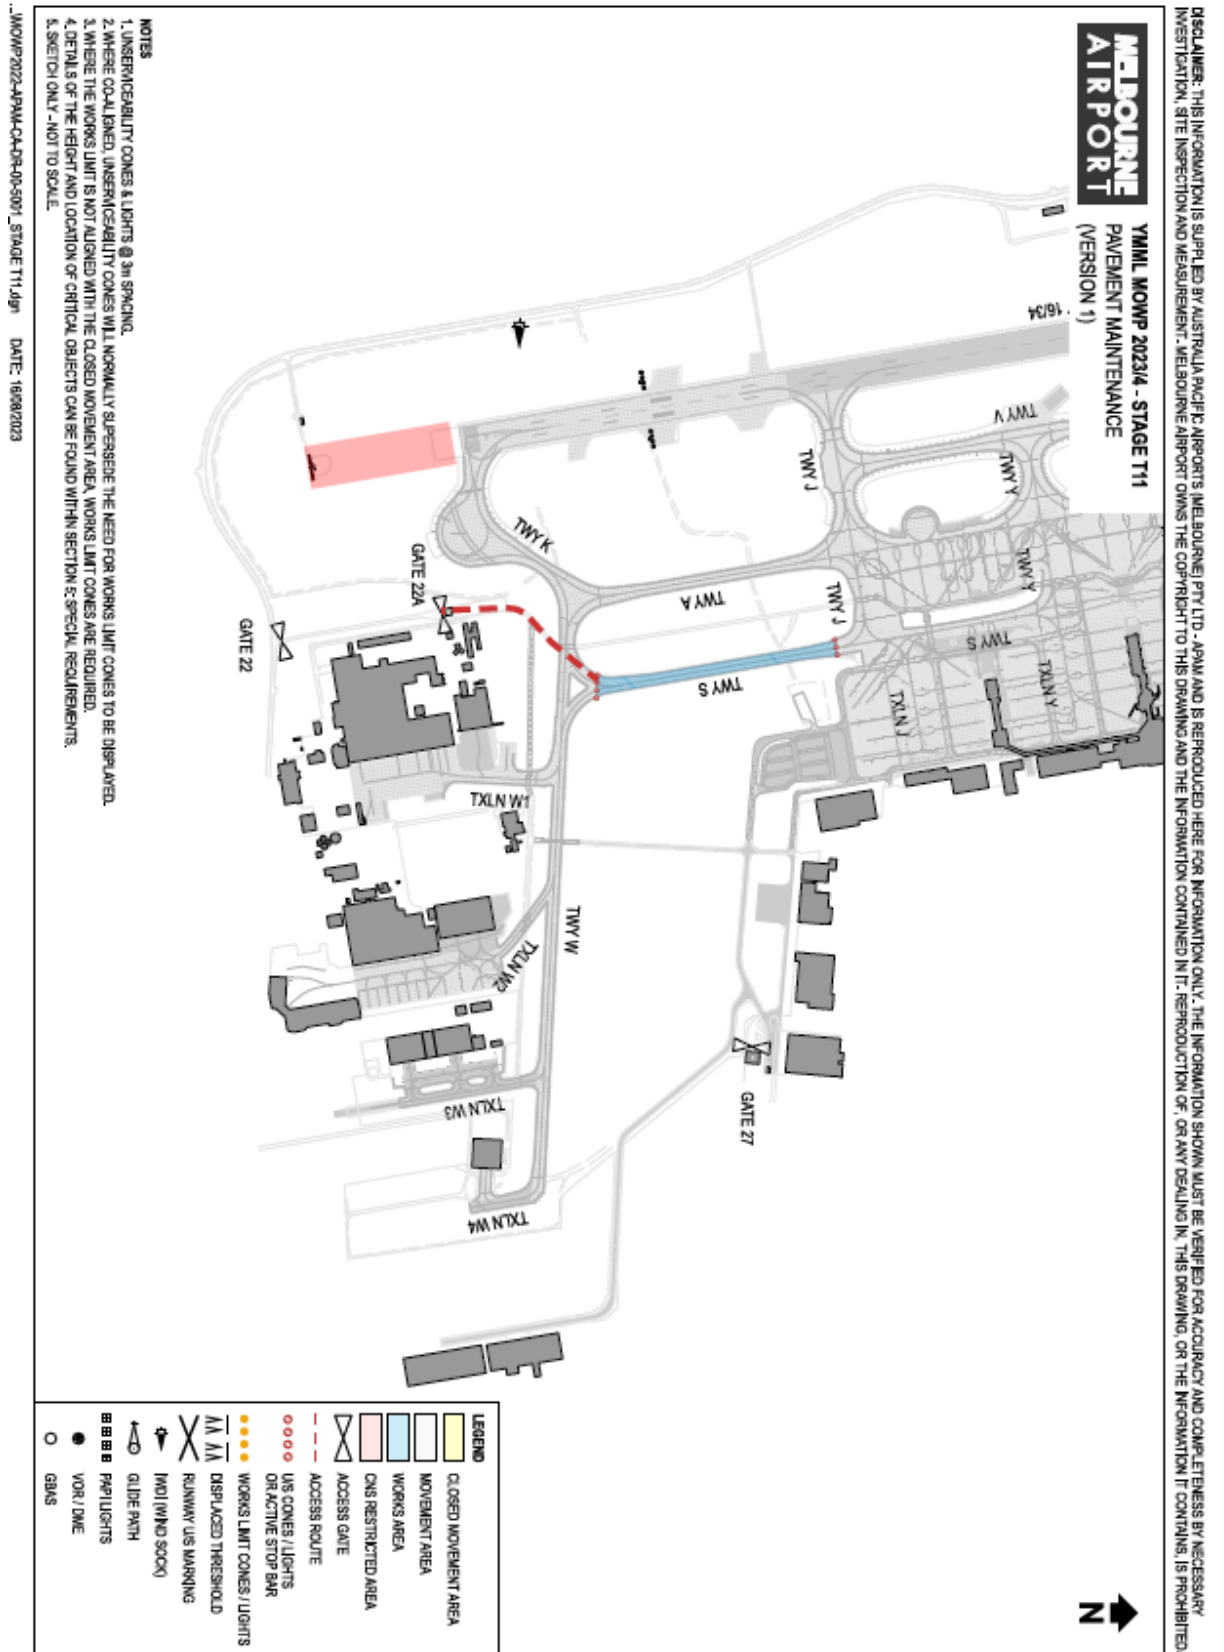


8.17. Stage T12

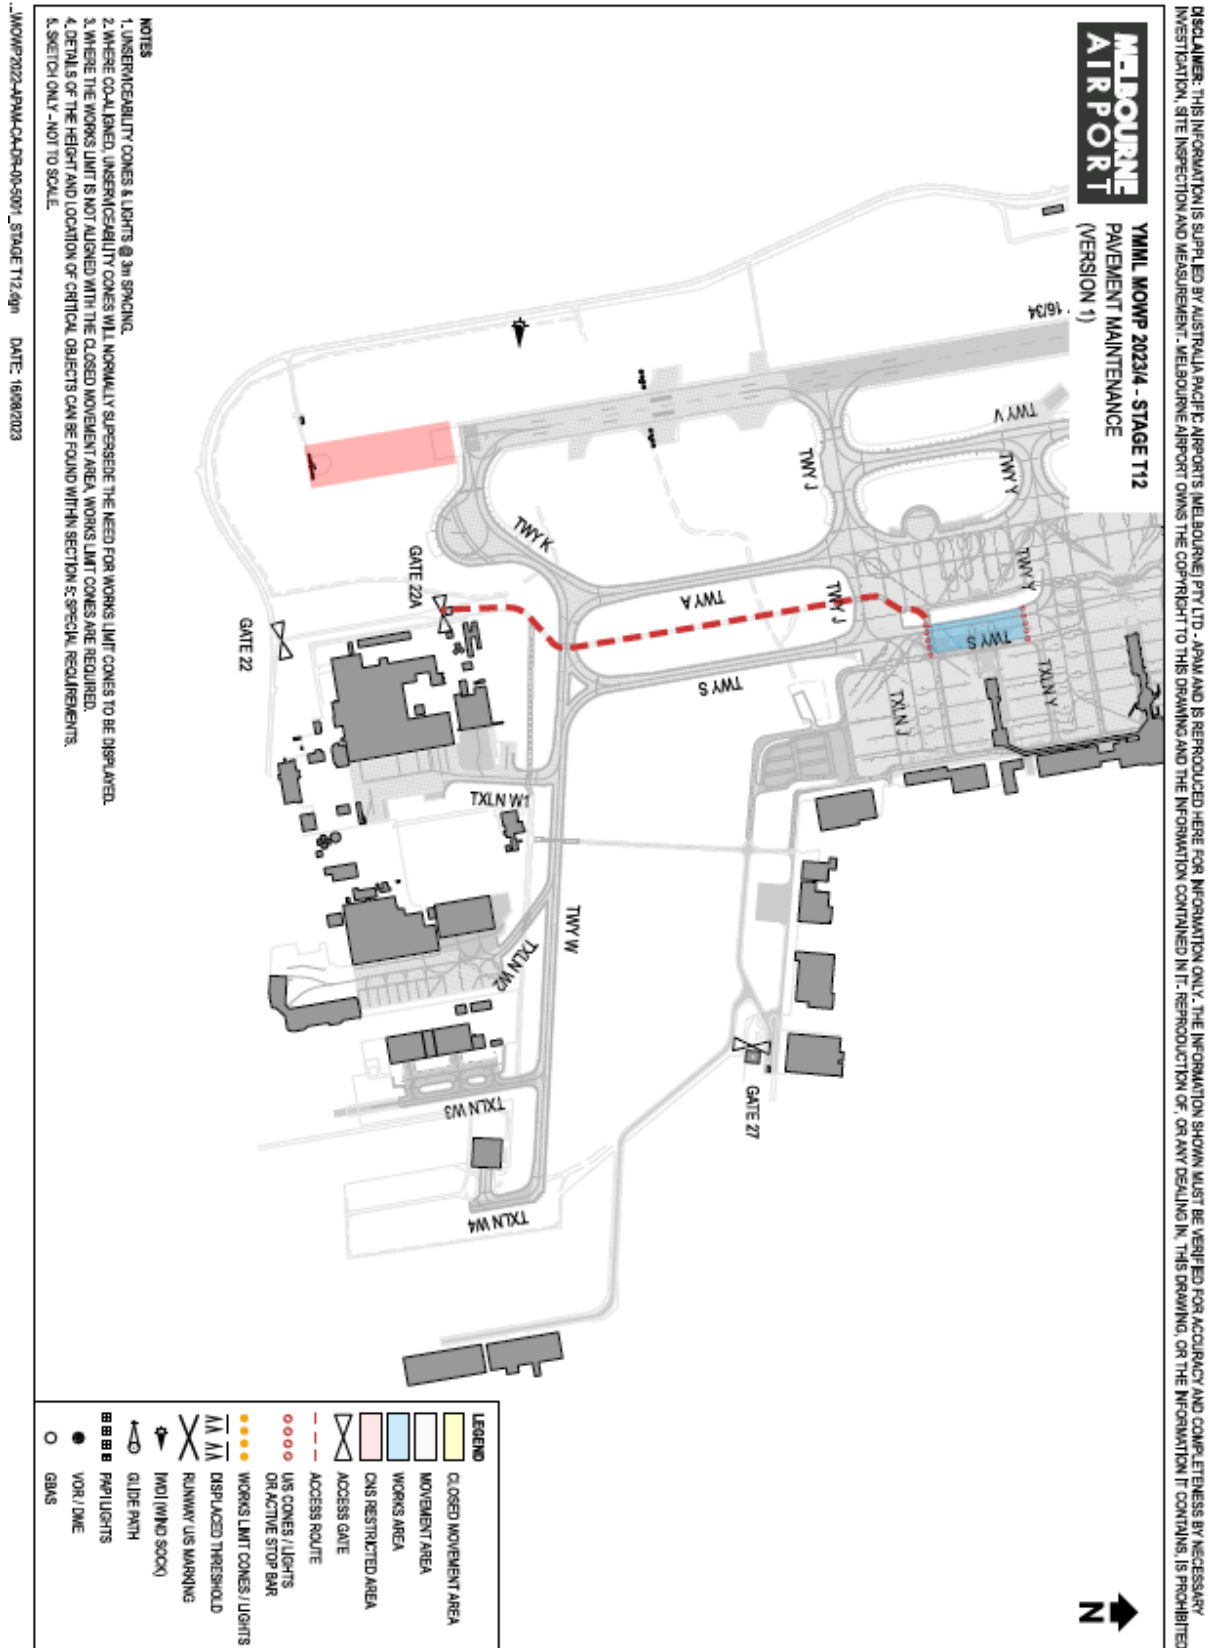


8.18. Stage T13

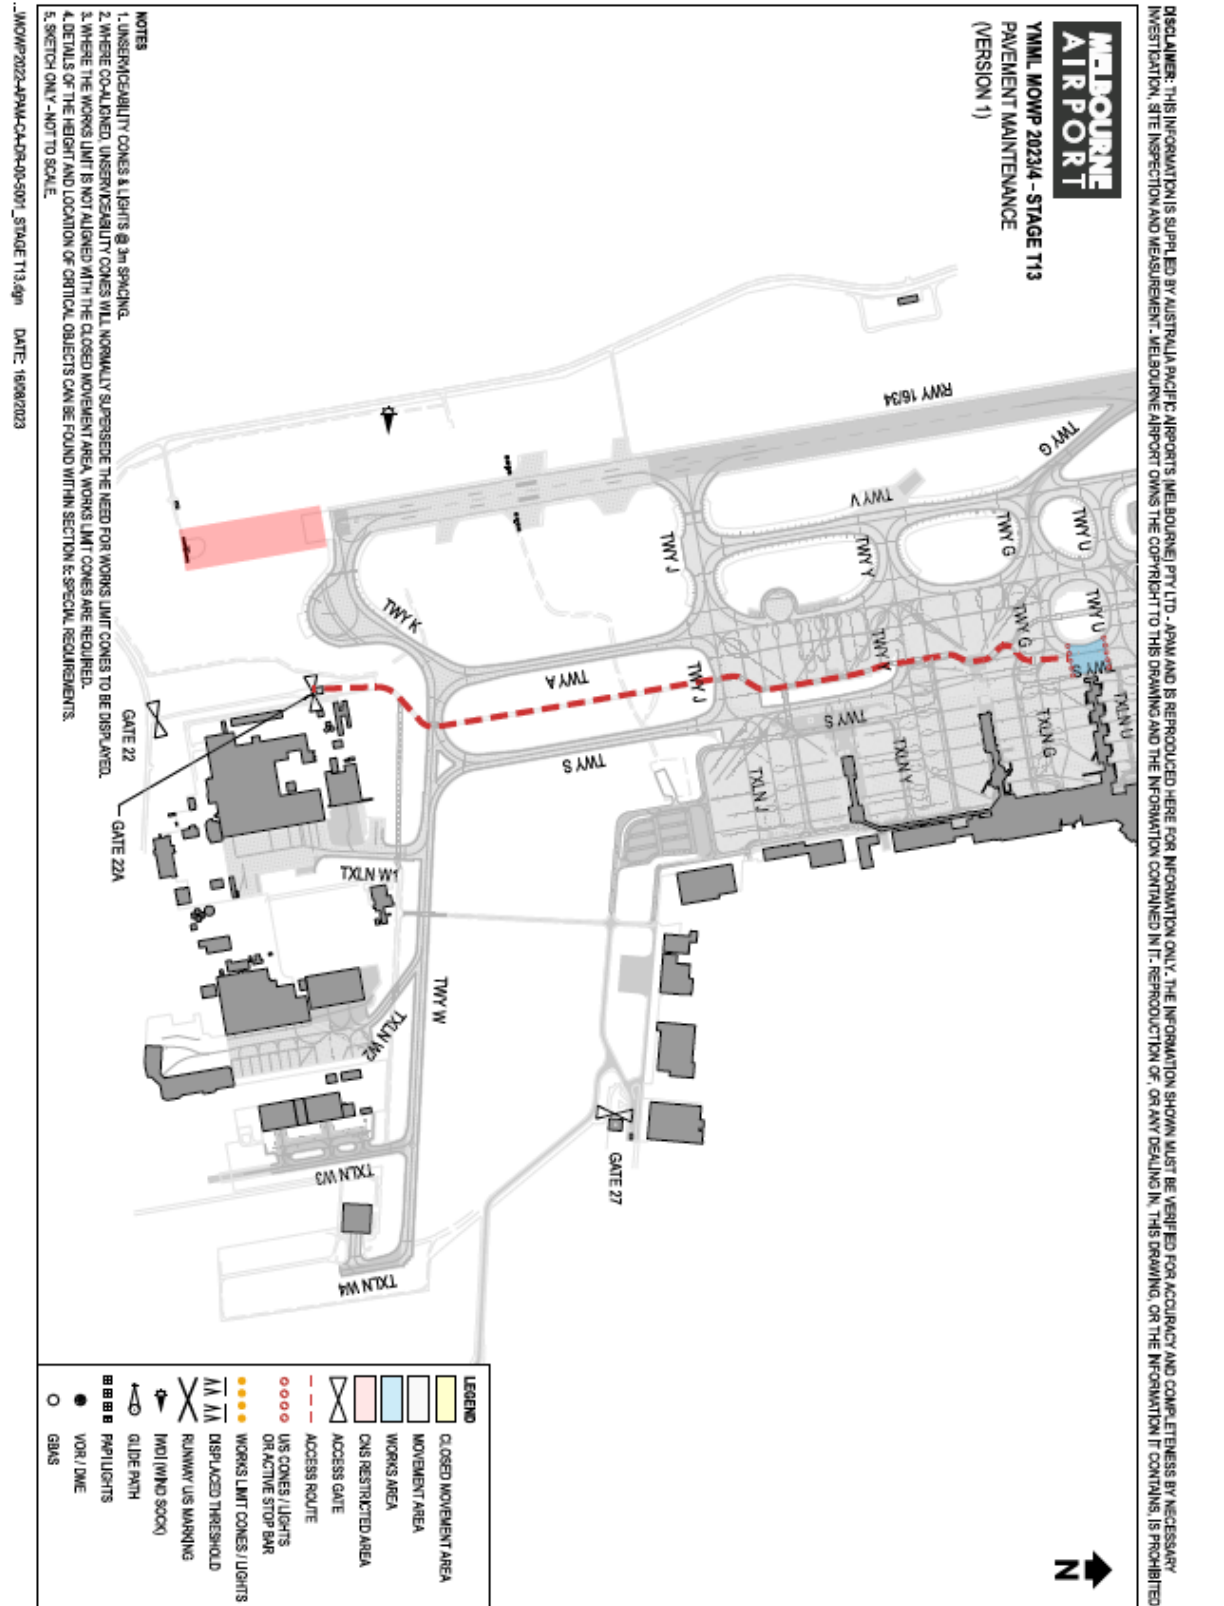


8.19. Stage T14

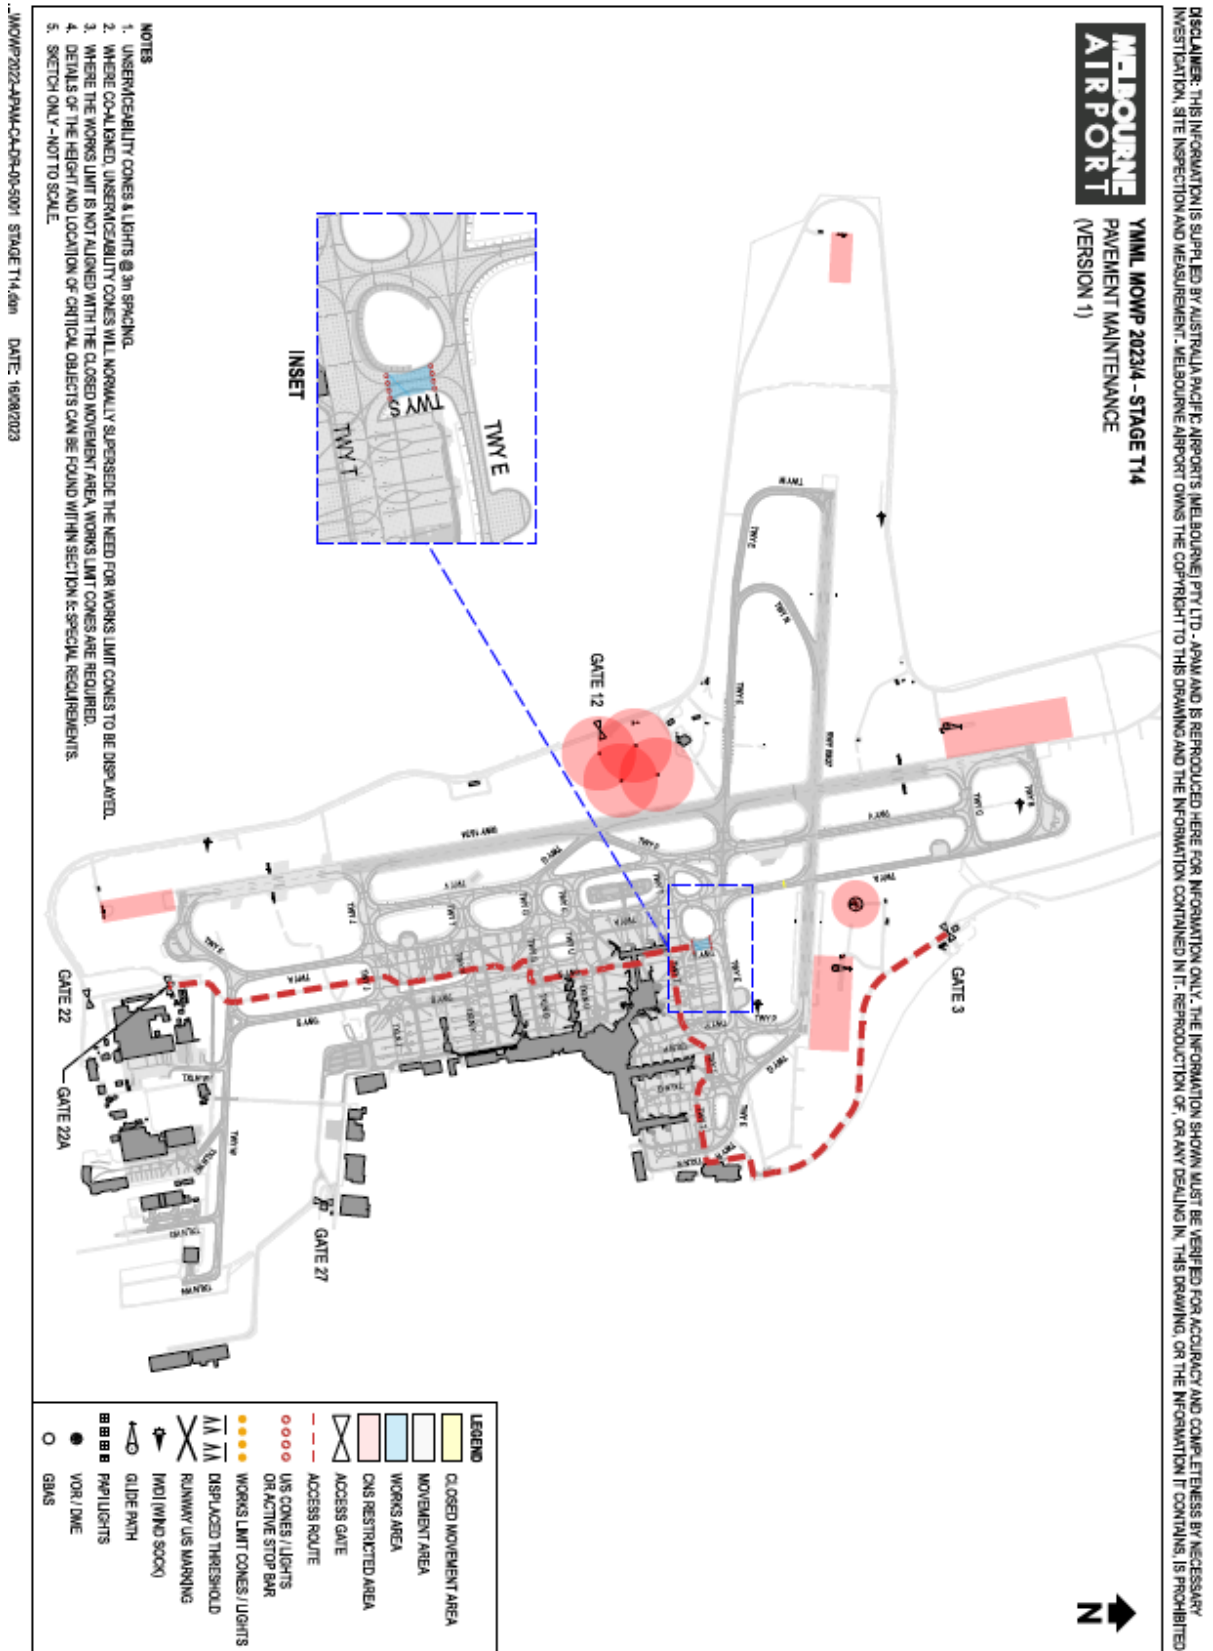

8.20. Stage T15

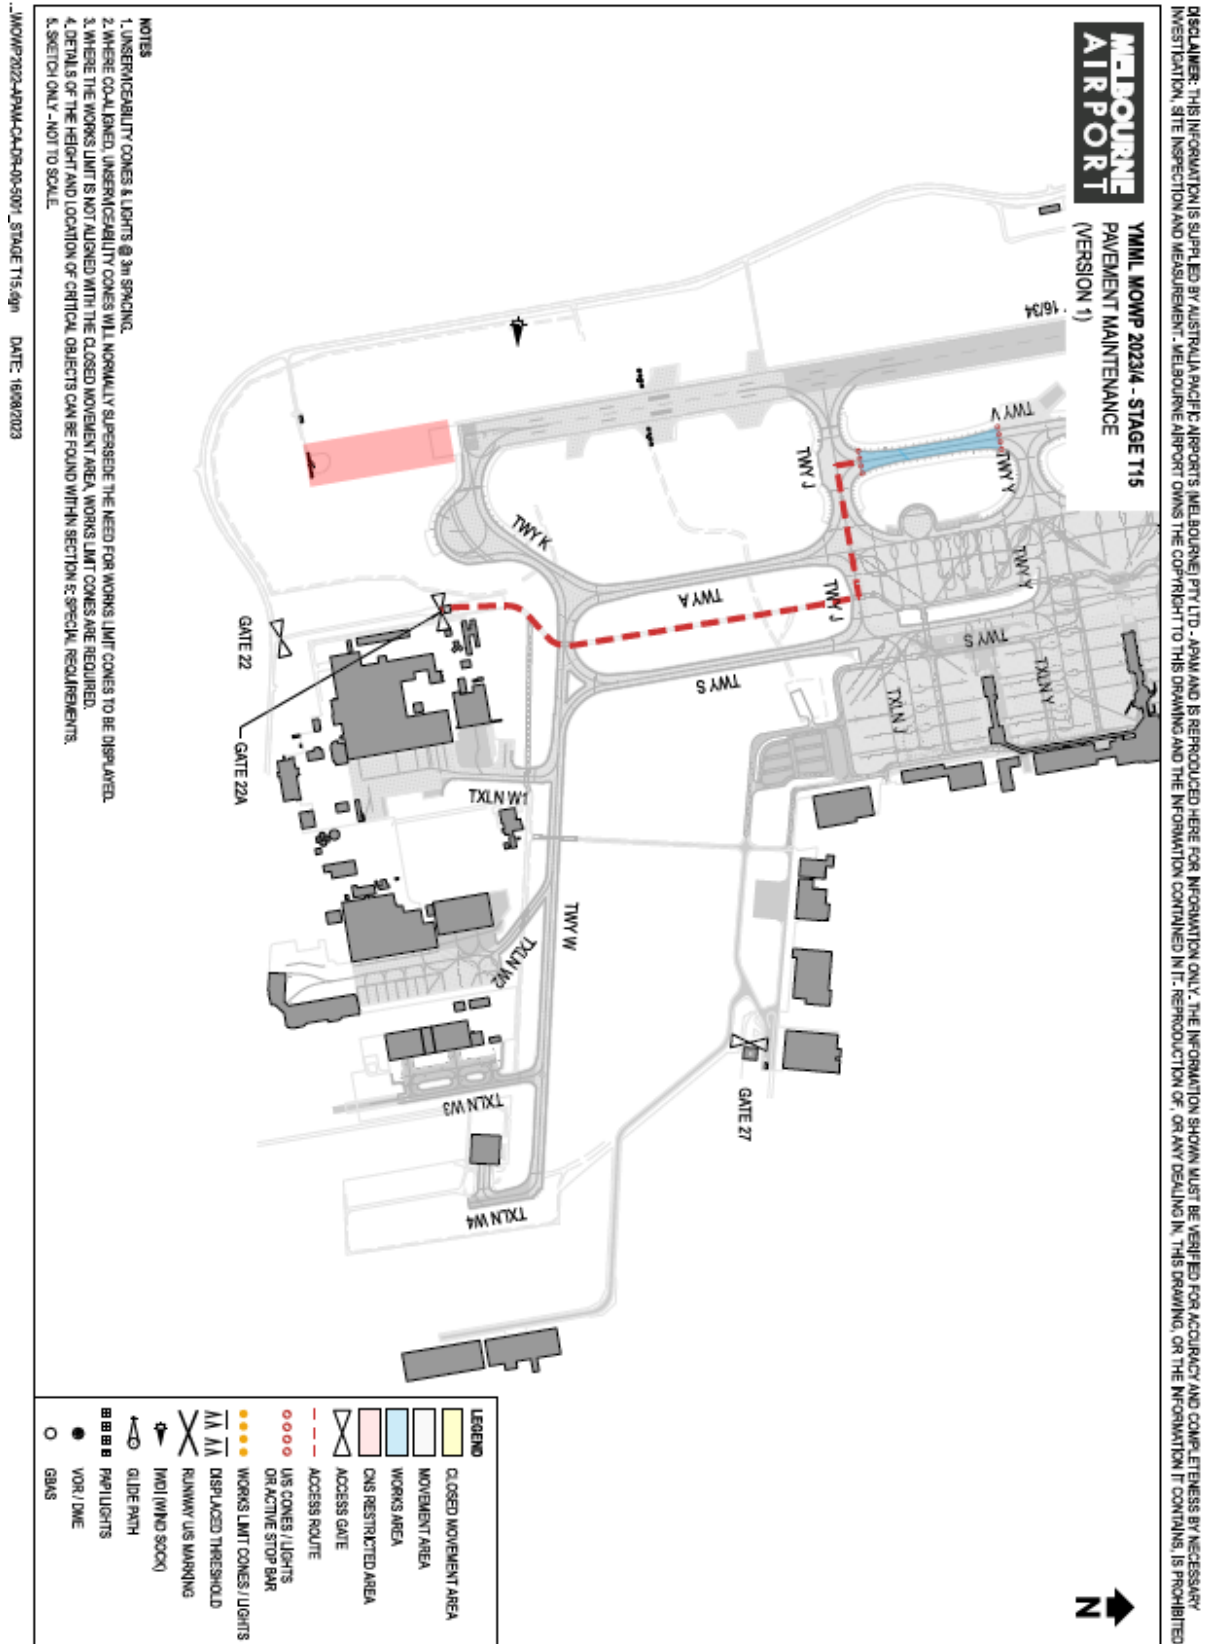


8.21. Stage T16

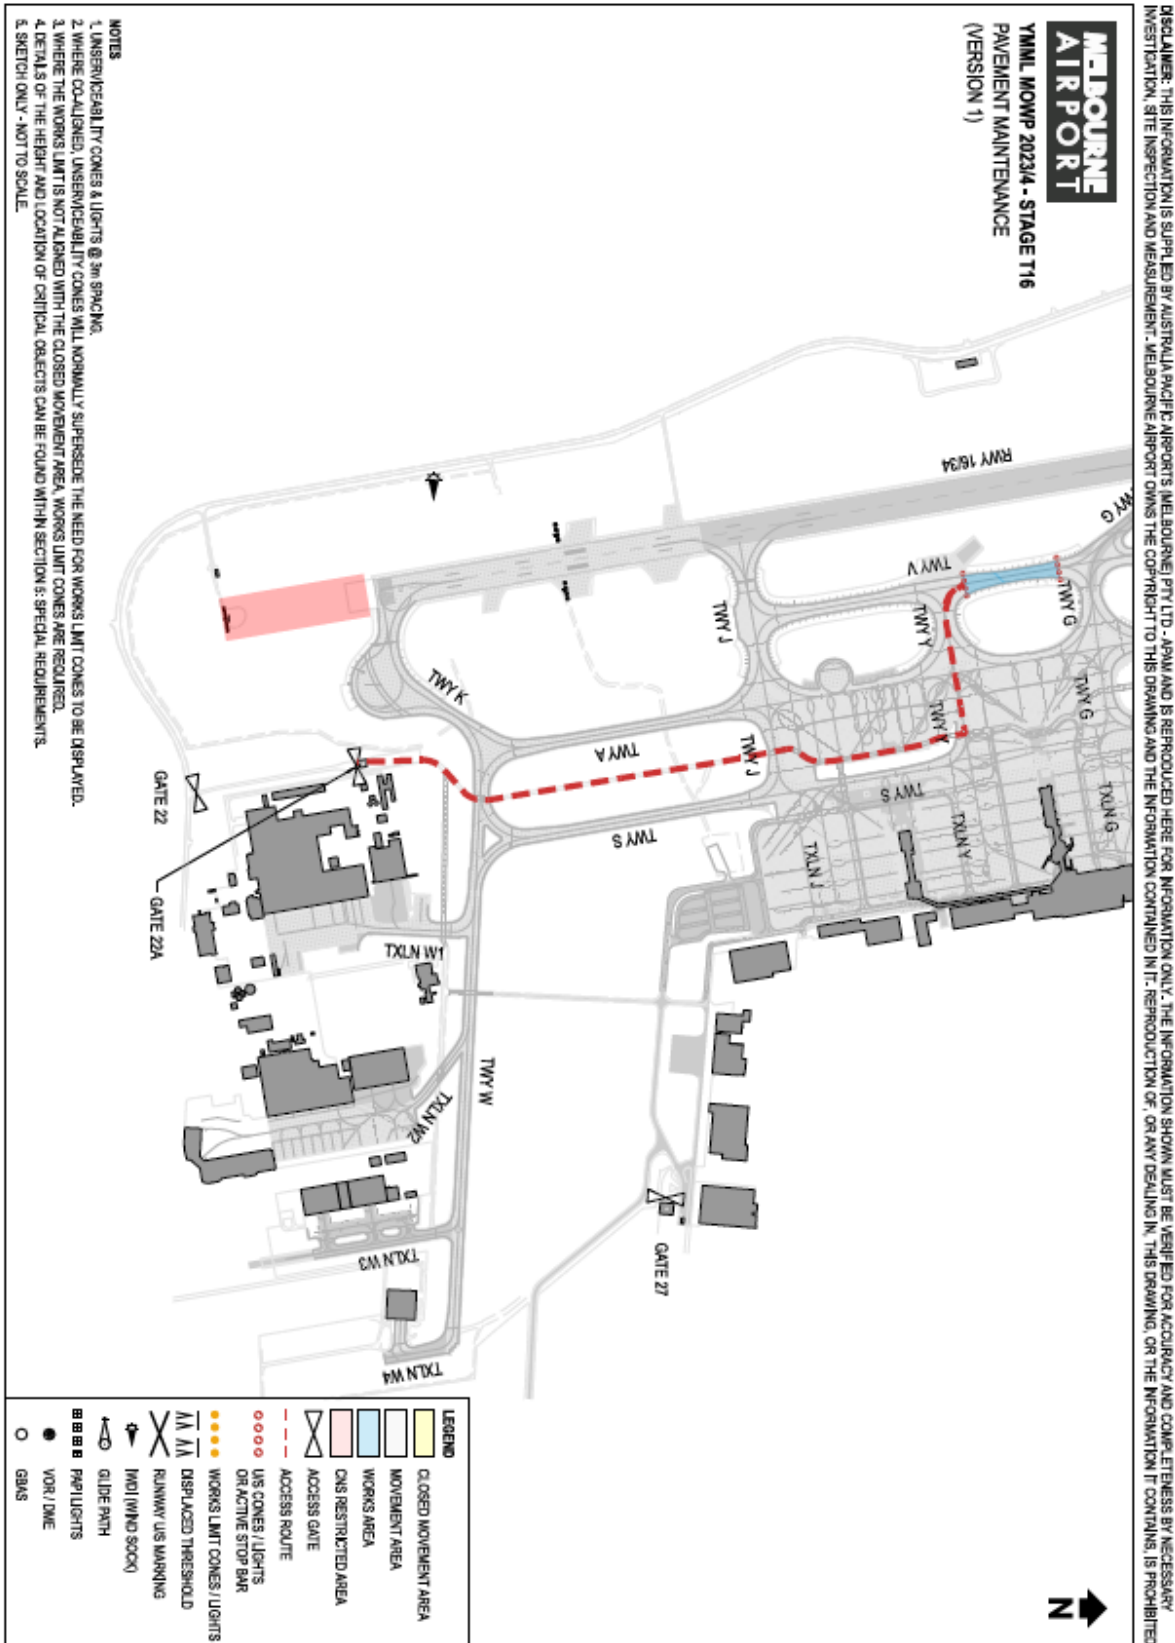


8.22. Stage T17




8.23. Stage T18

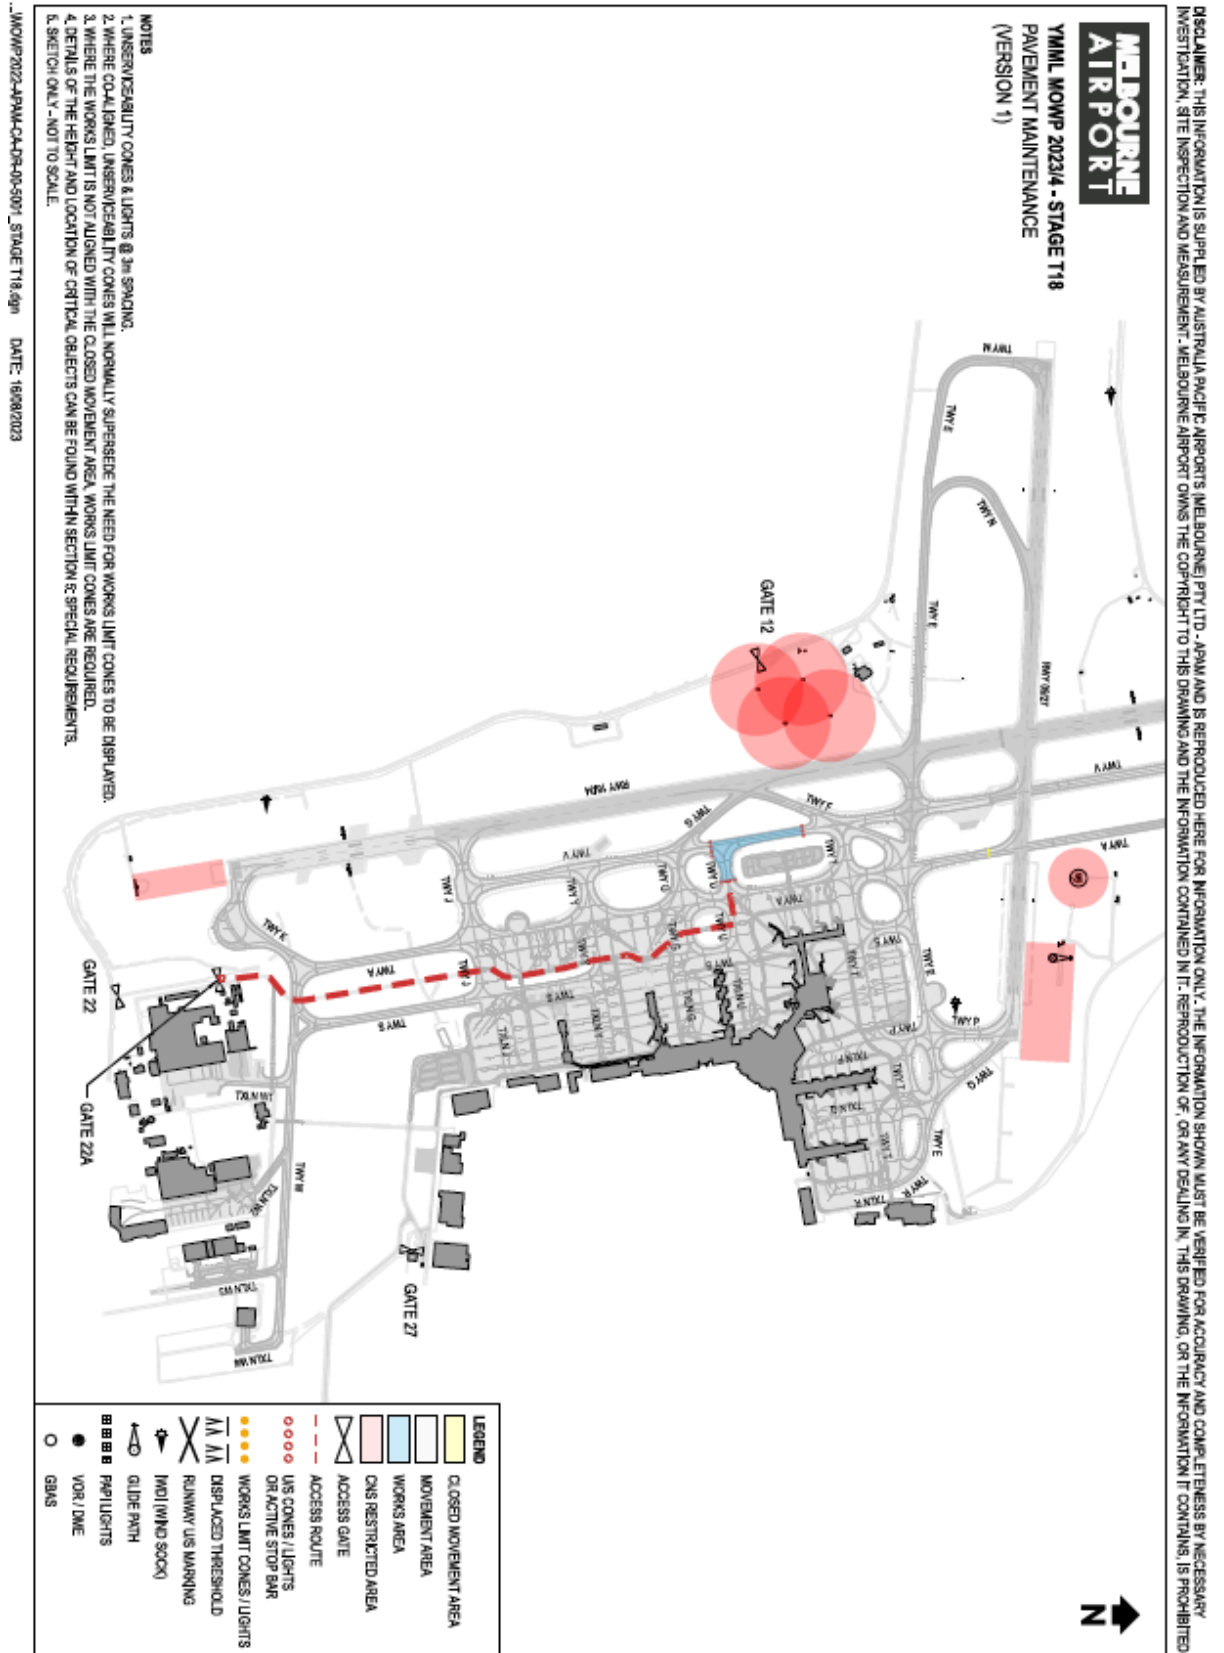


8.24. Stage T19

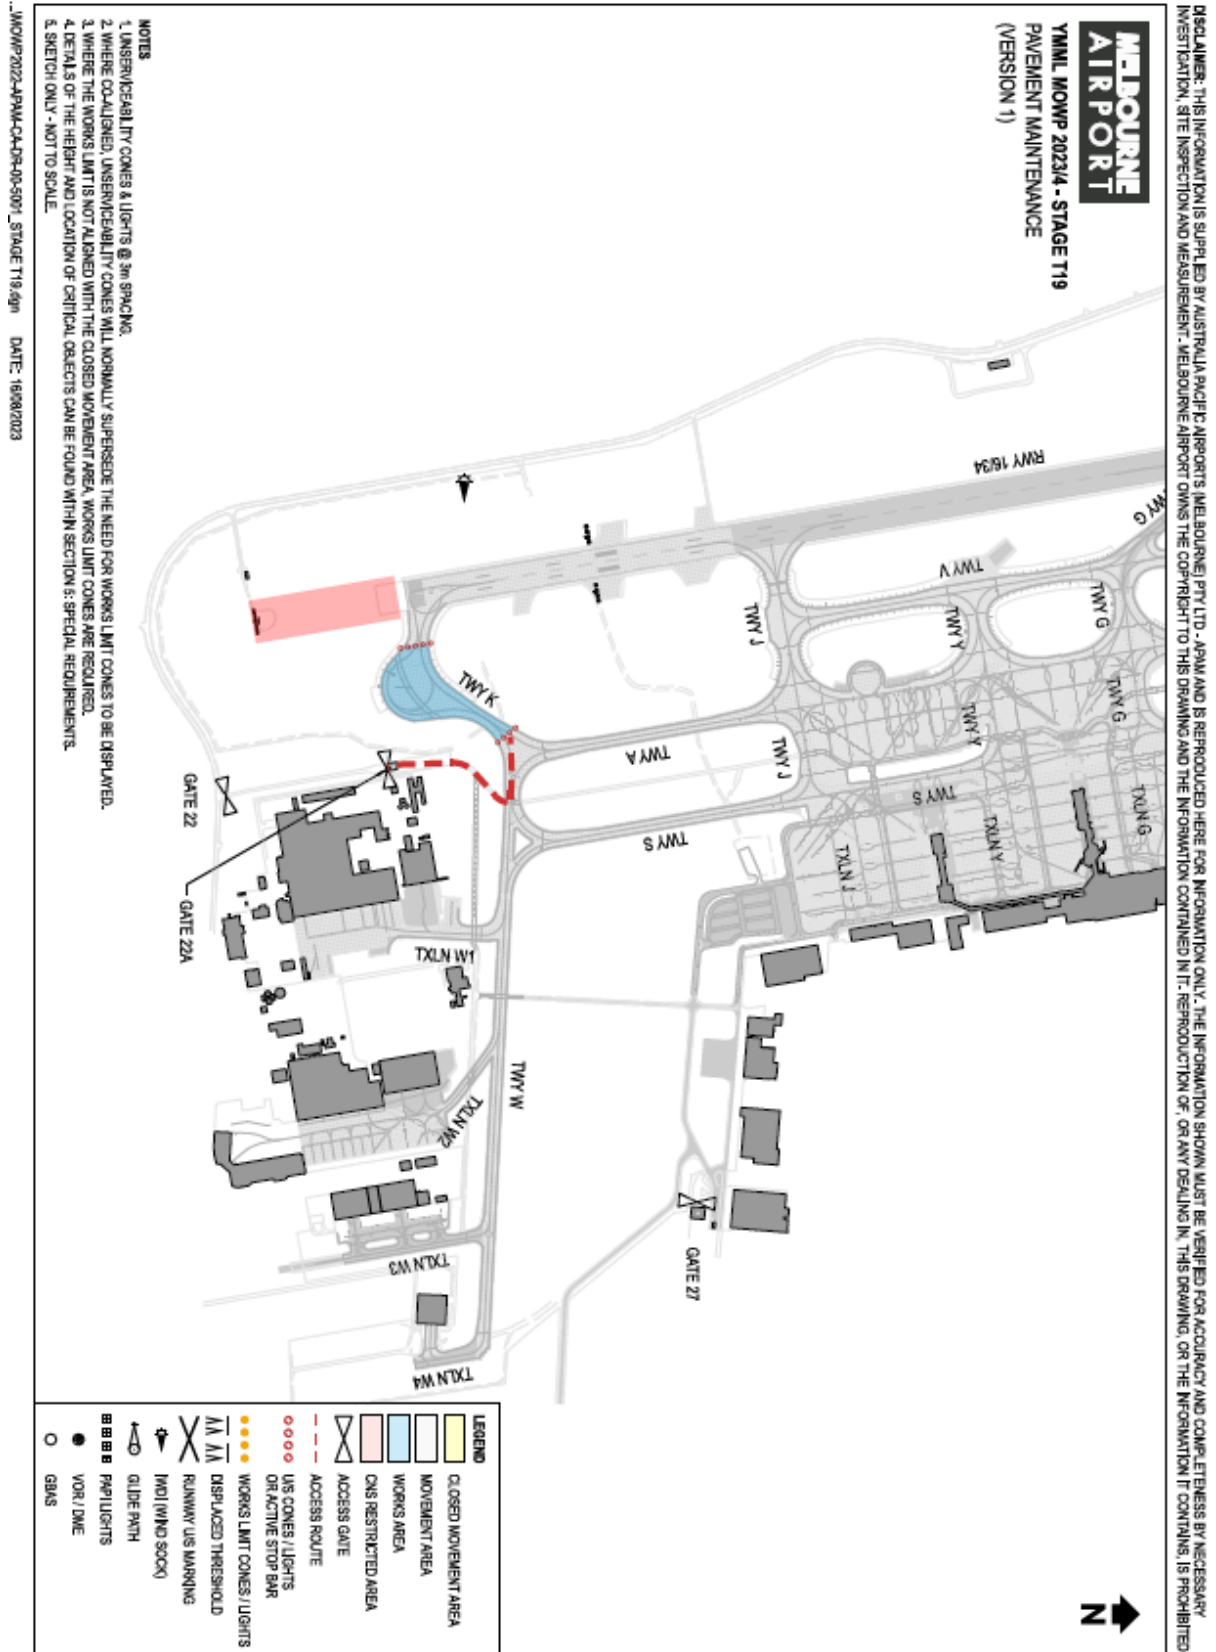


8.25. Stage T20

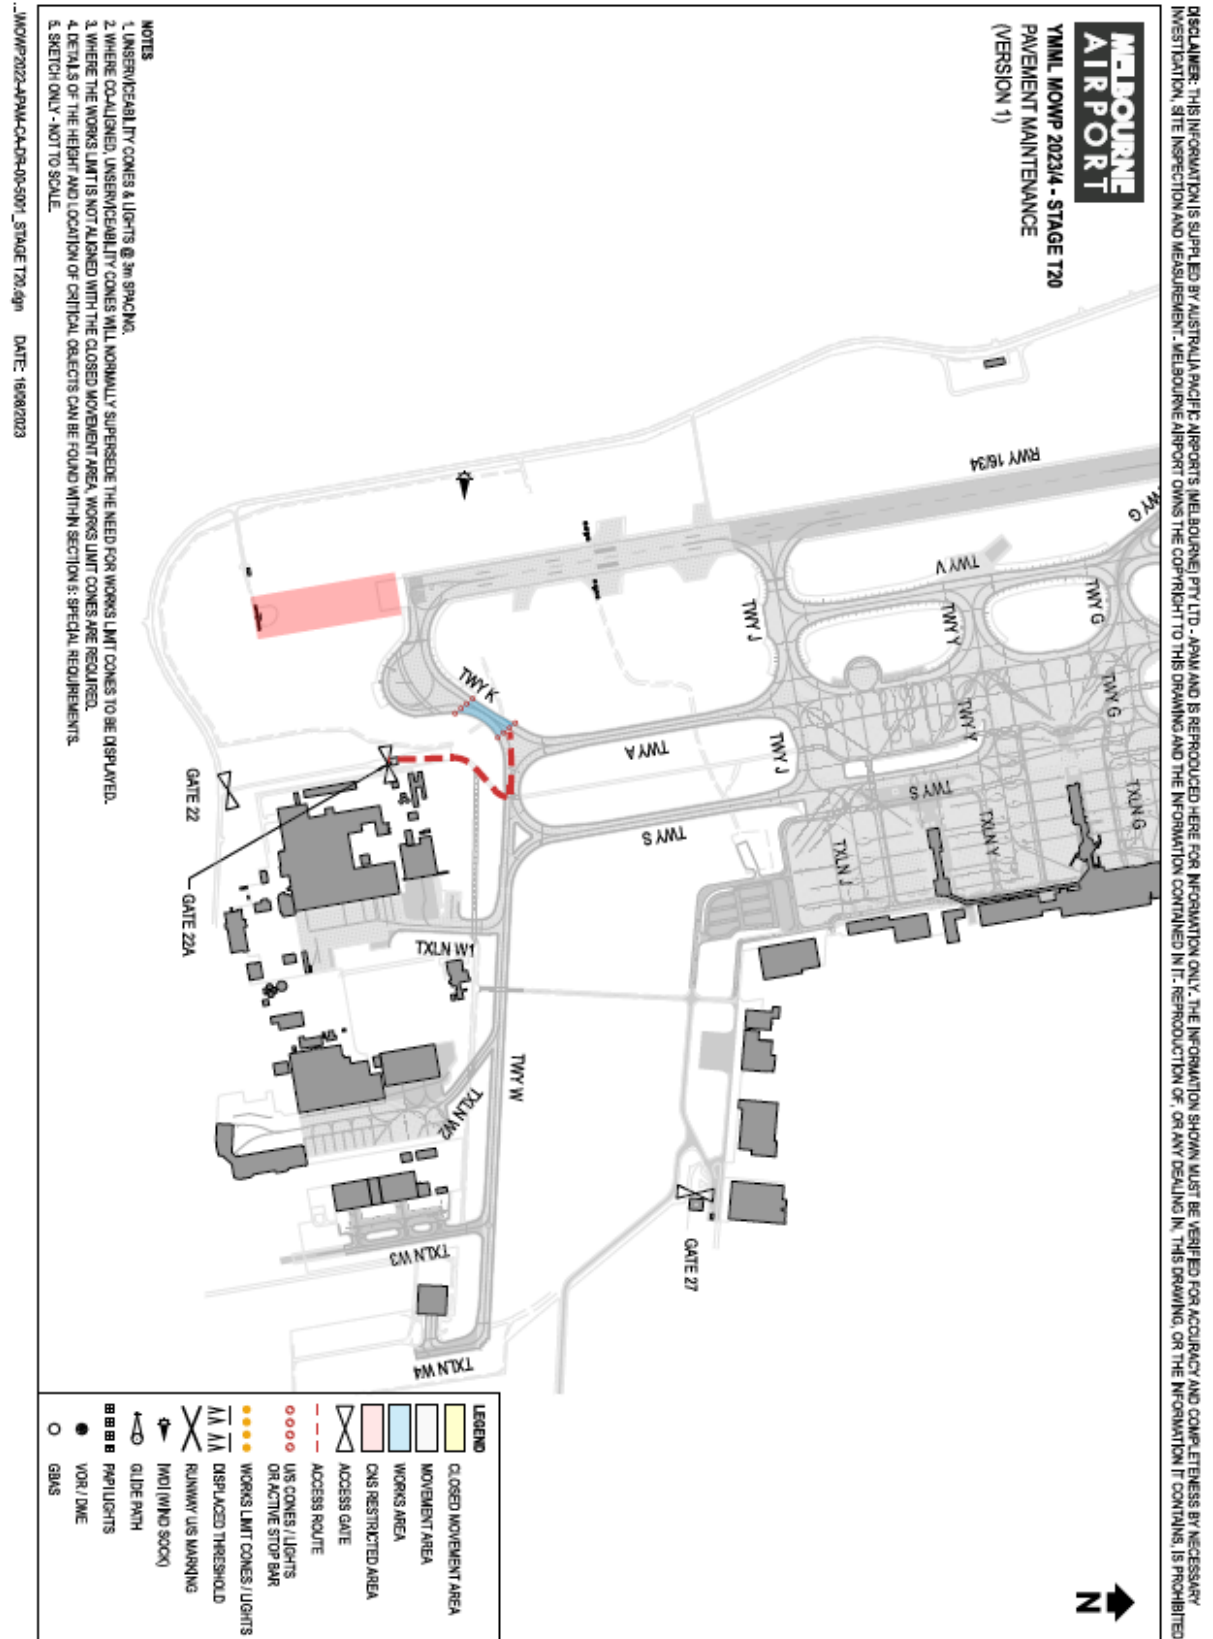


8.26. Stage T21

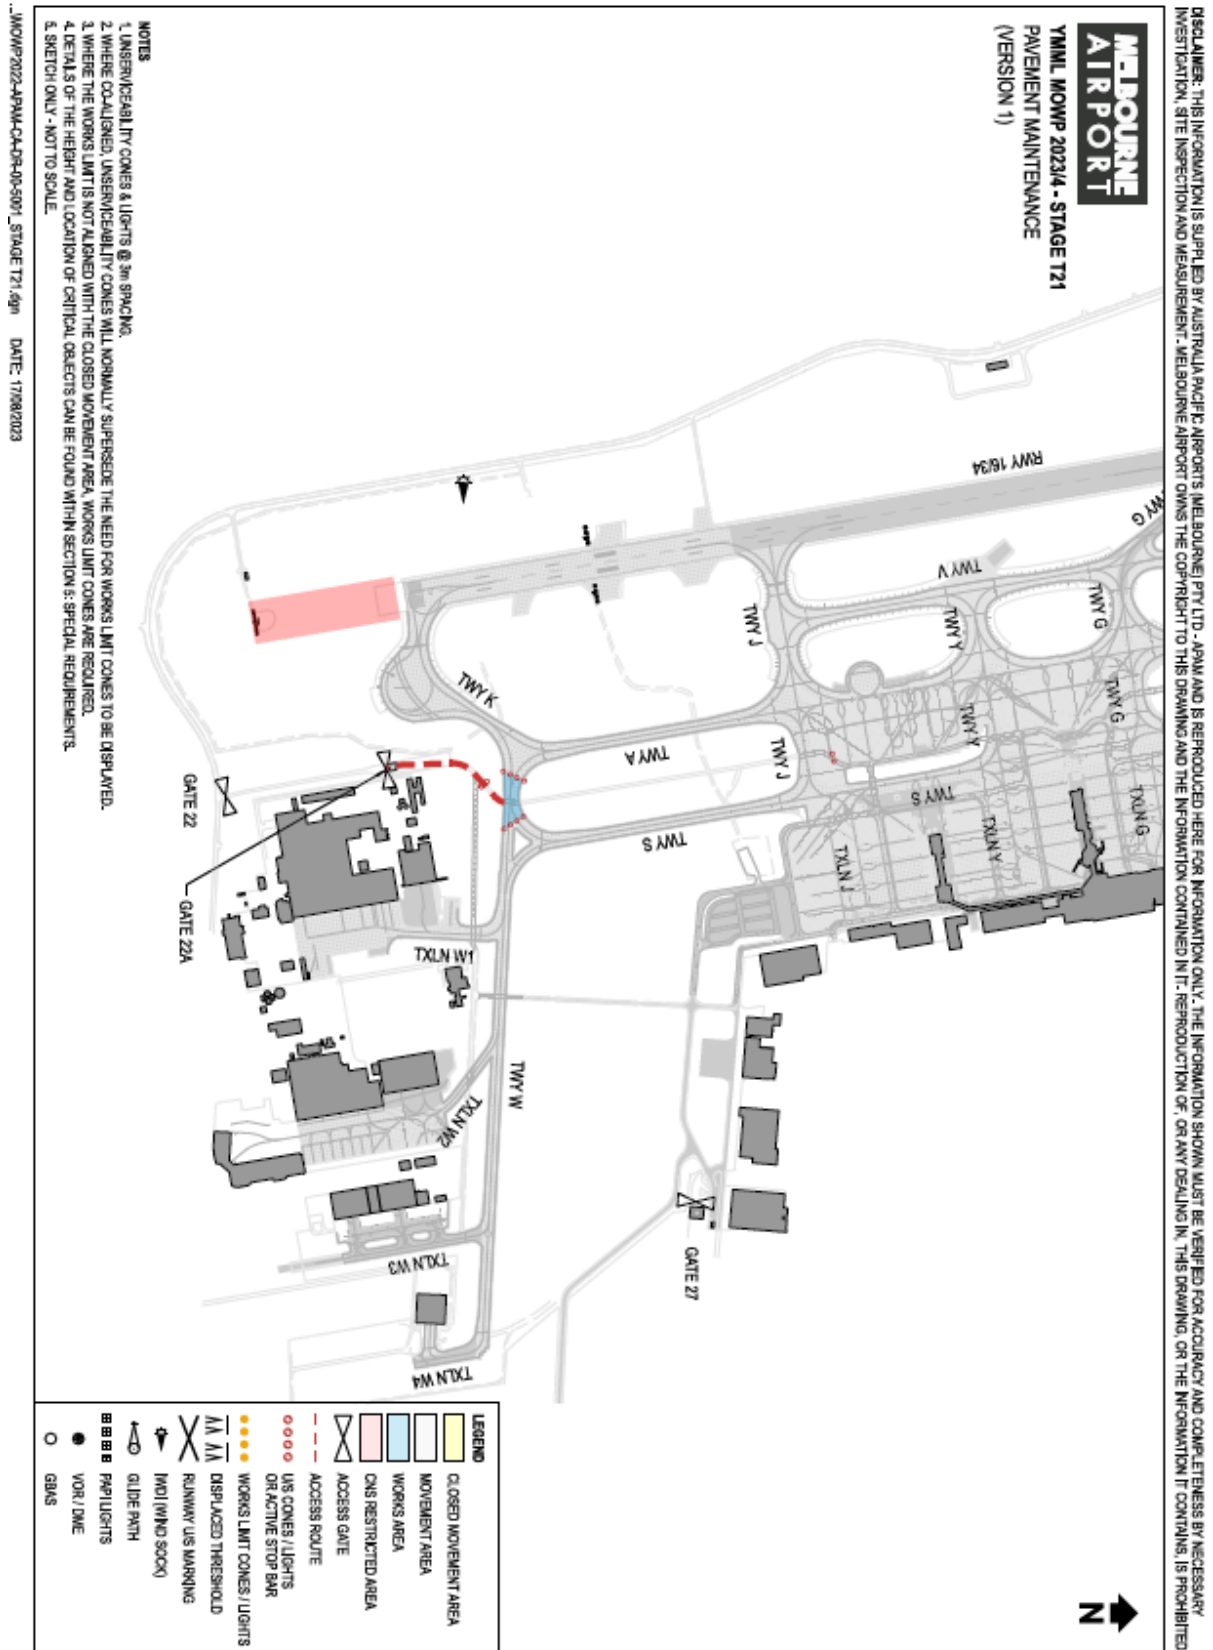


8.27. Stage T22

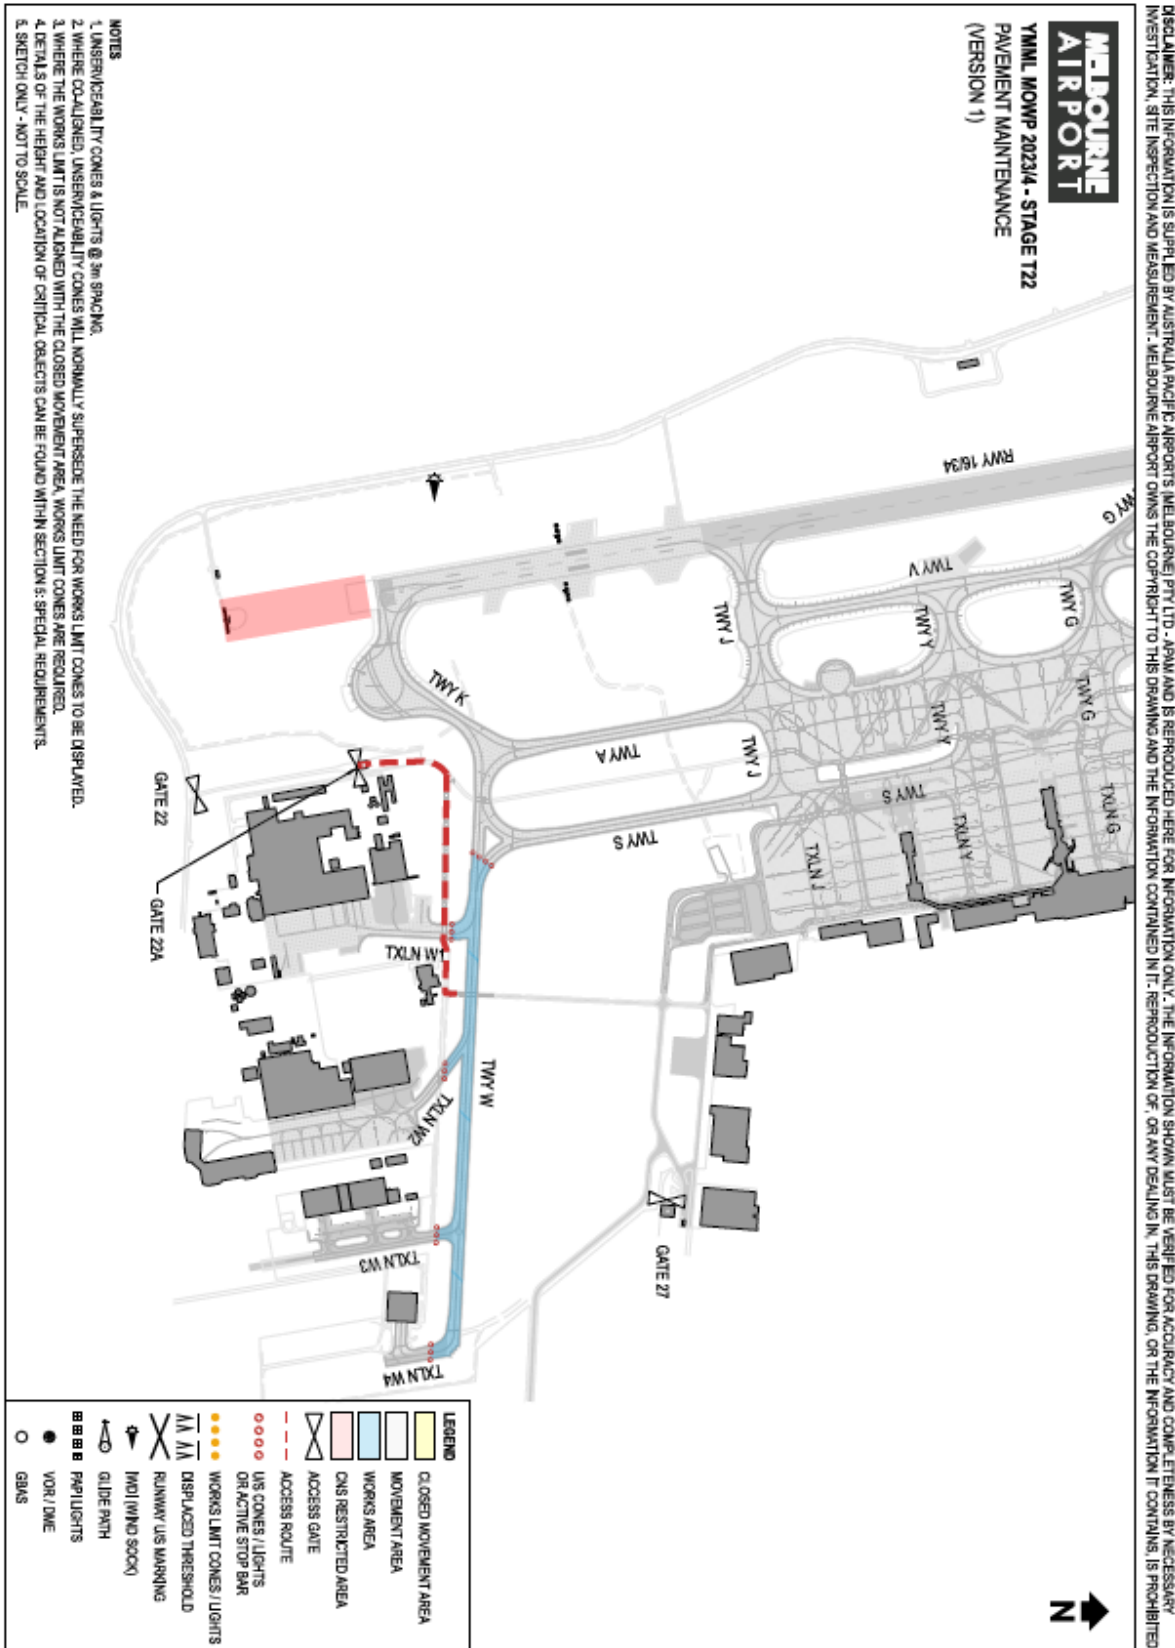


8.28. Stage T23

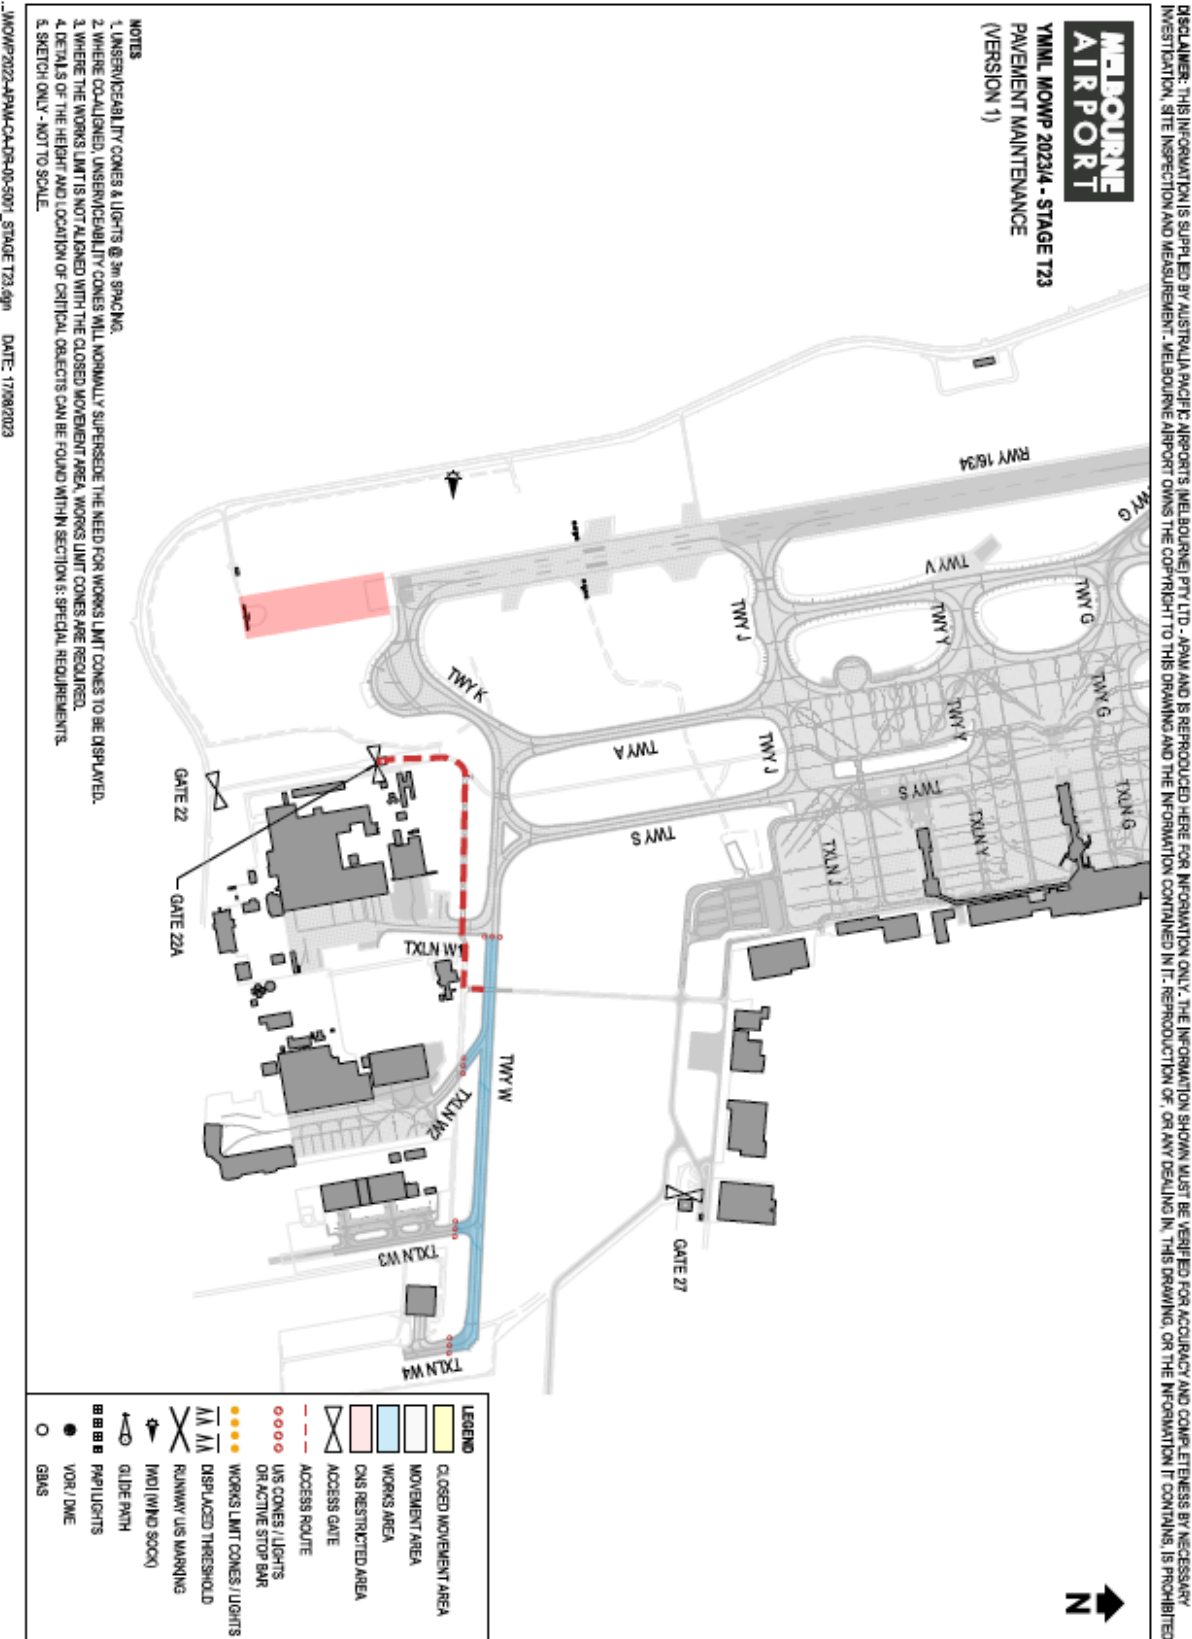


8.29. Stage T24

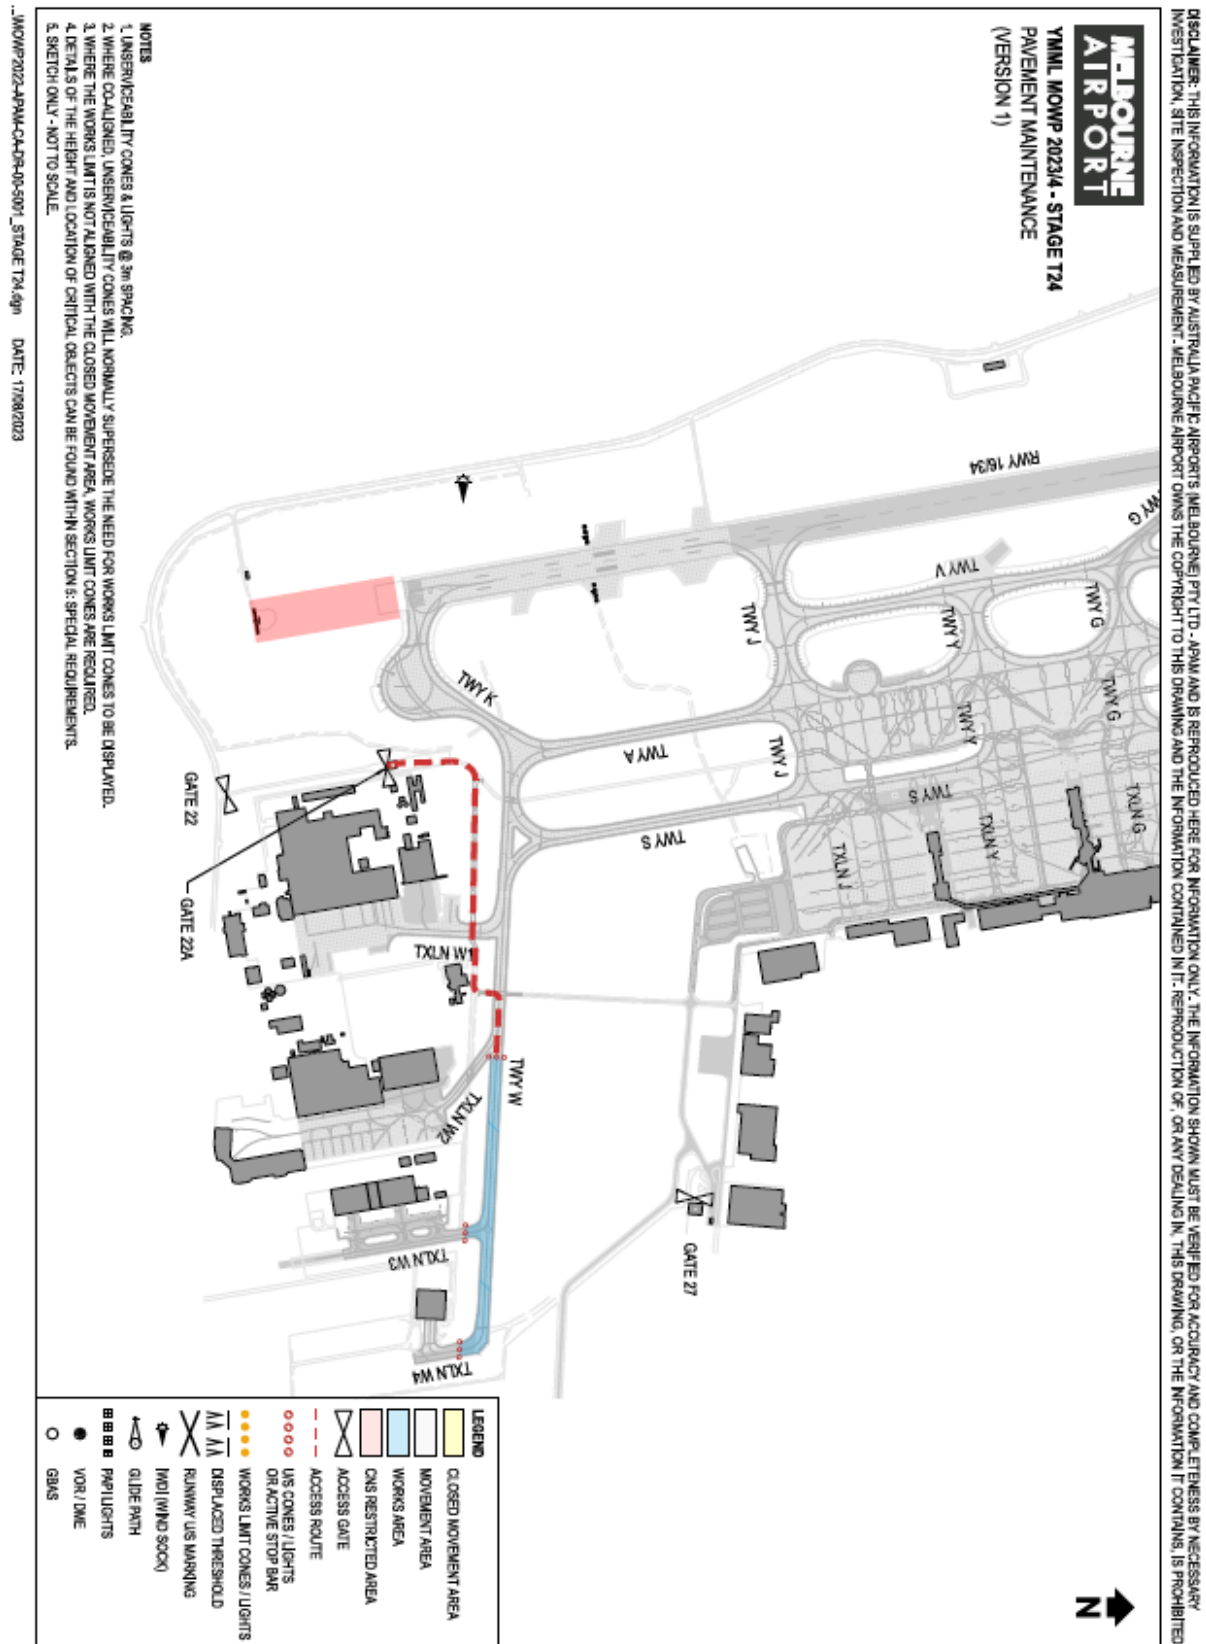


8.30. Stage T25

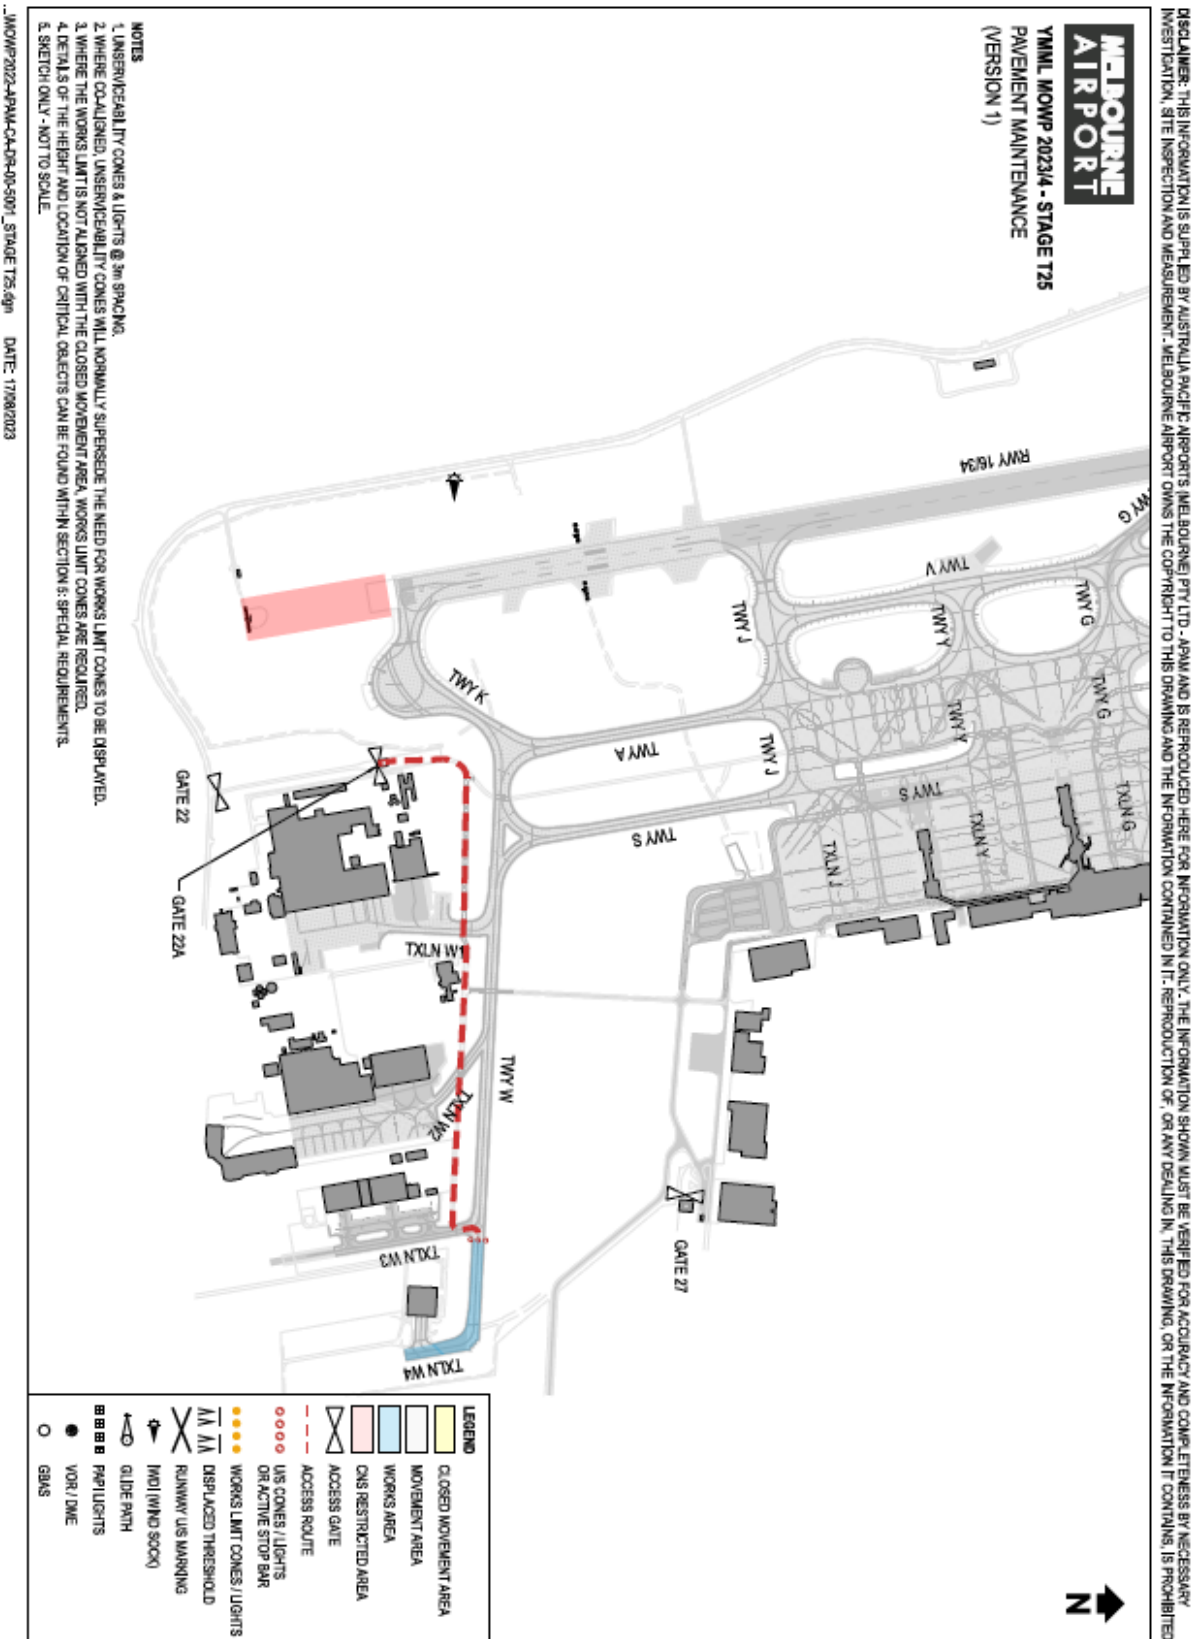


8.31. Stage T26

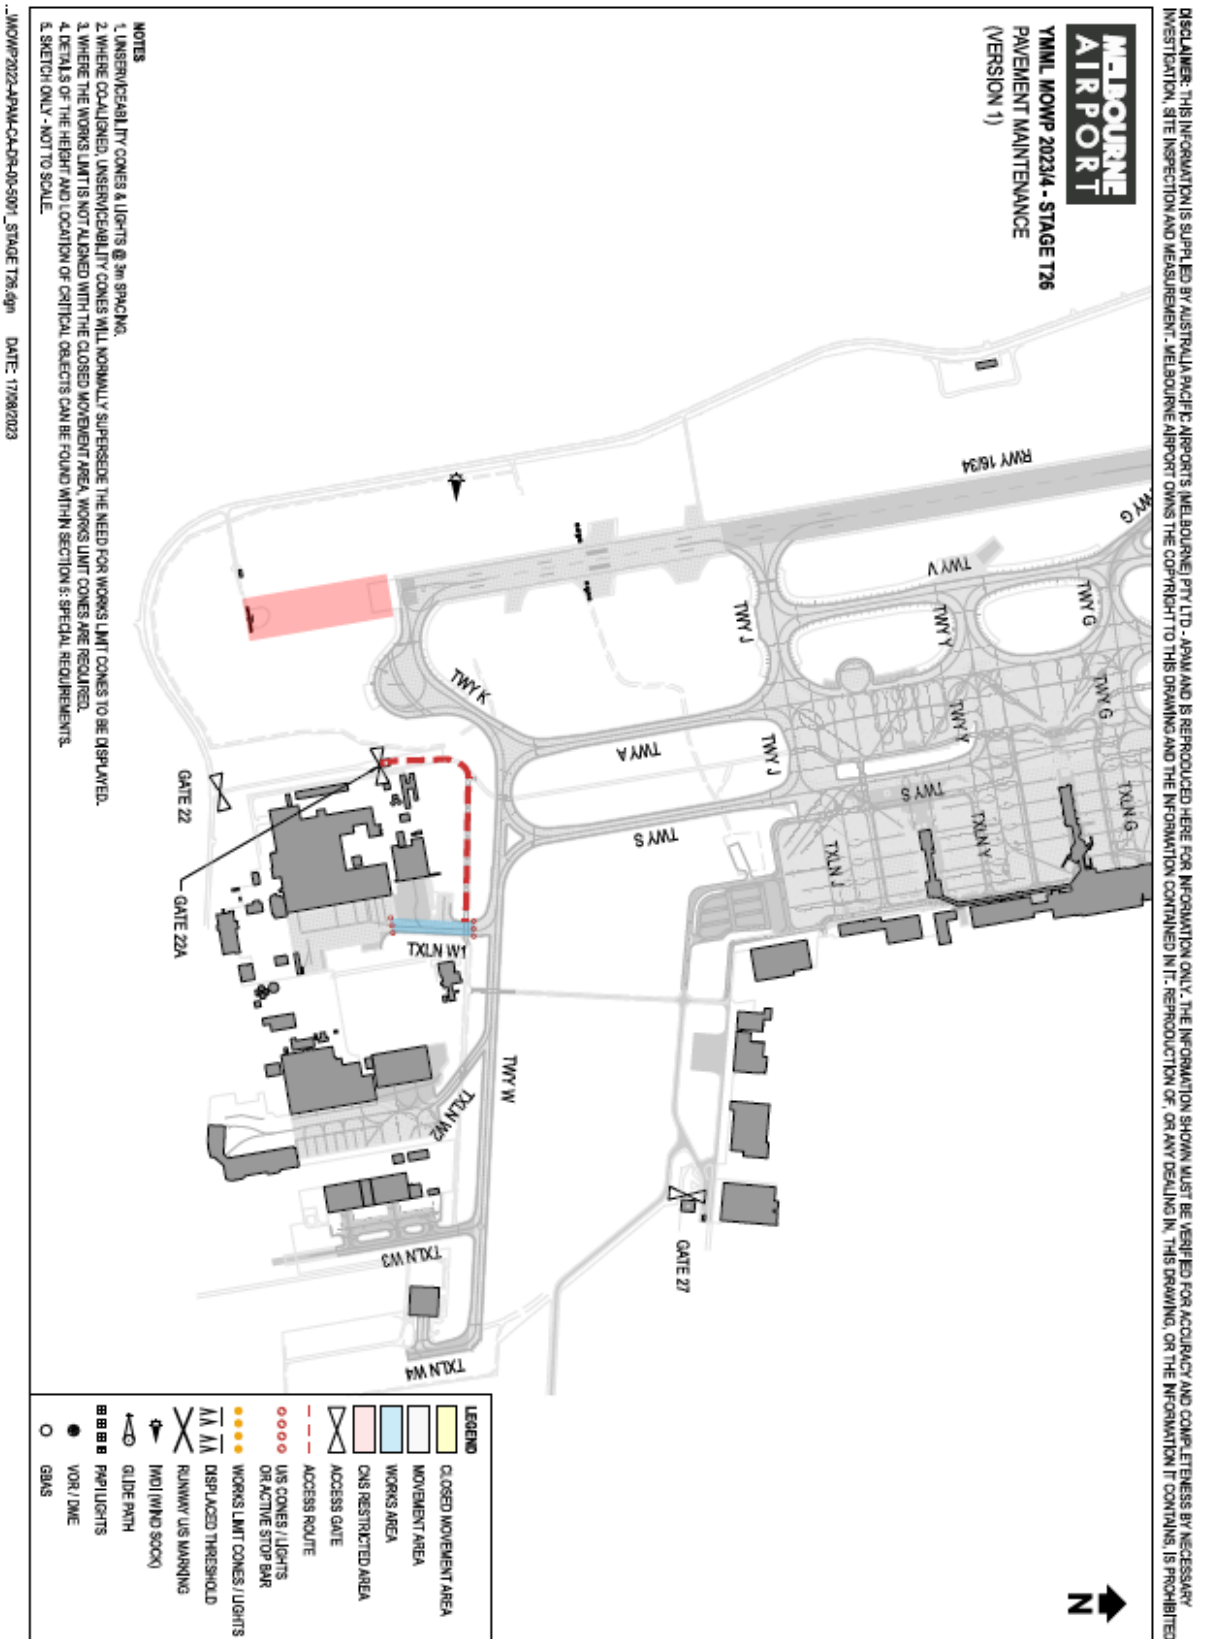


8.32. Stage T27

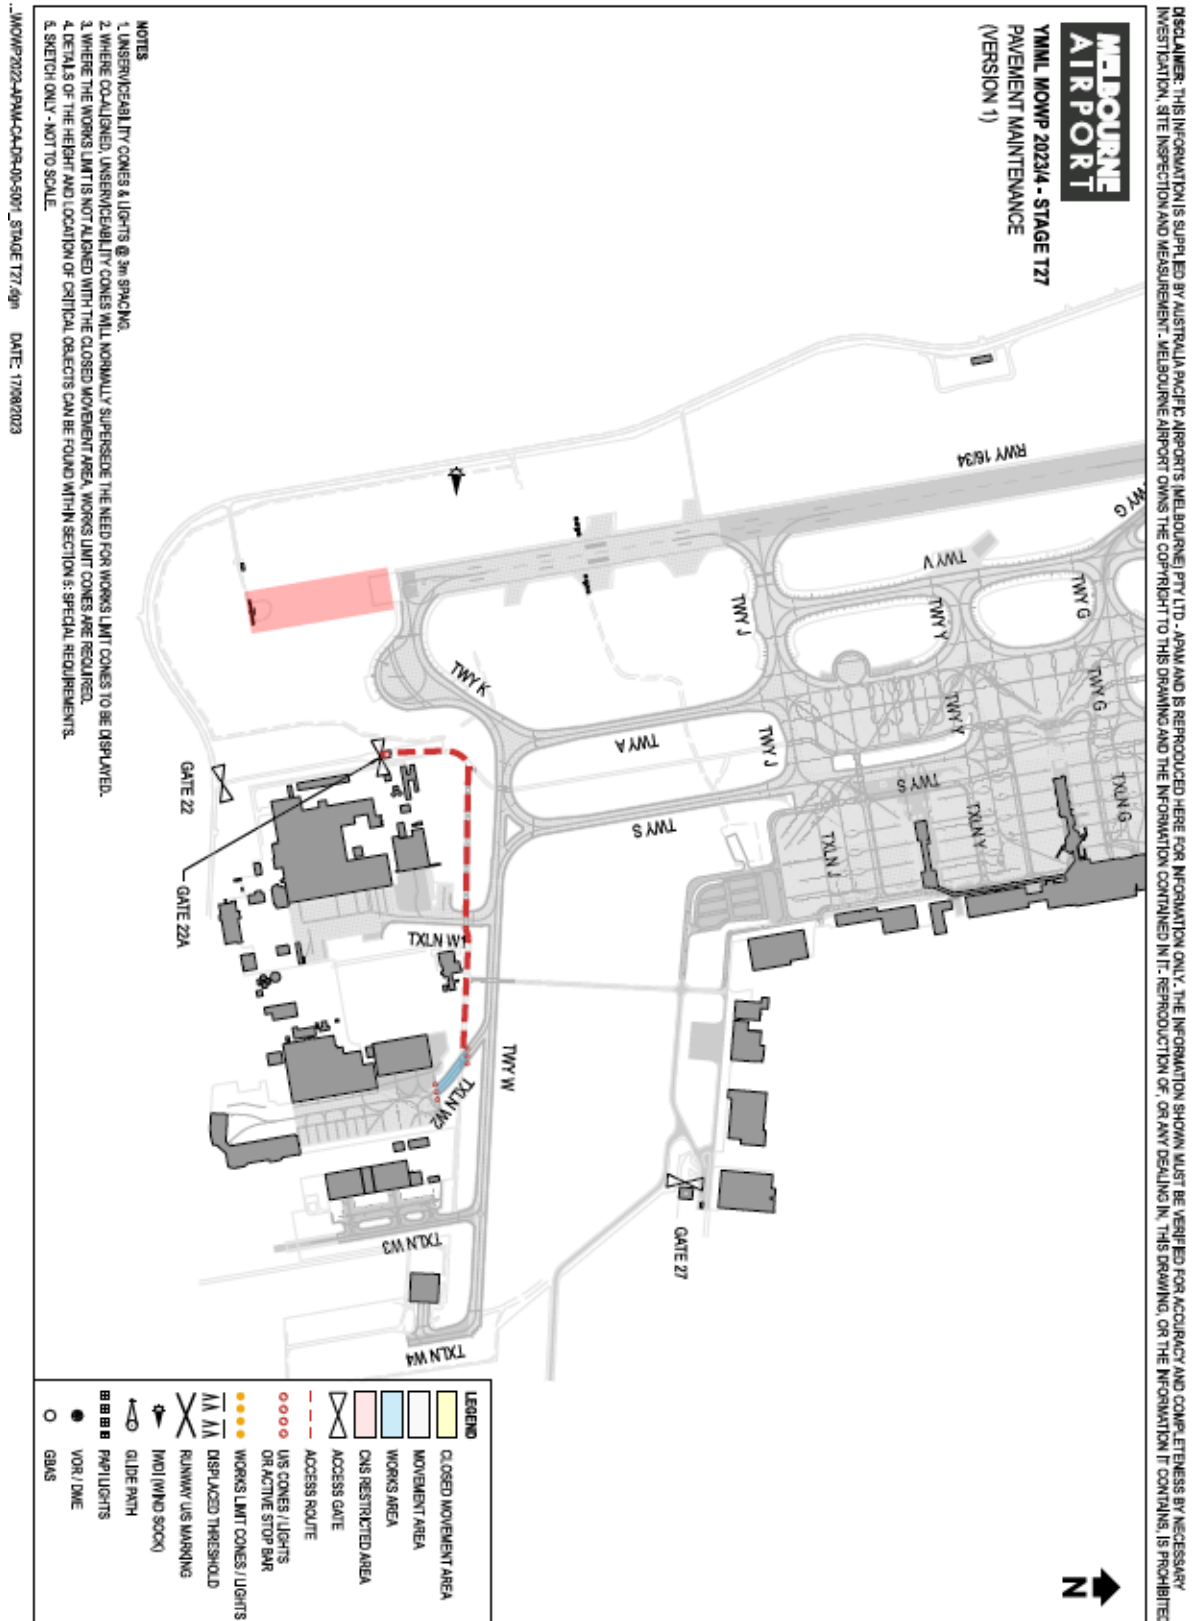


8.33. Stage T28

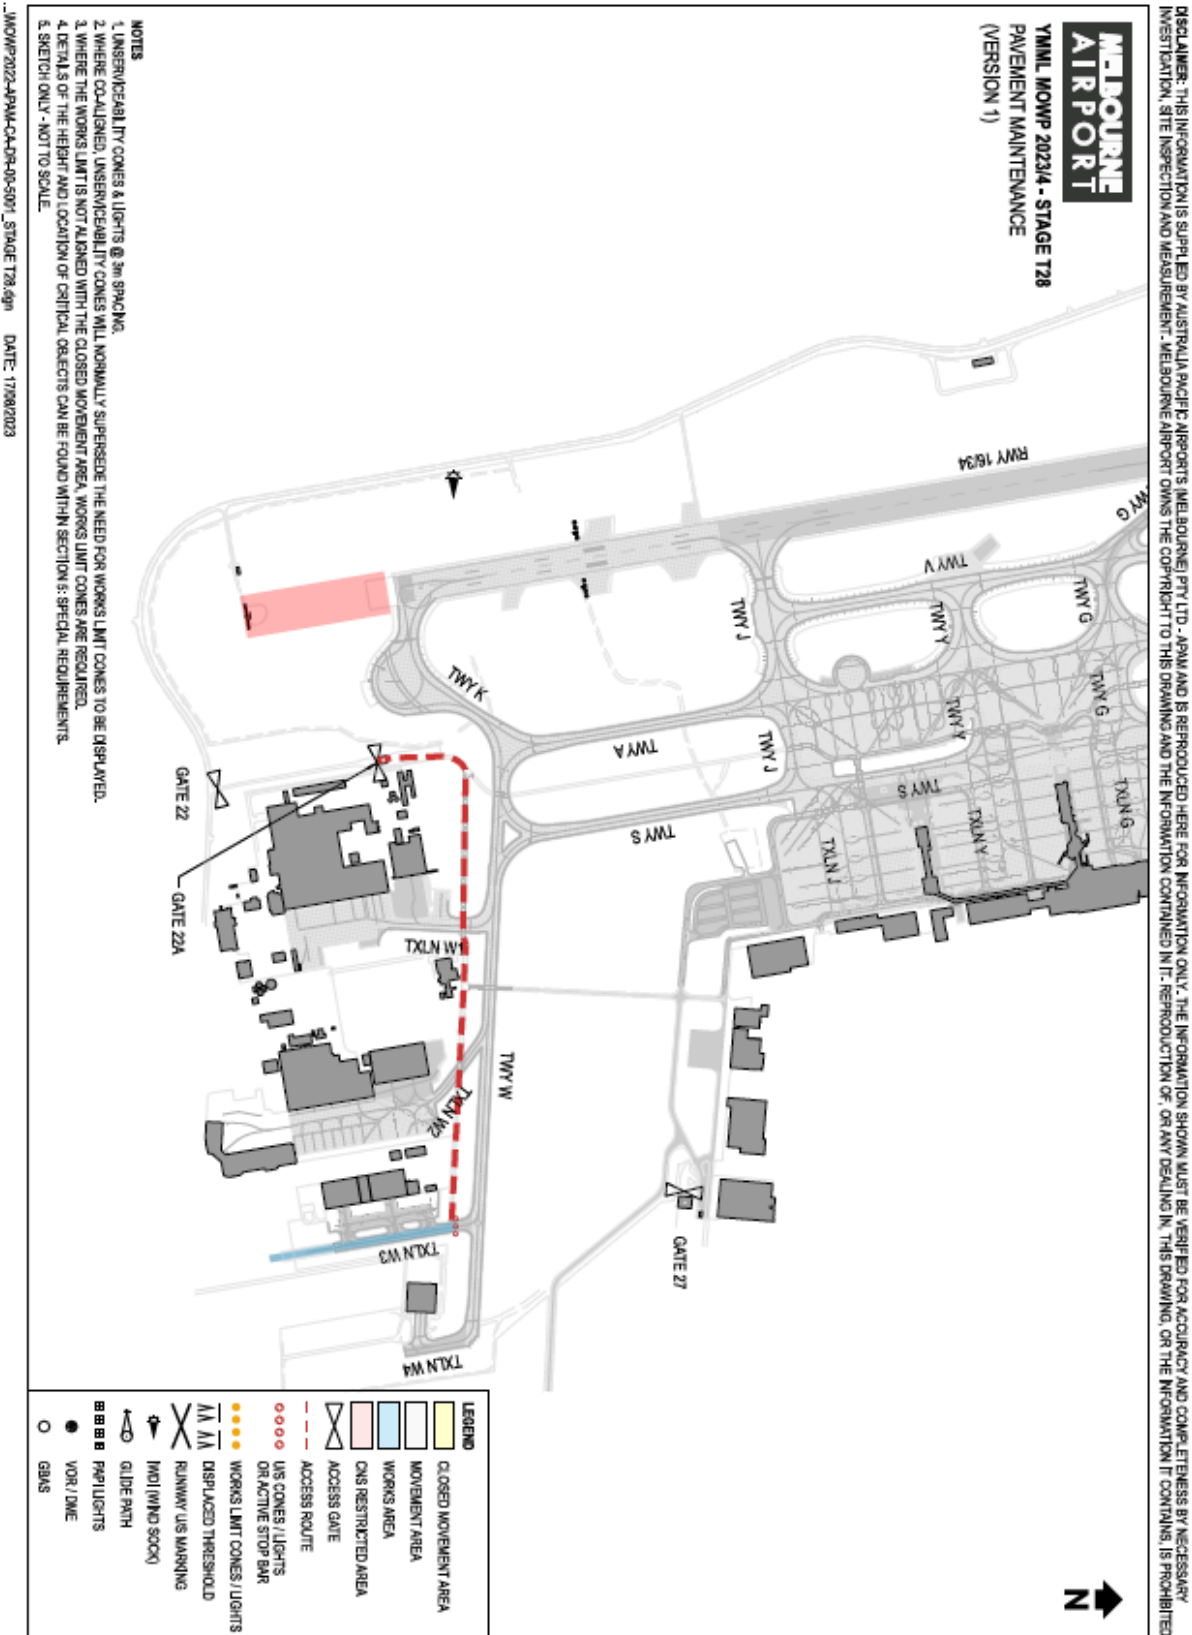


8.34. Stage T29

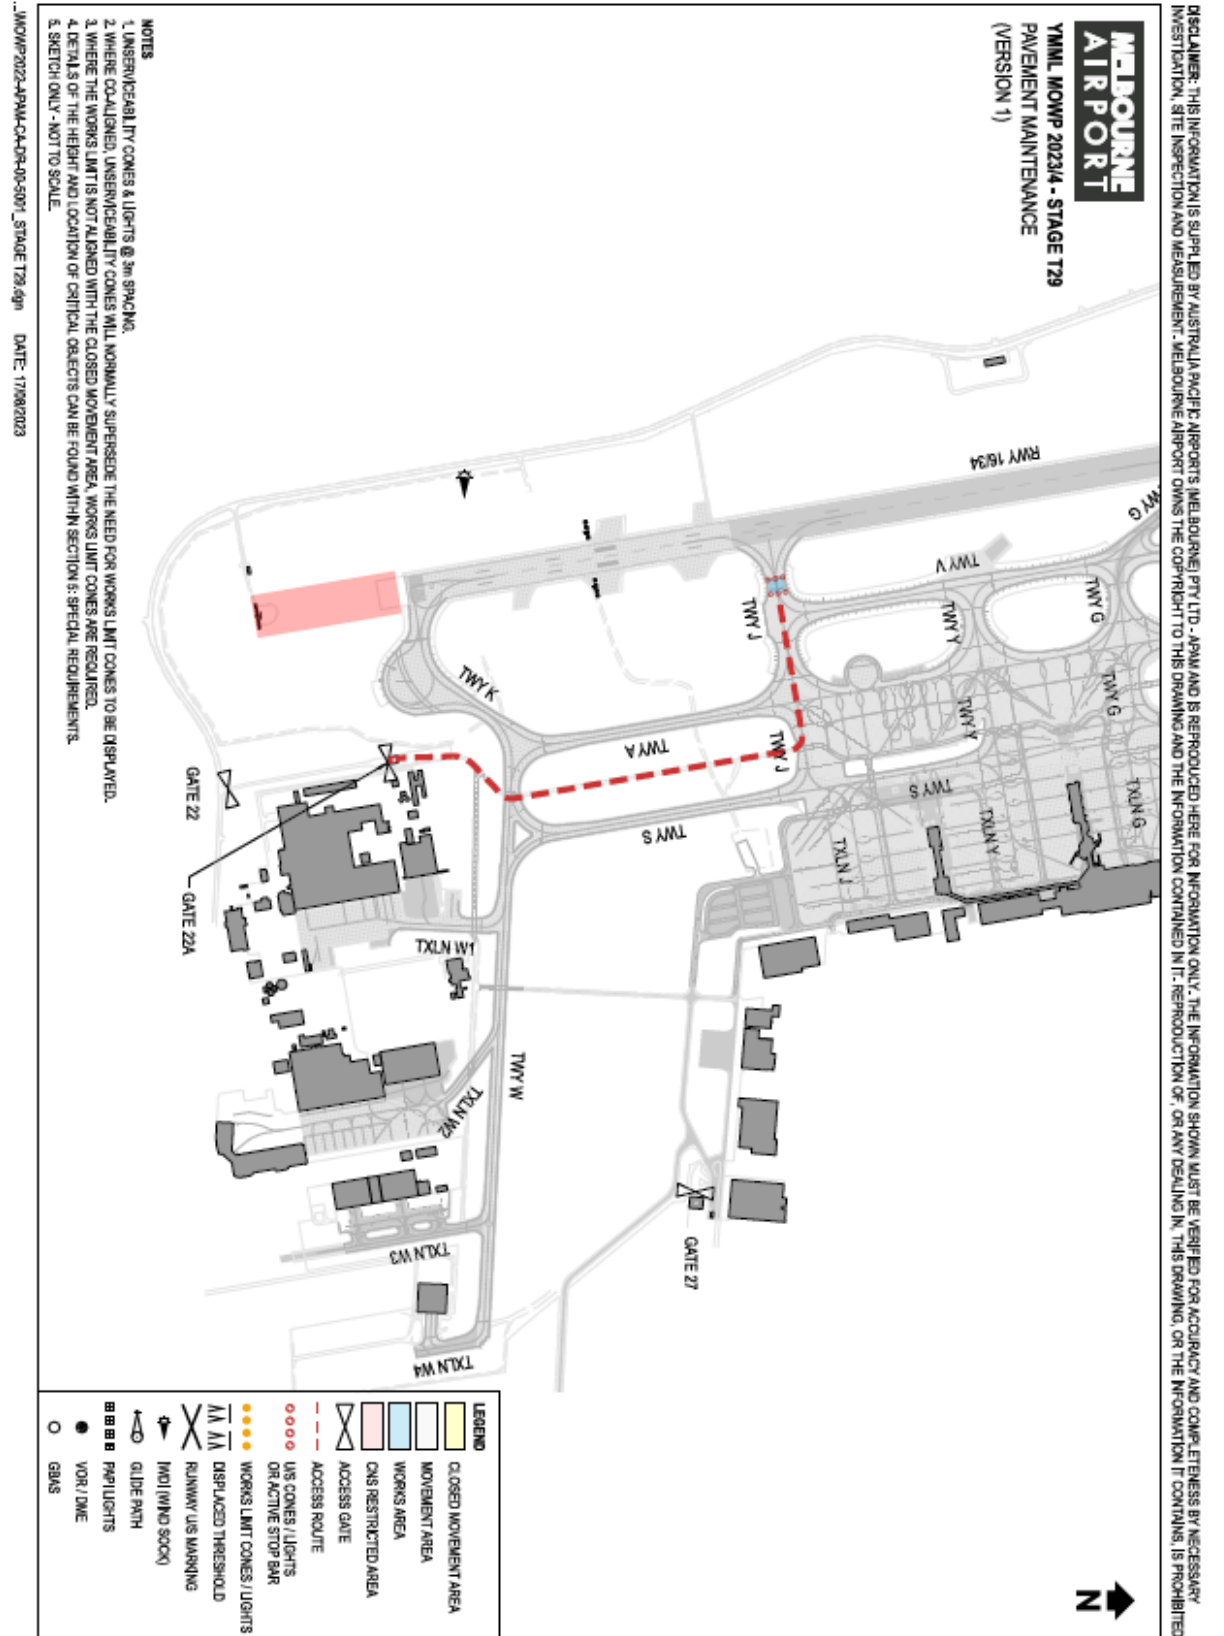


8.35. Stage T30

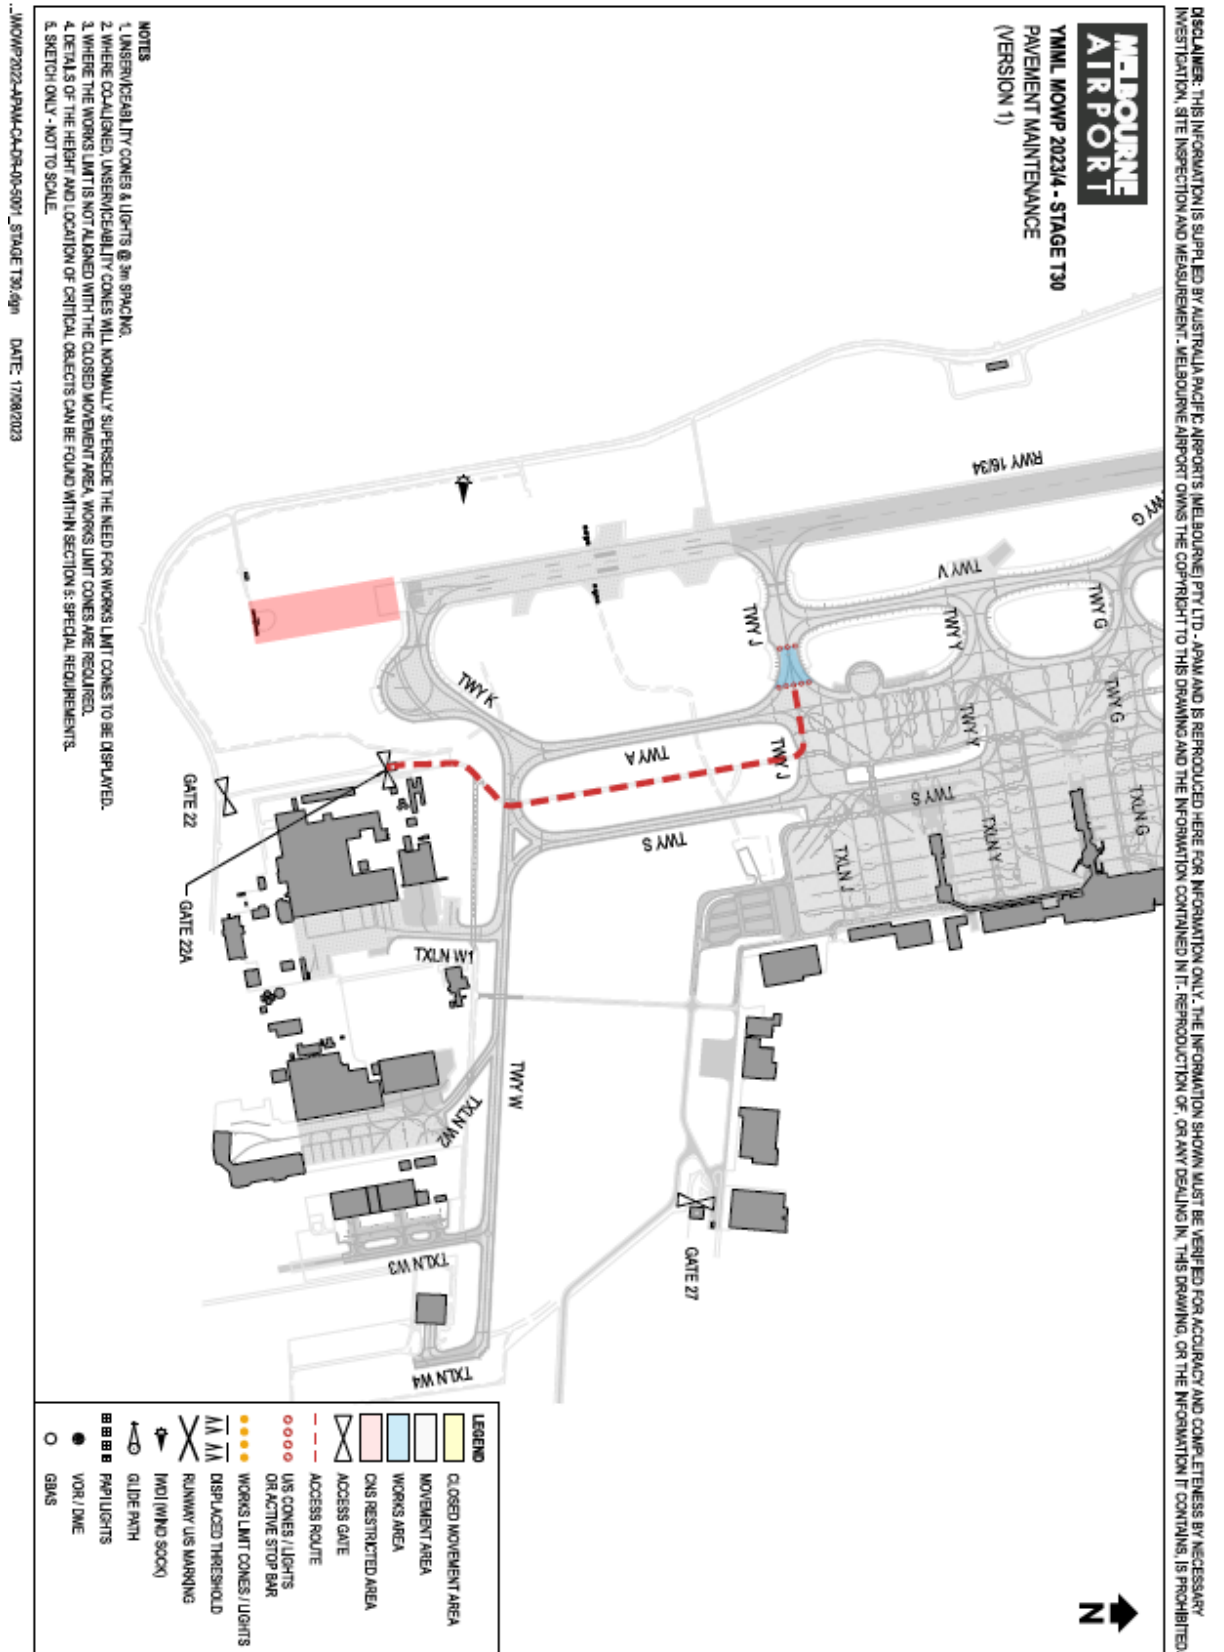


8.36. Stage T31

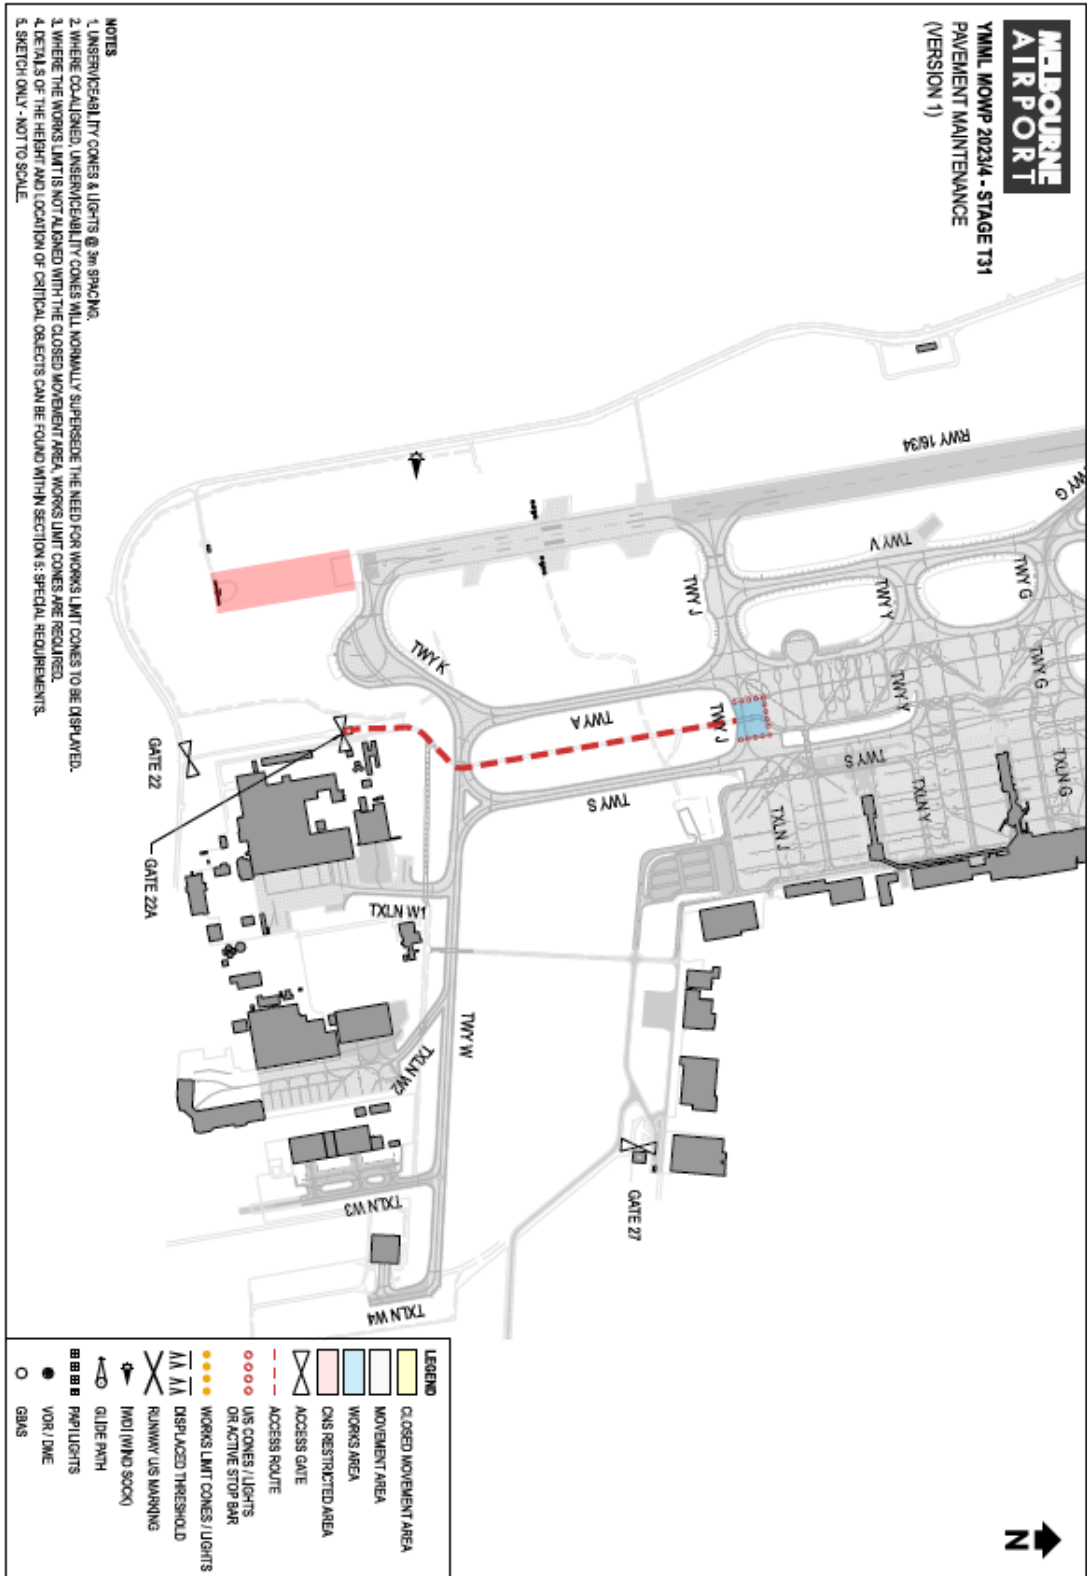


8.37. Stage T32

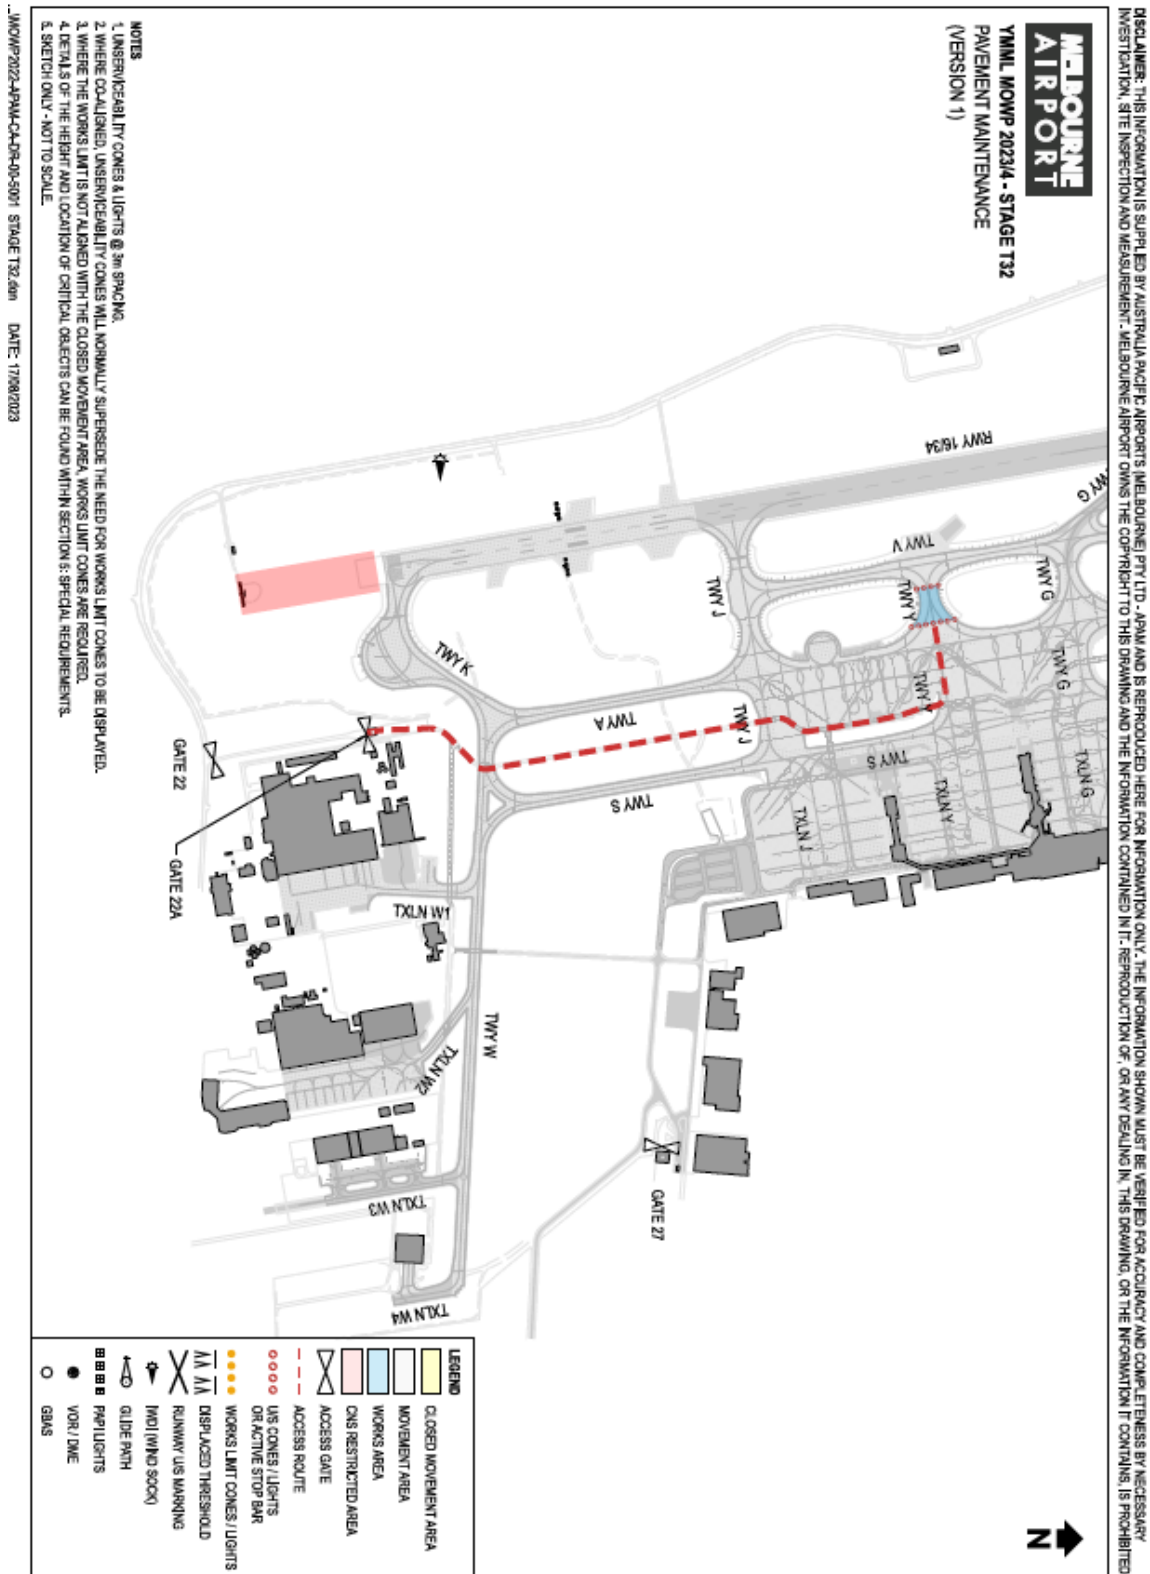


8.38. Stage T33

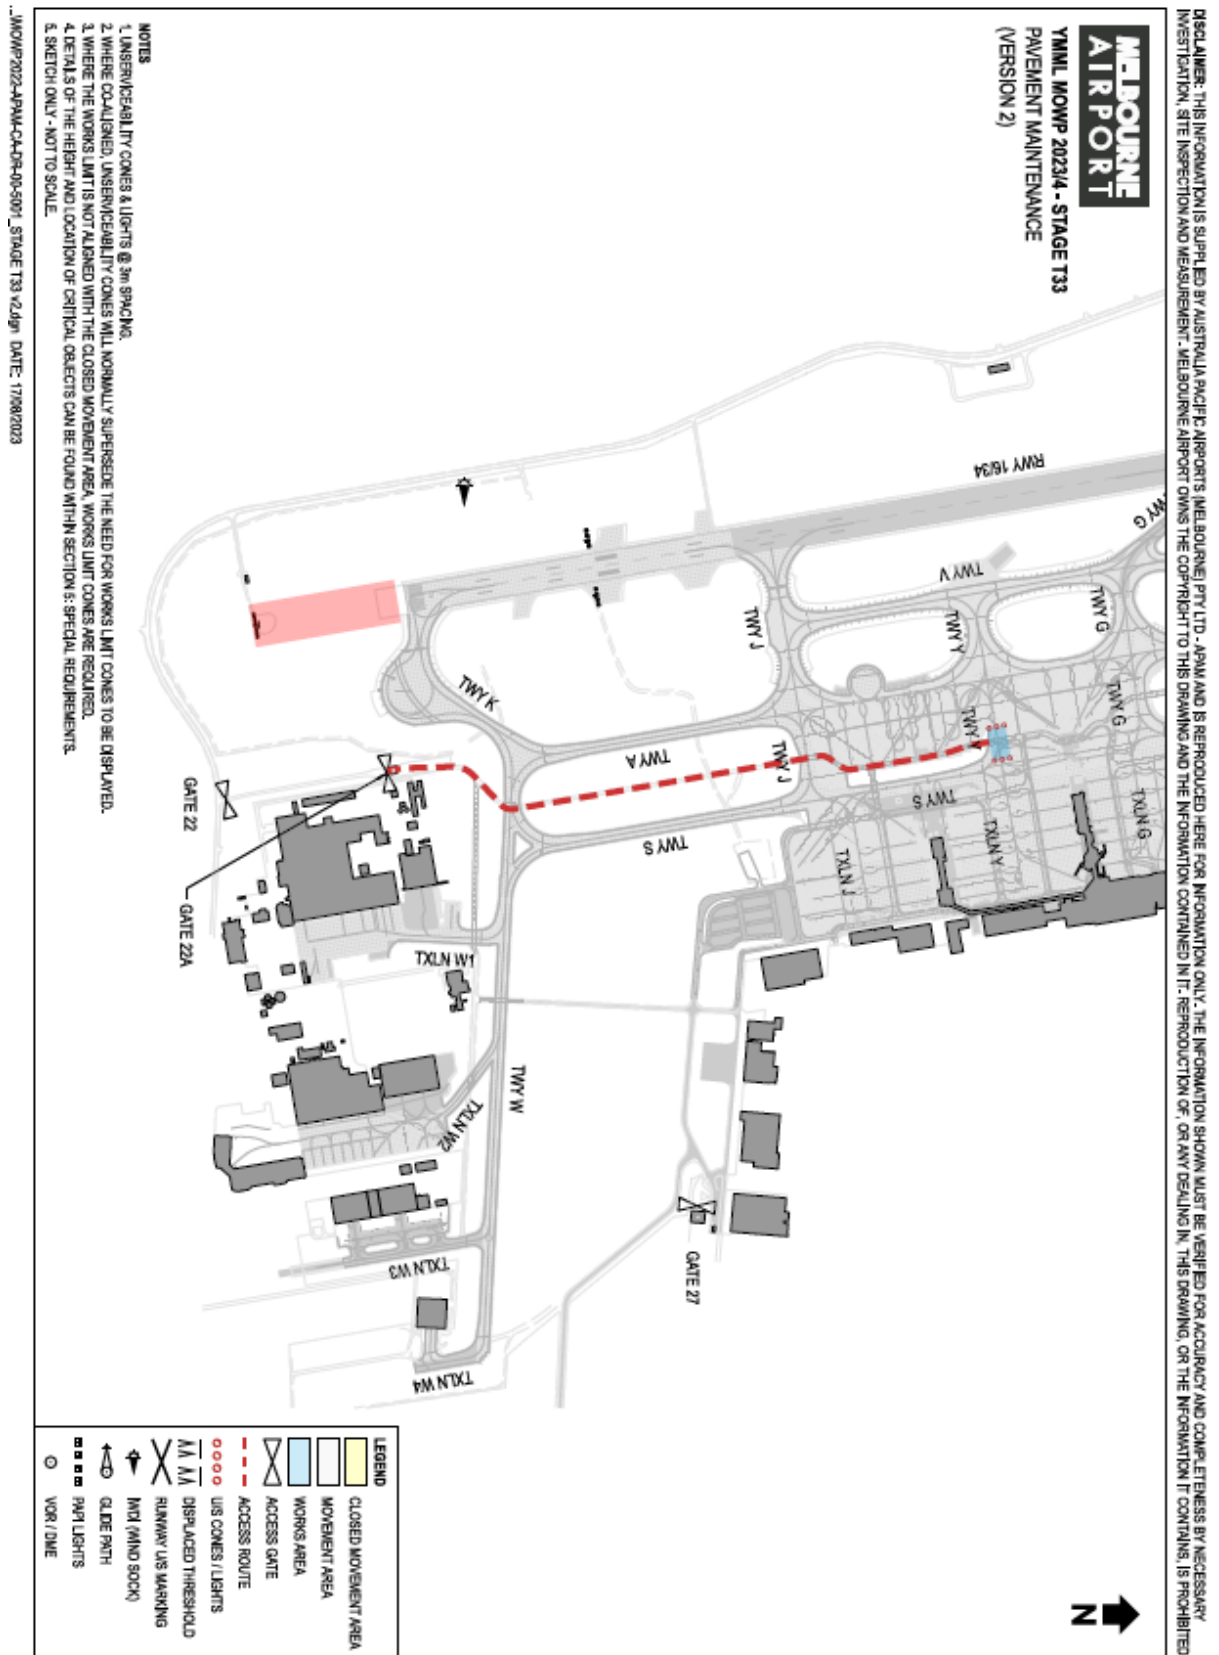


8.39. Stage T34

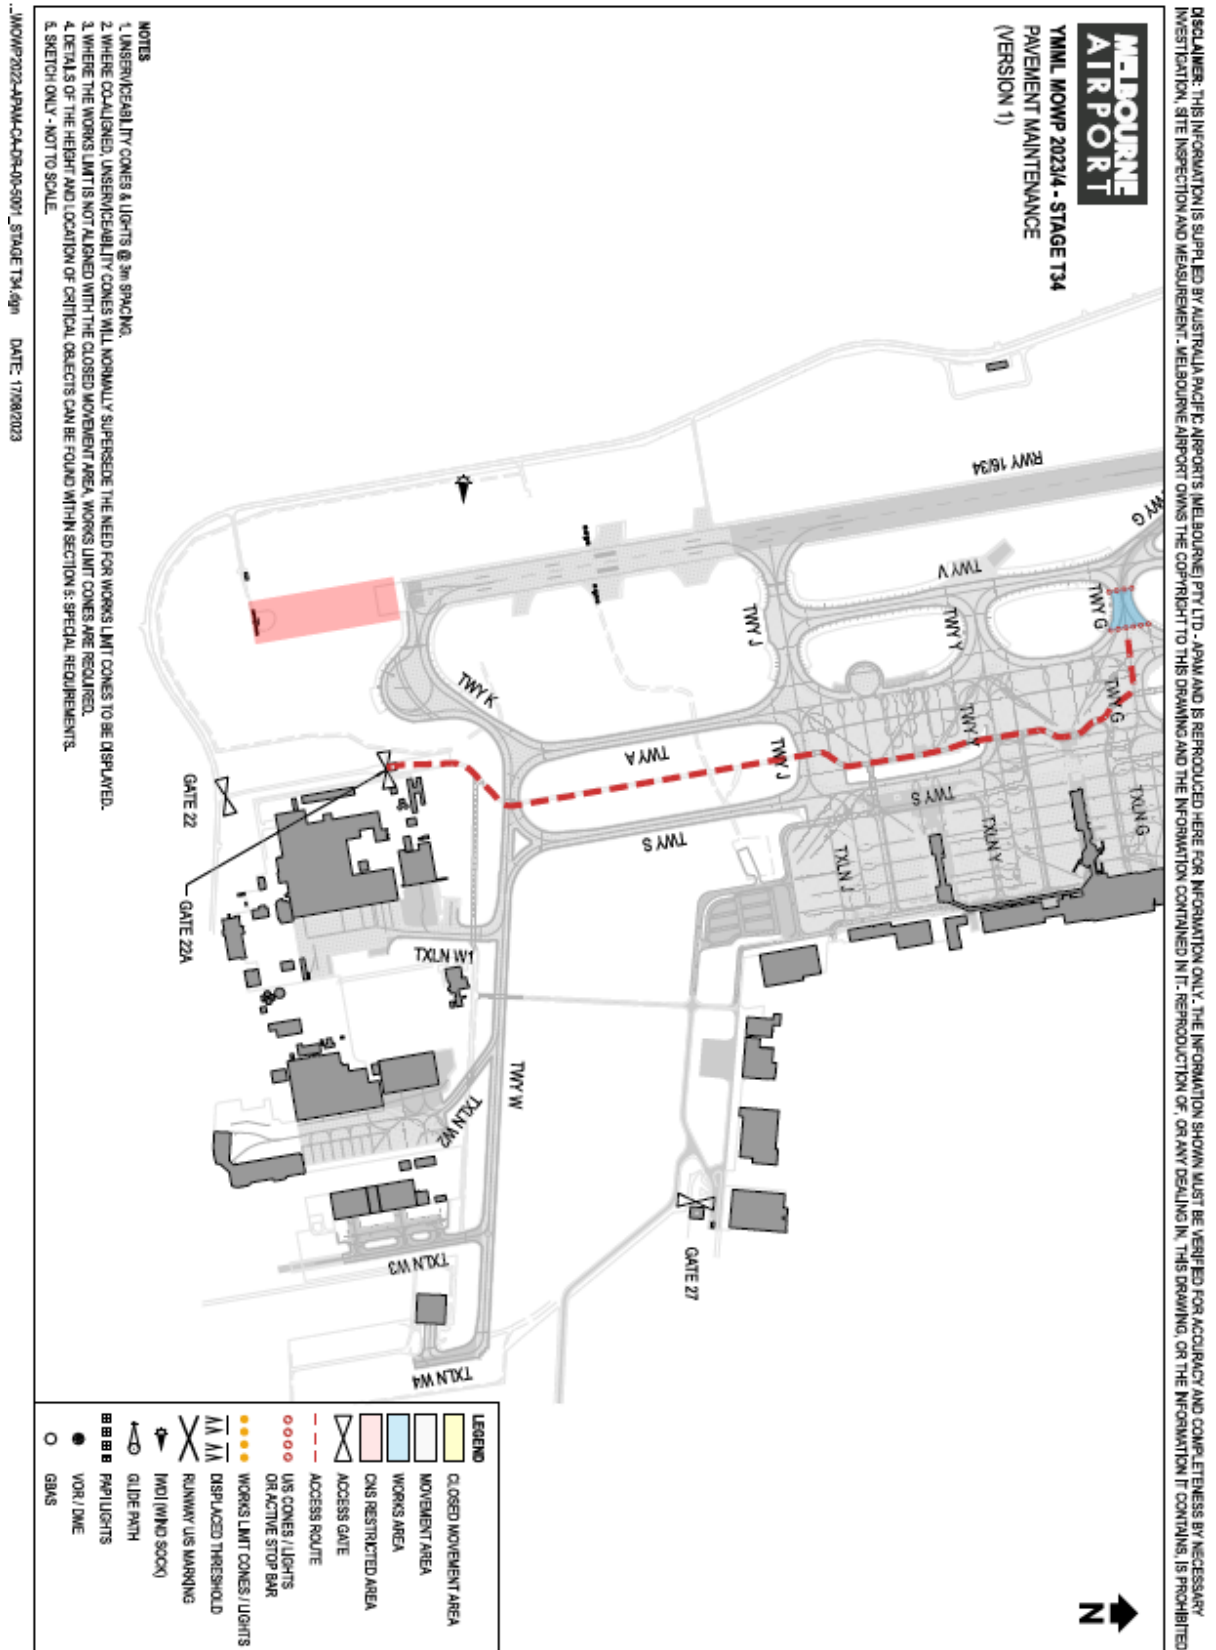


8.40. Stage T35

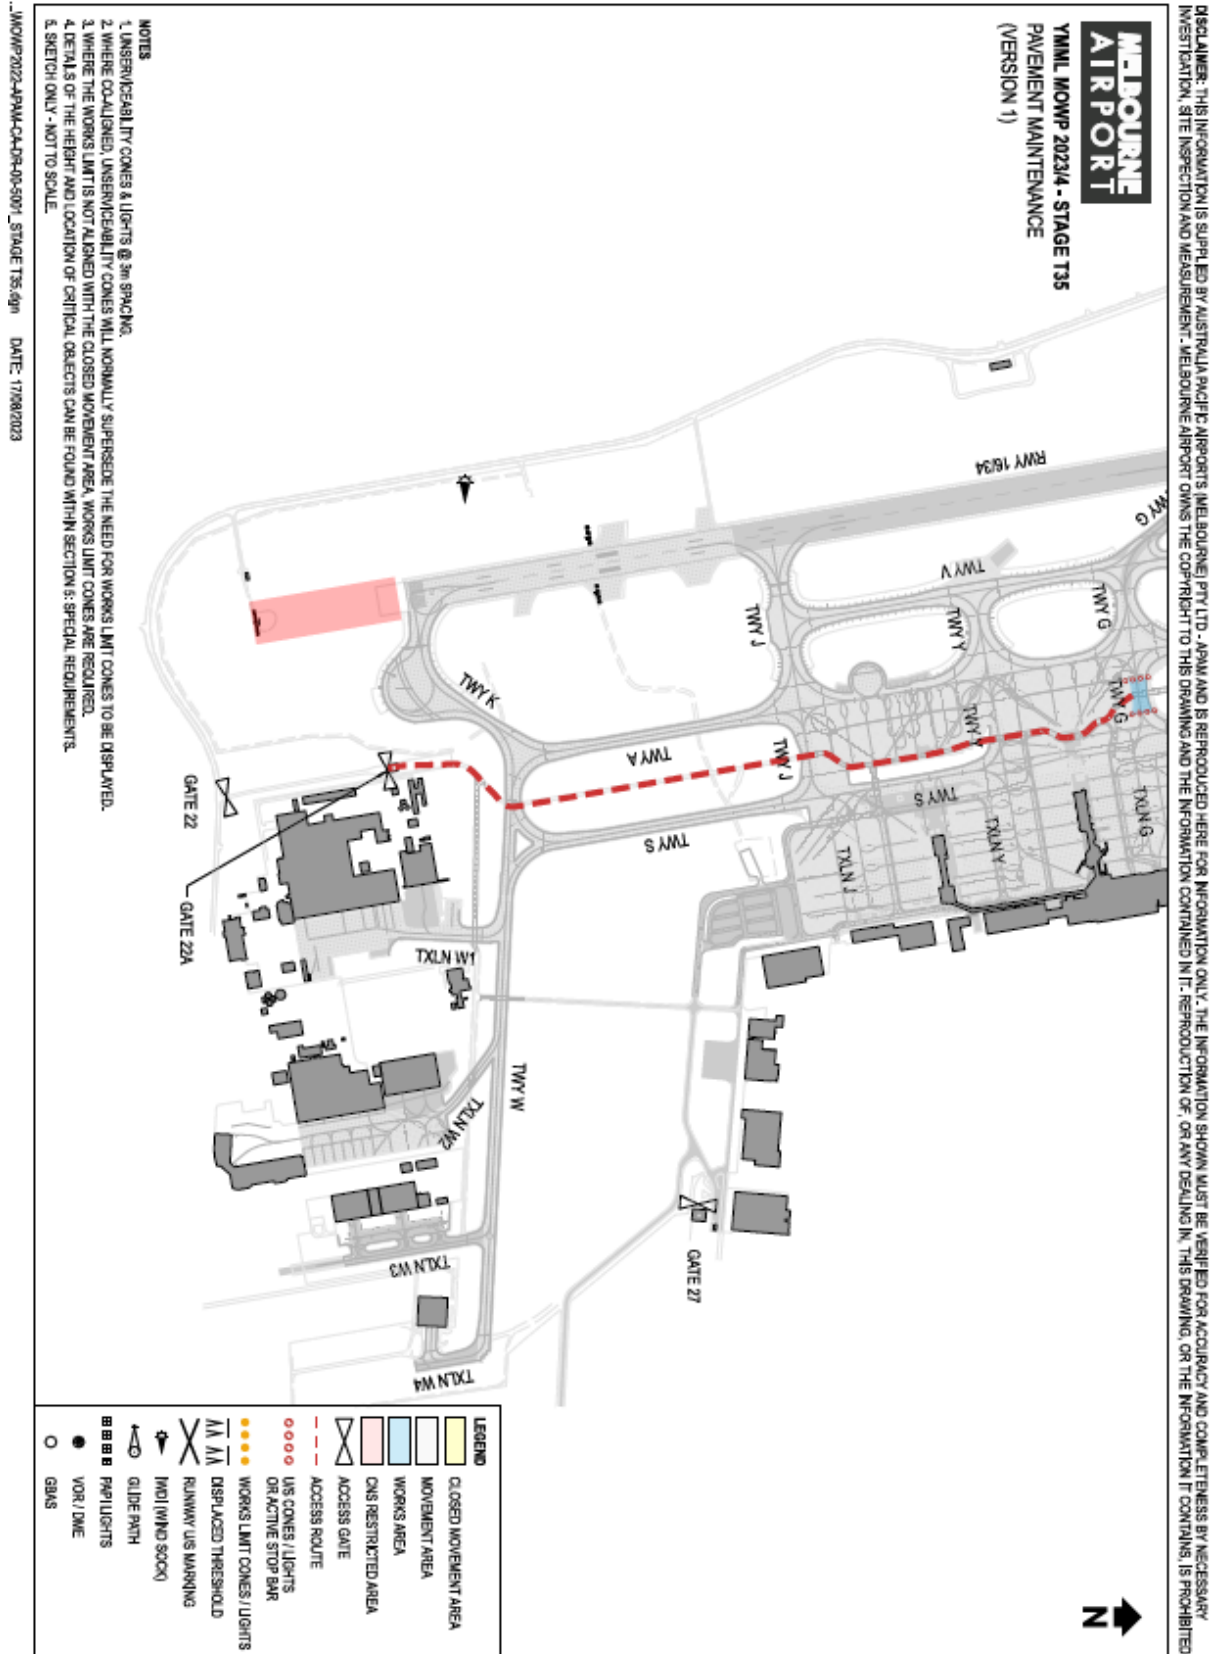


8.41. Stage T36

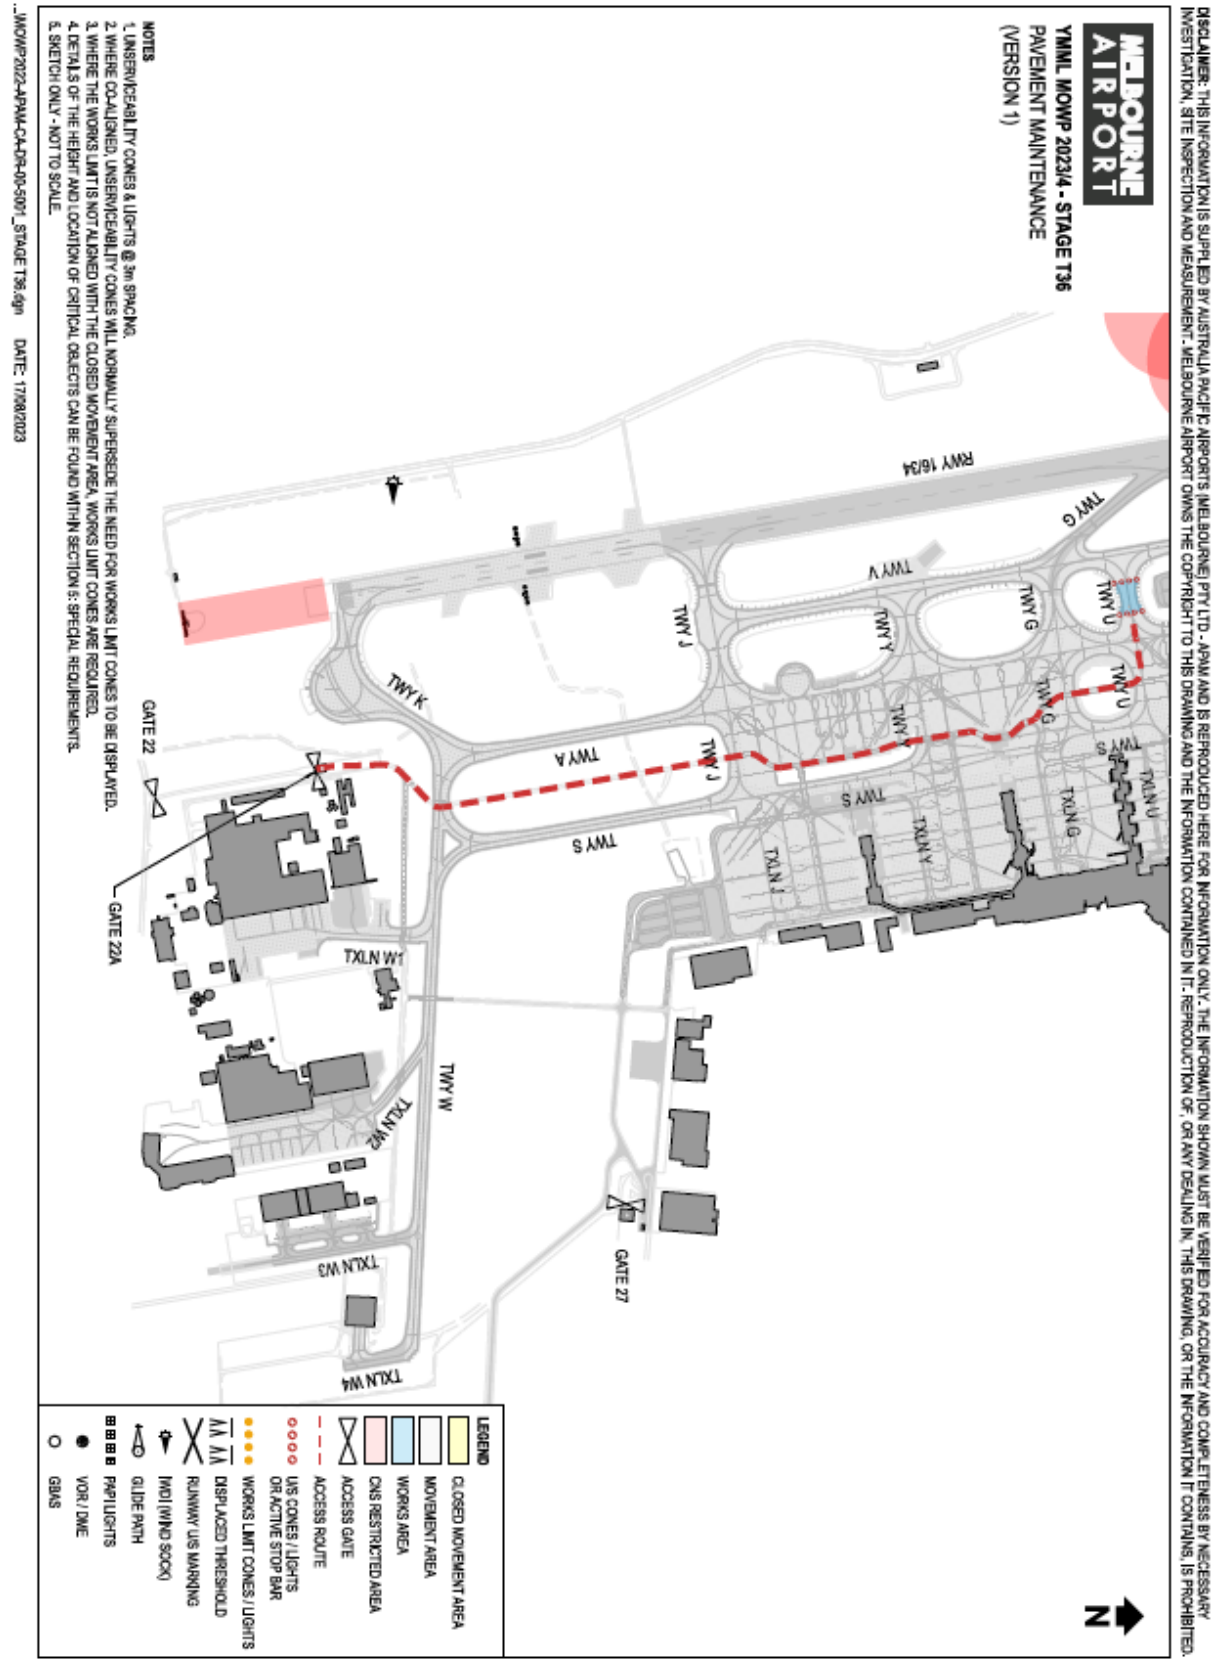


8.42. Stage T37

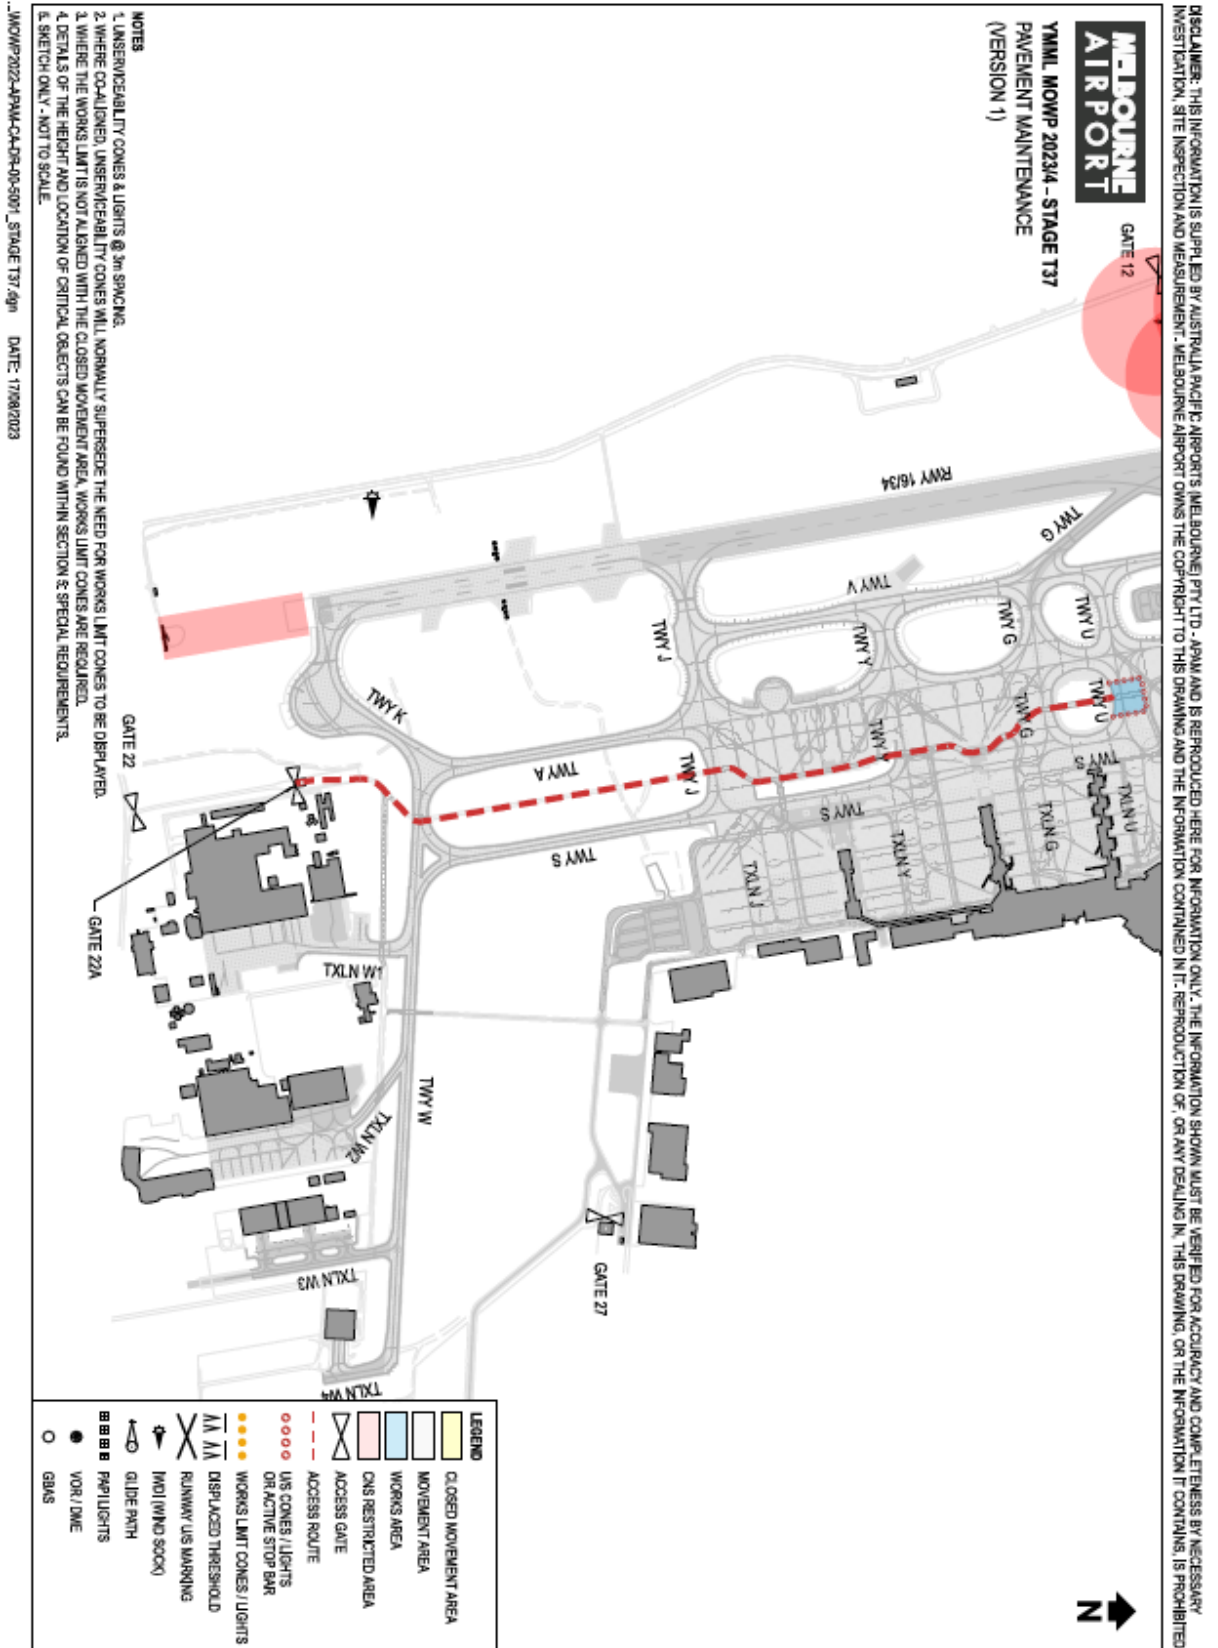


8.43. Stage T38

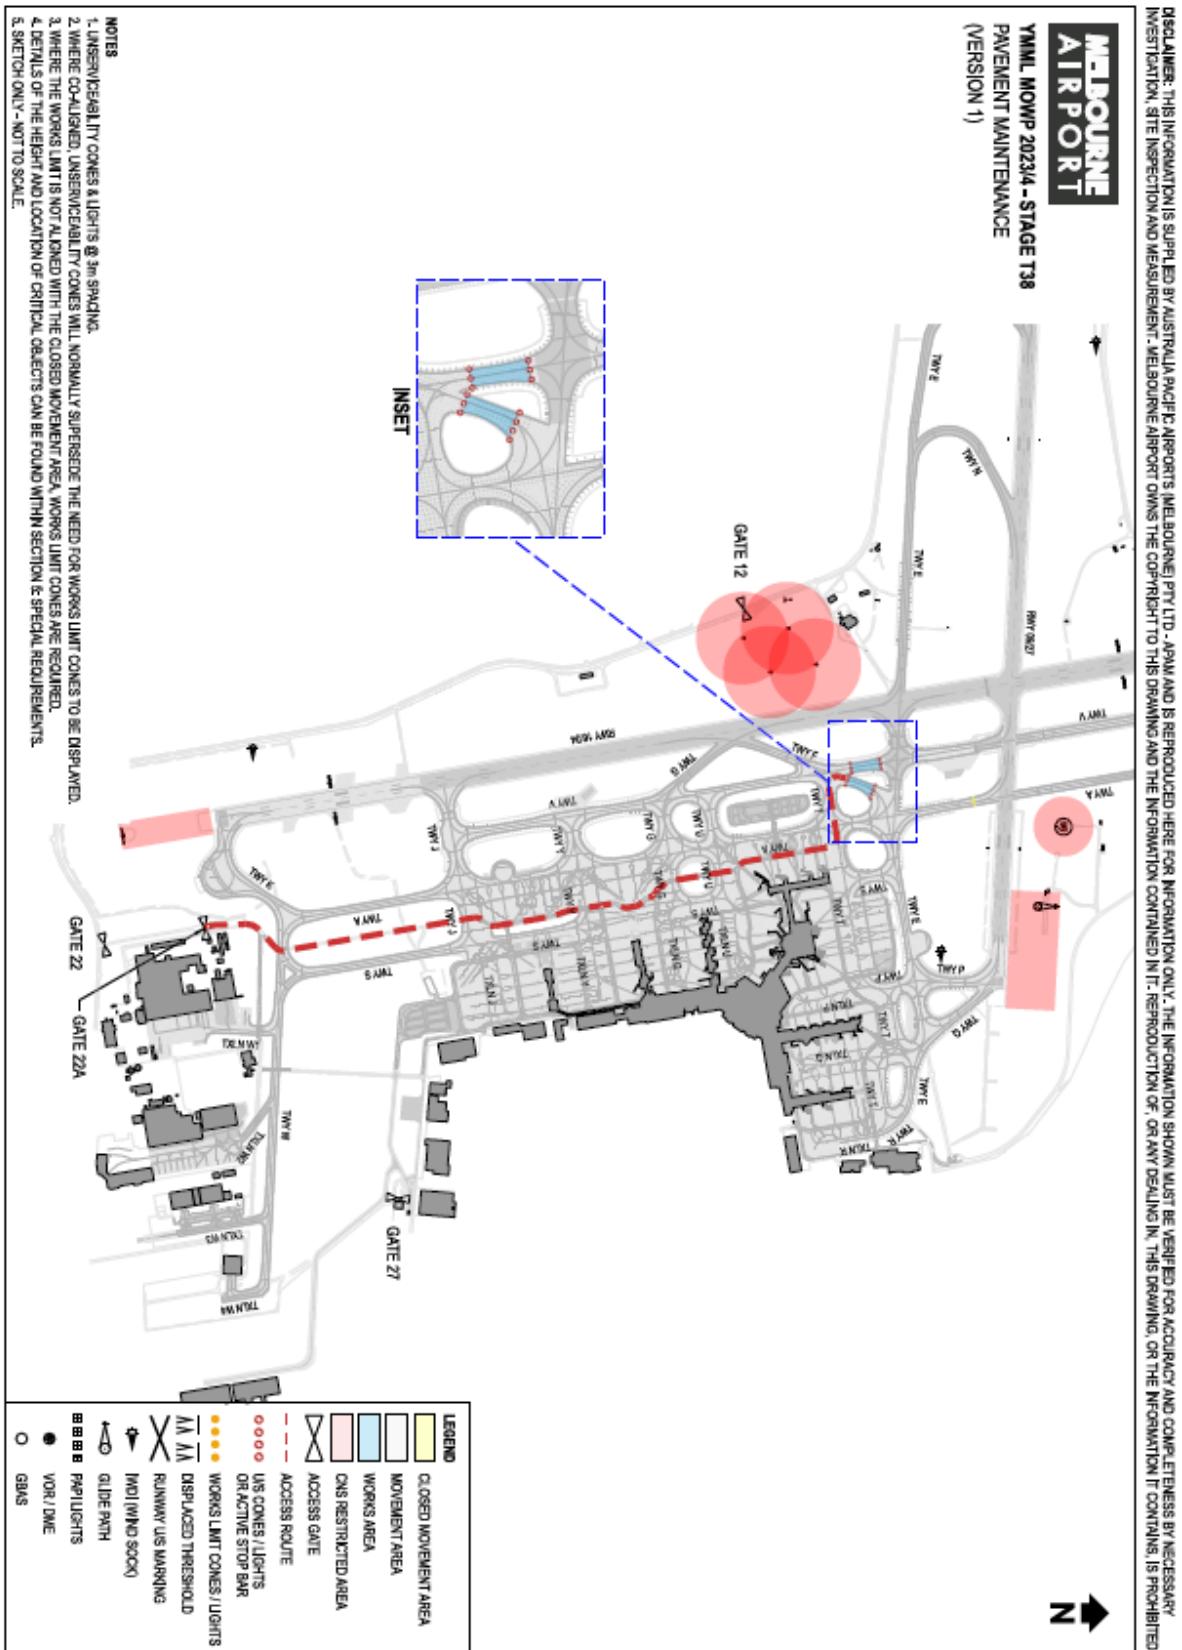


8.44. Stage T39

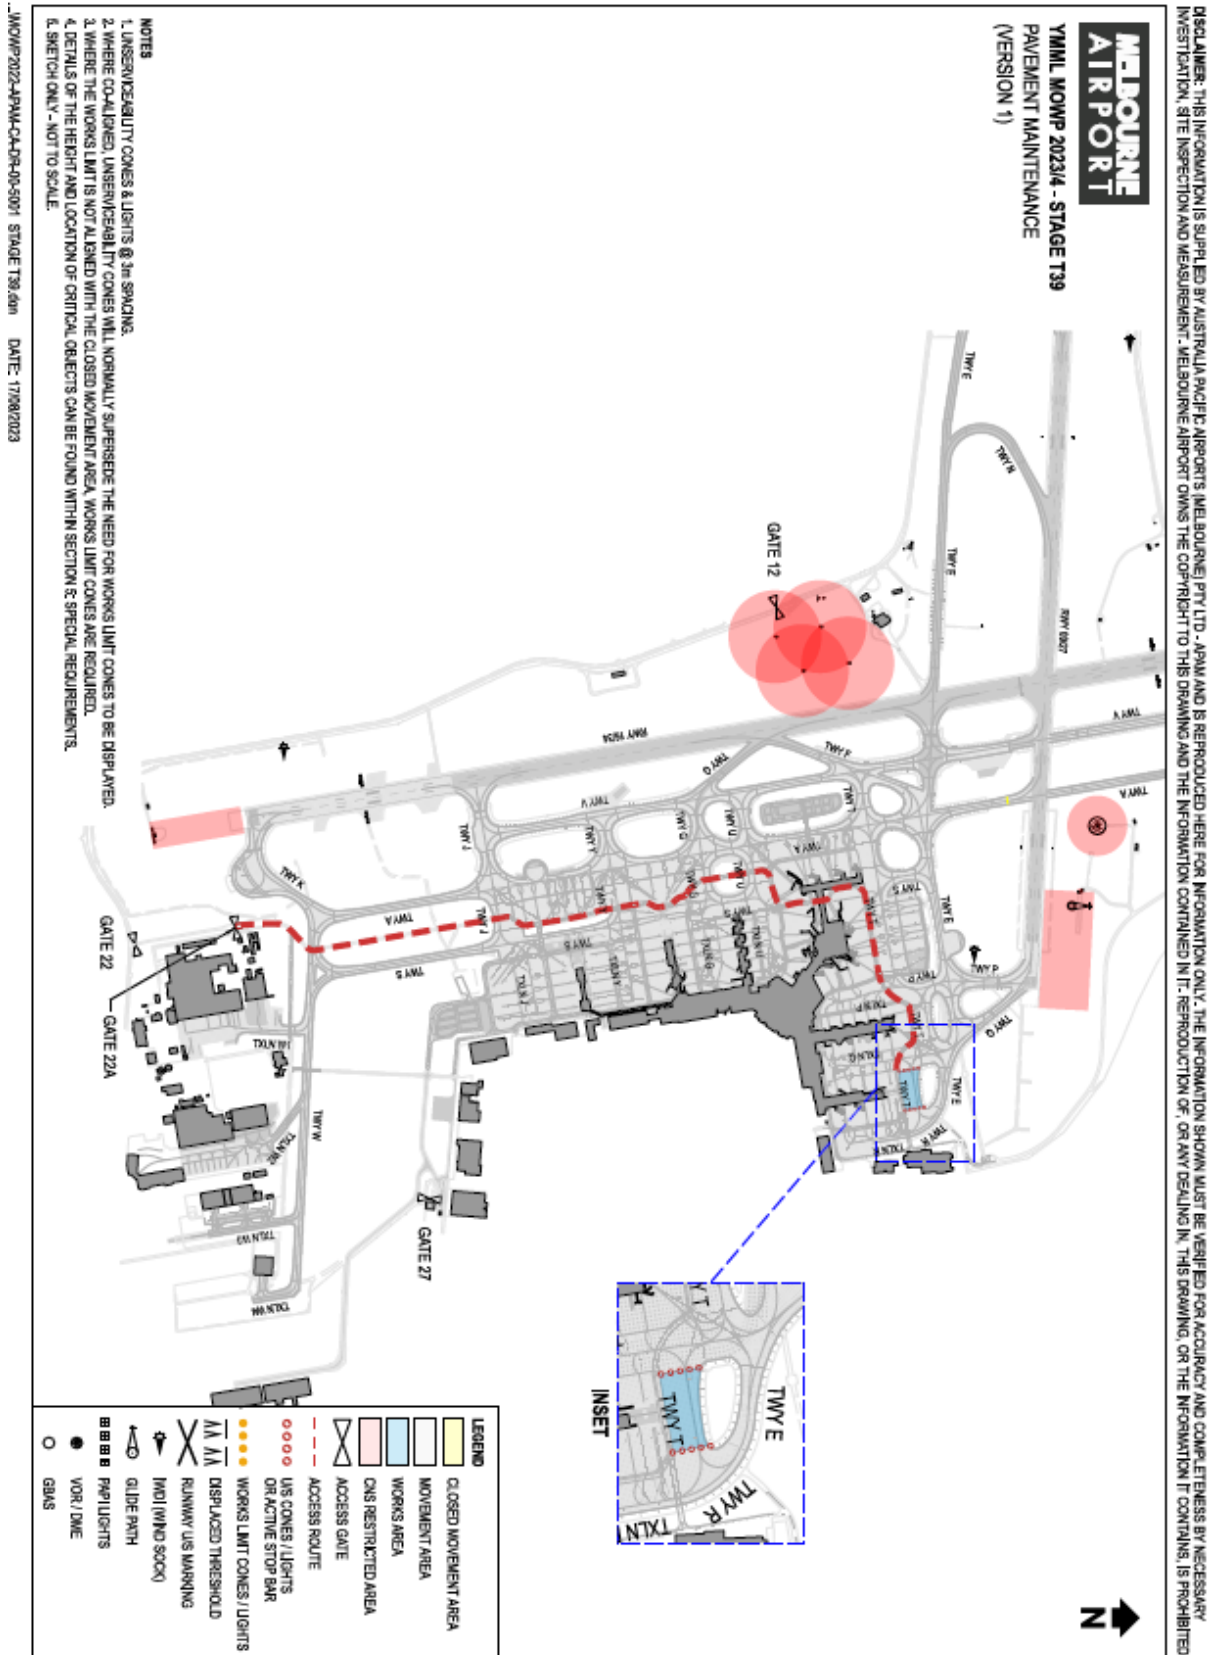


8.45. Stage T40

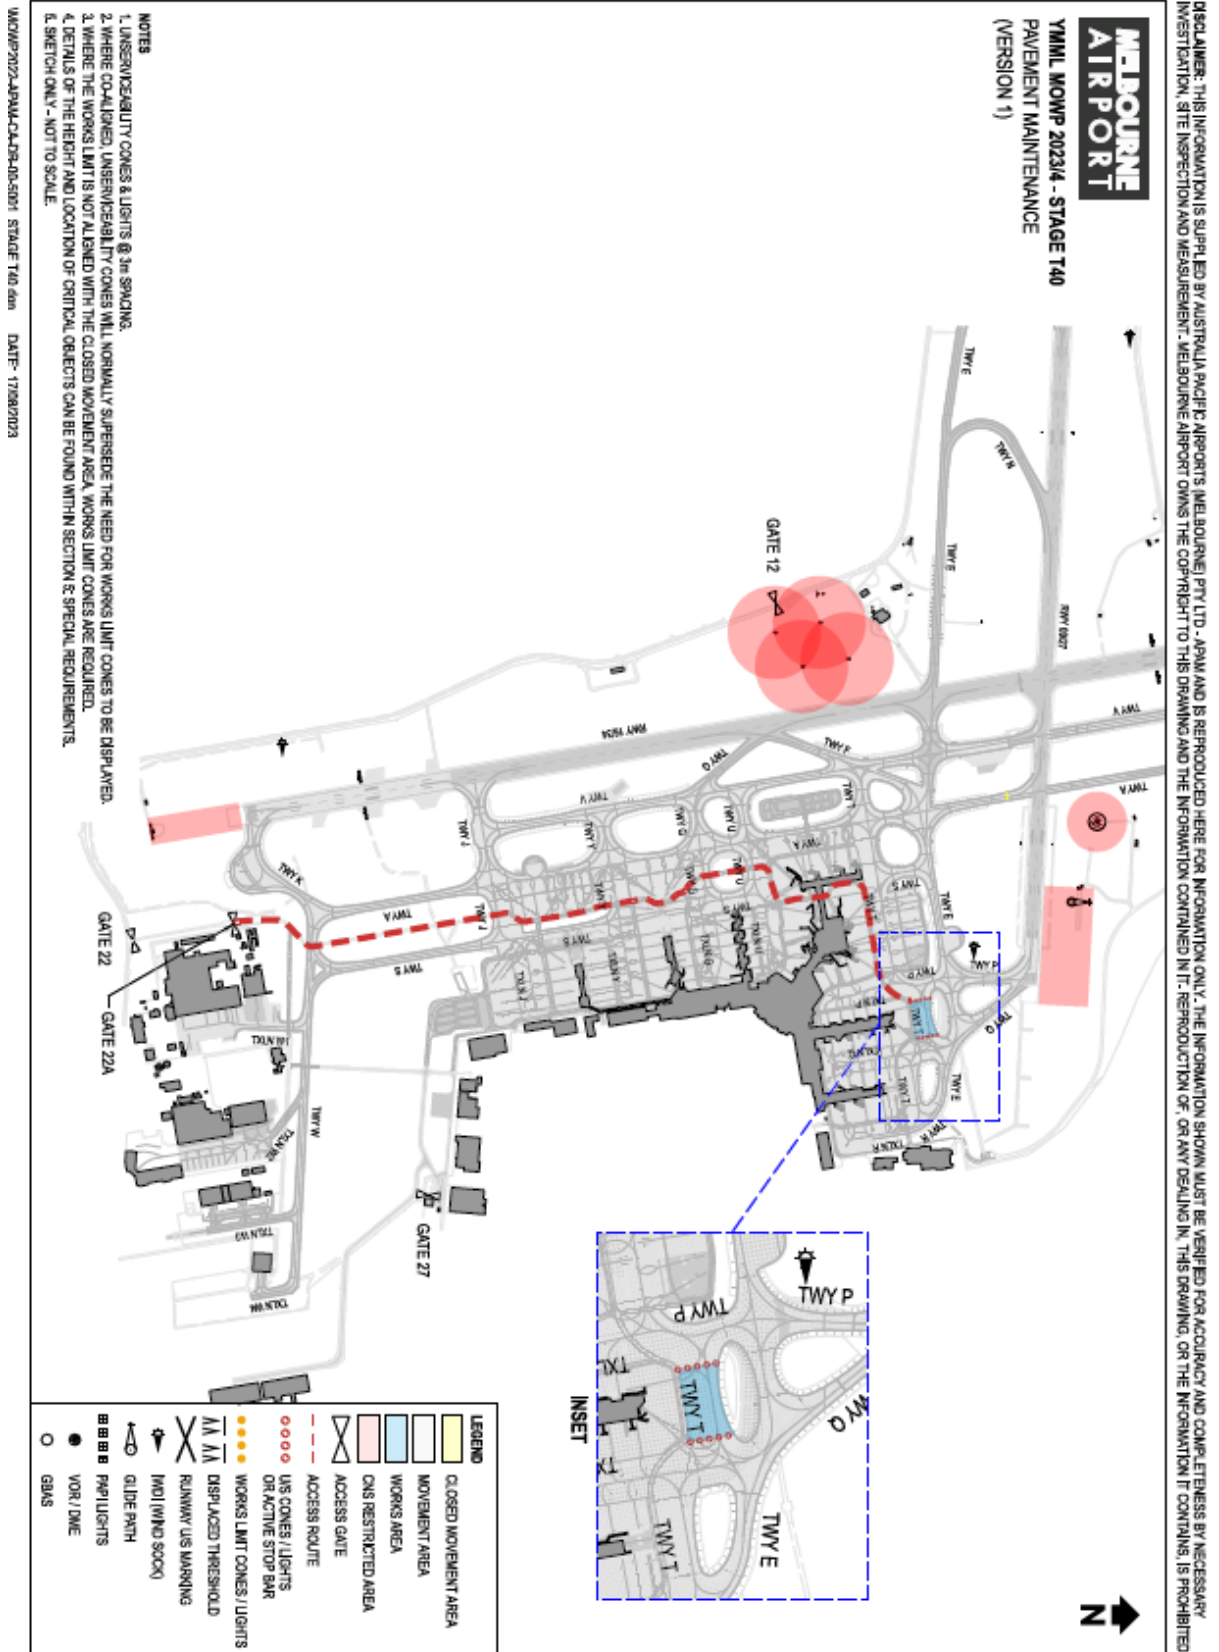


8.46. Stage T41

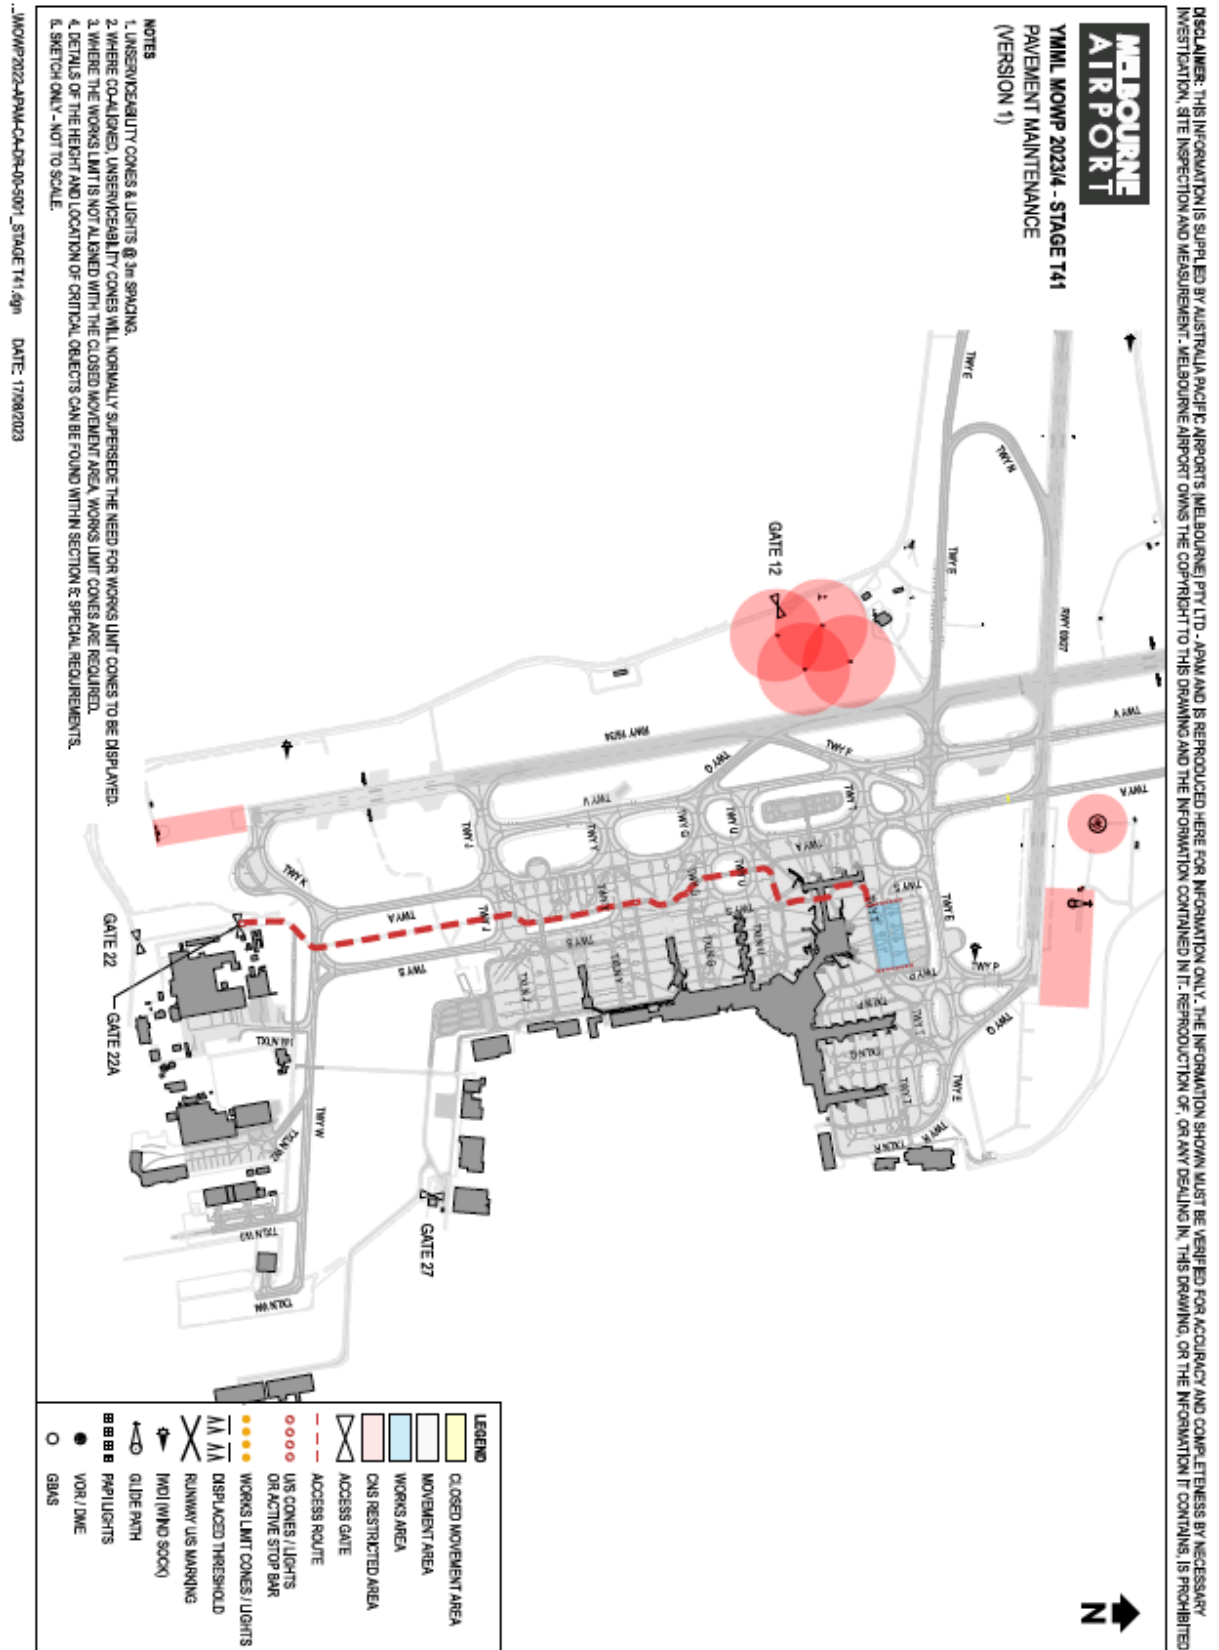

8.47. Stage T42

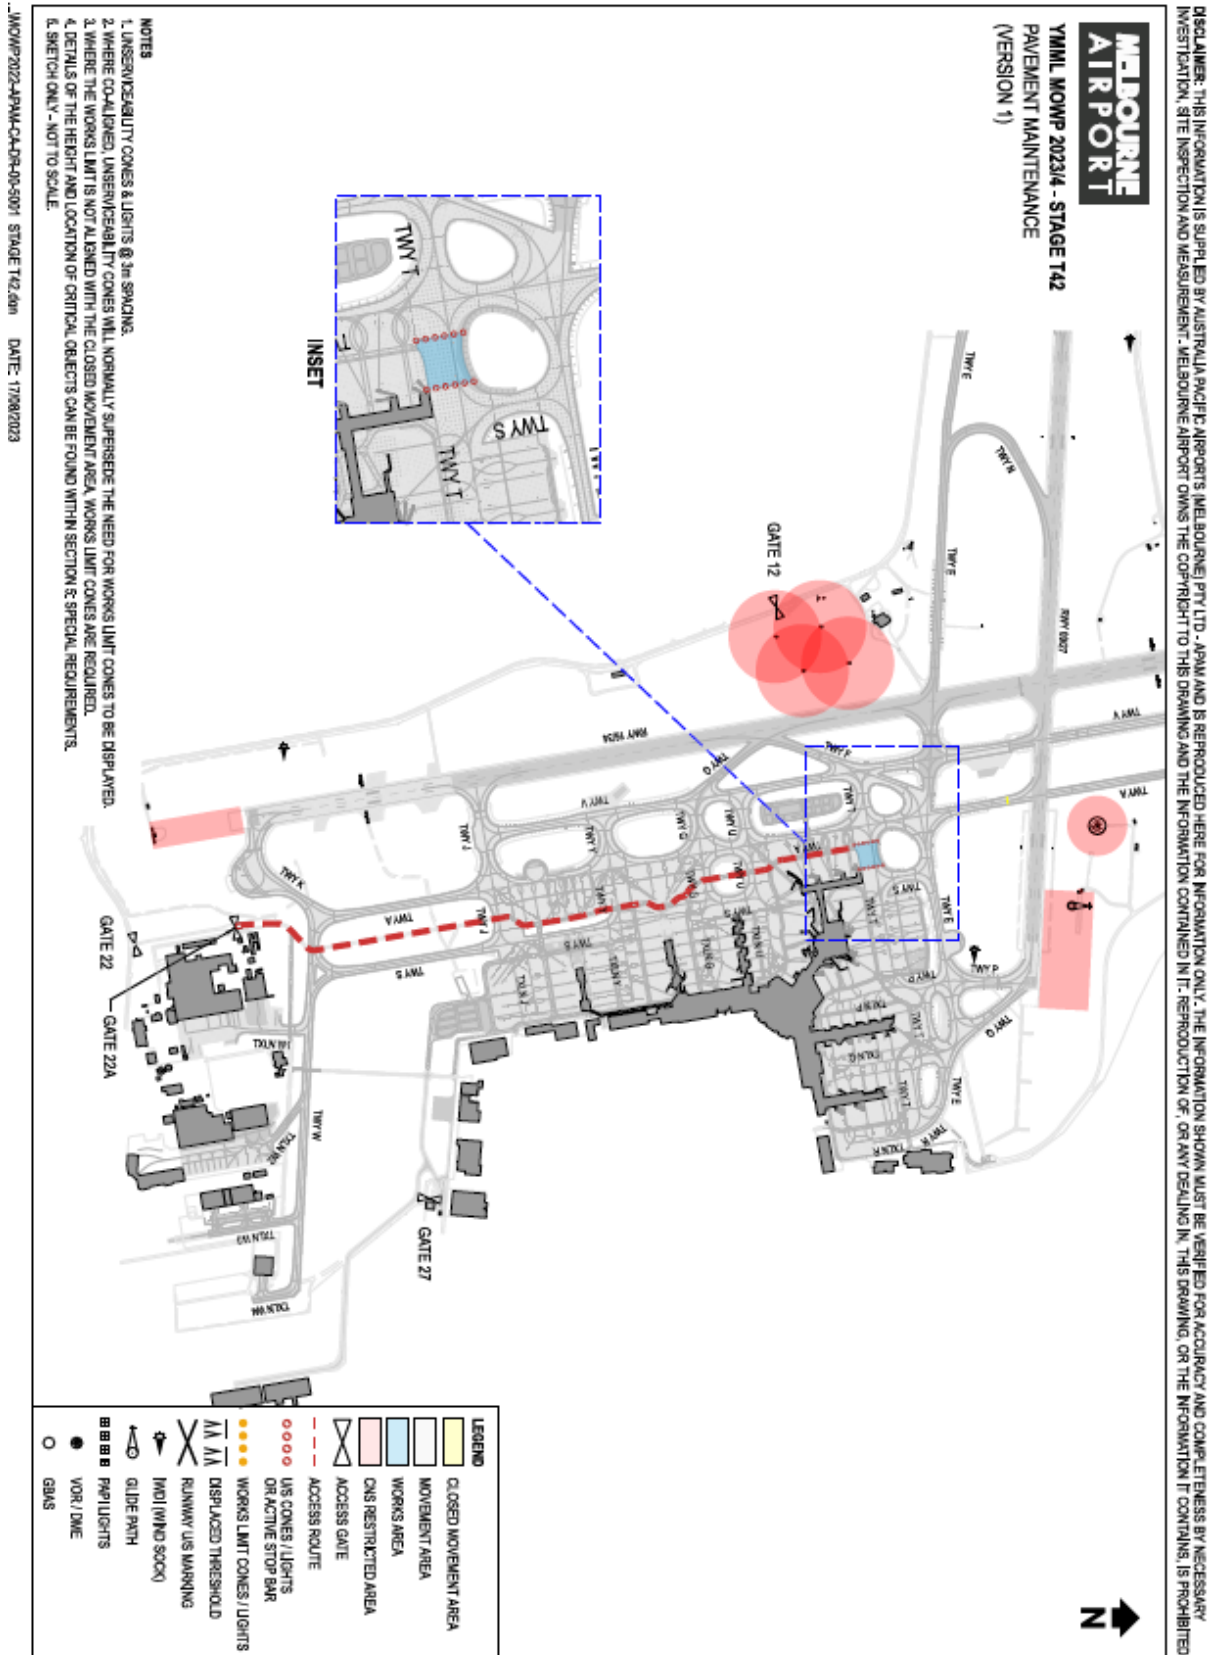


8.48. Stage T43

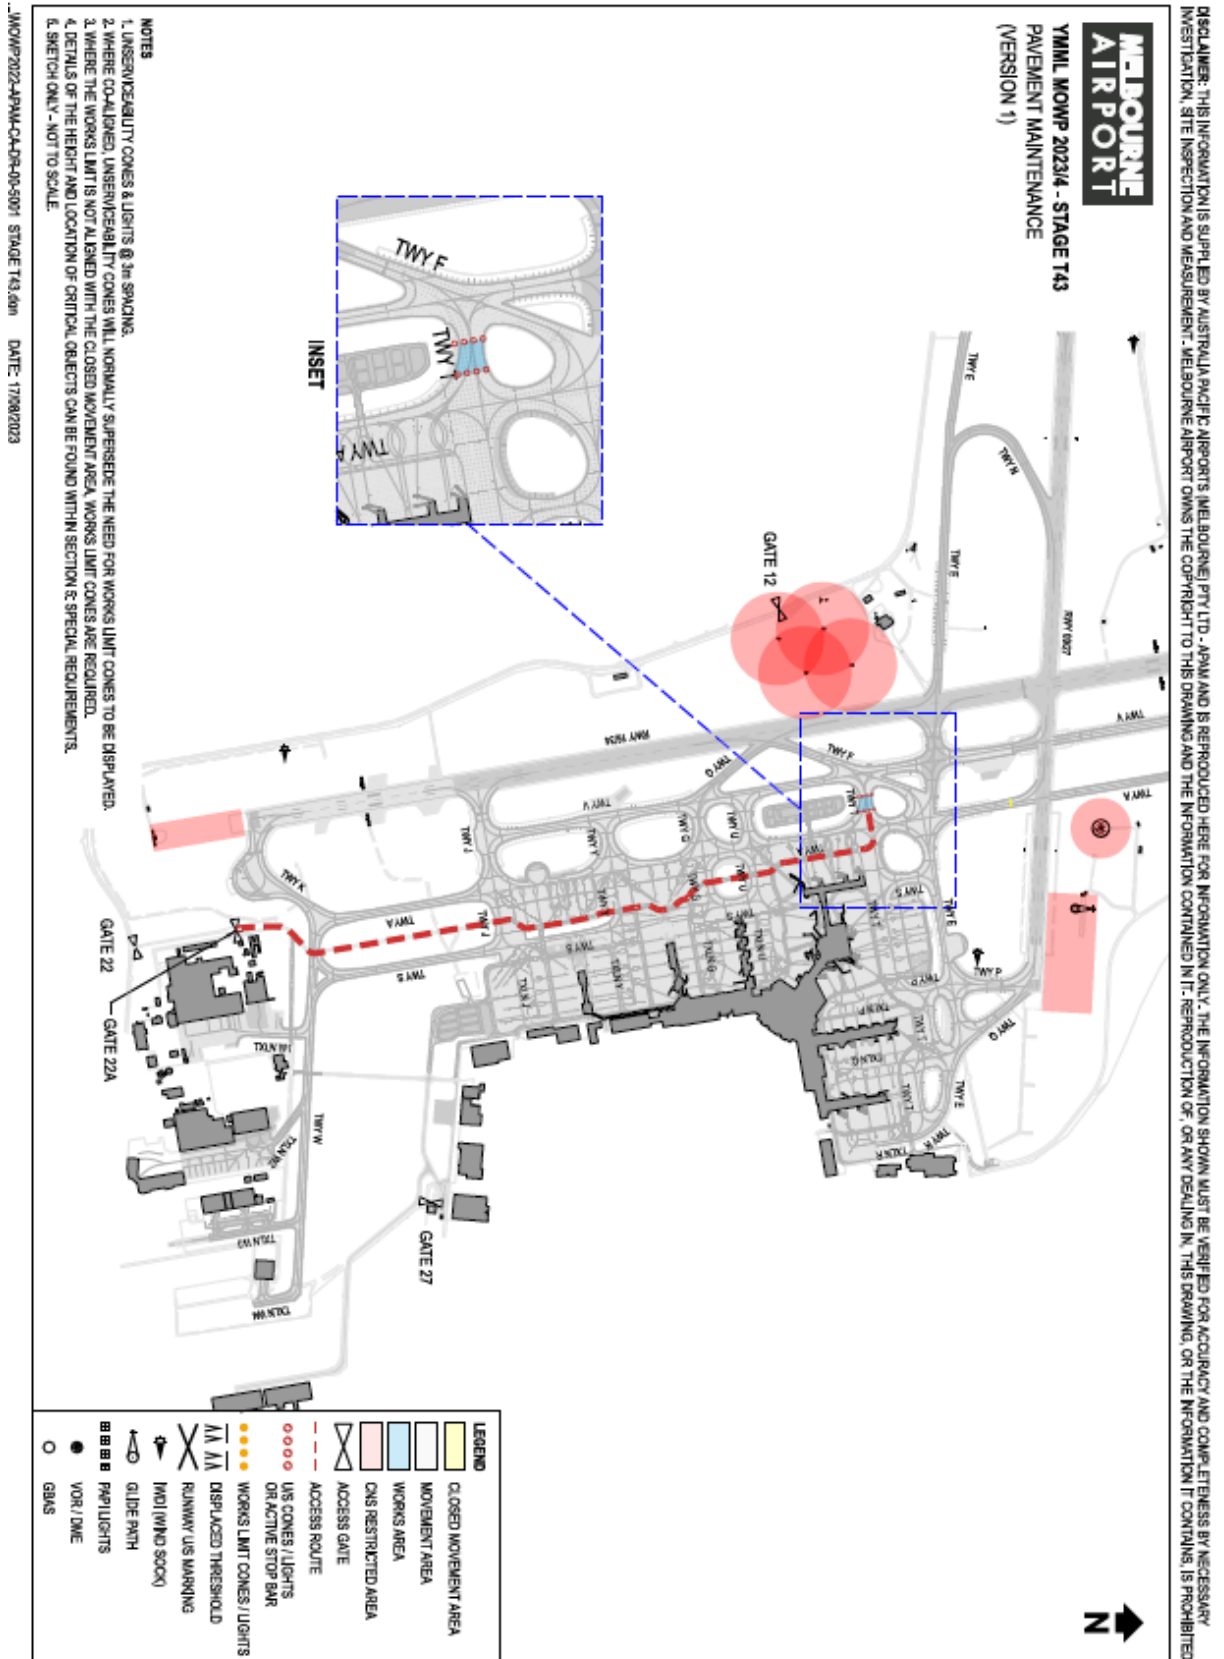

8.49. Stage T44




8.50. Stage T45

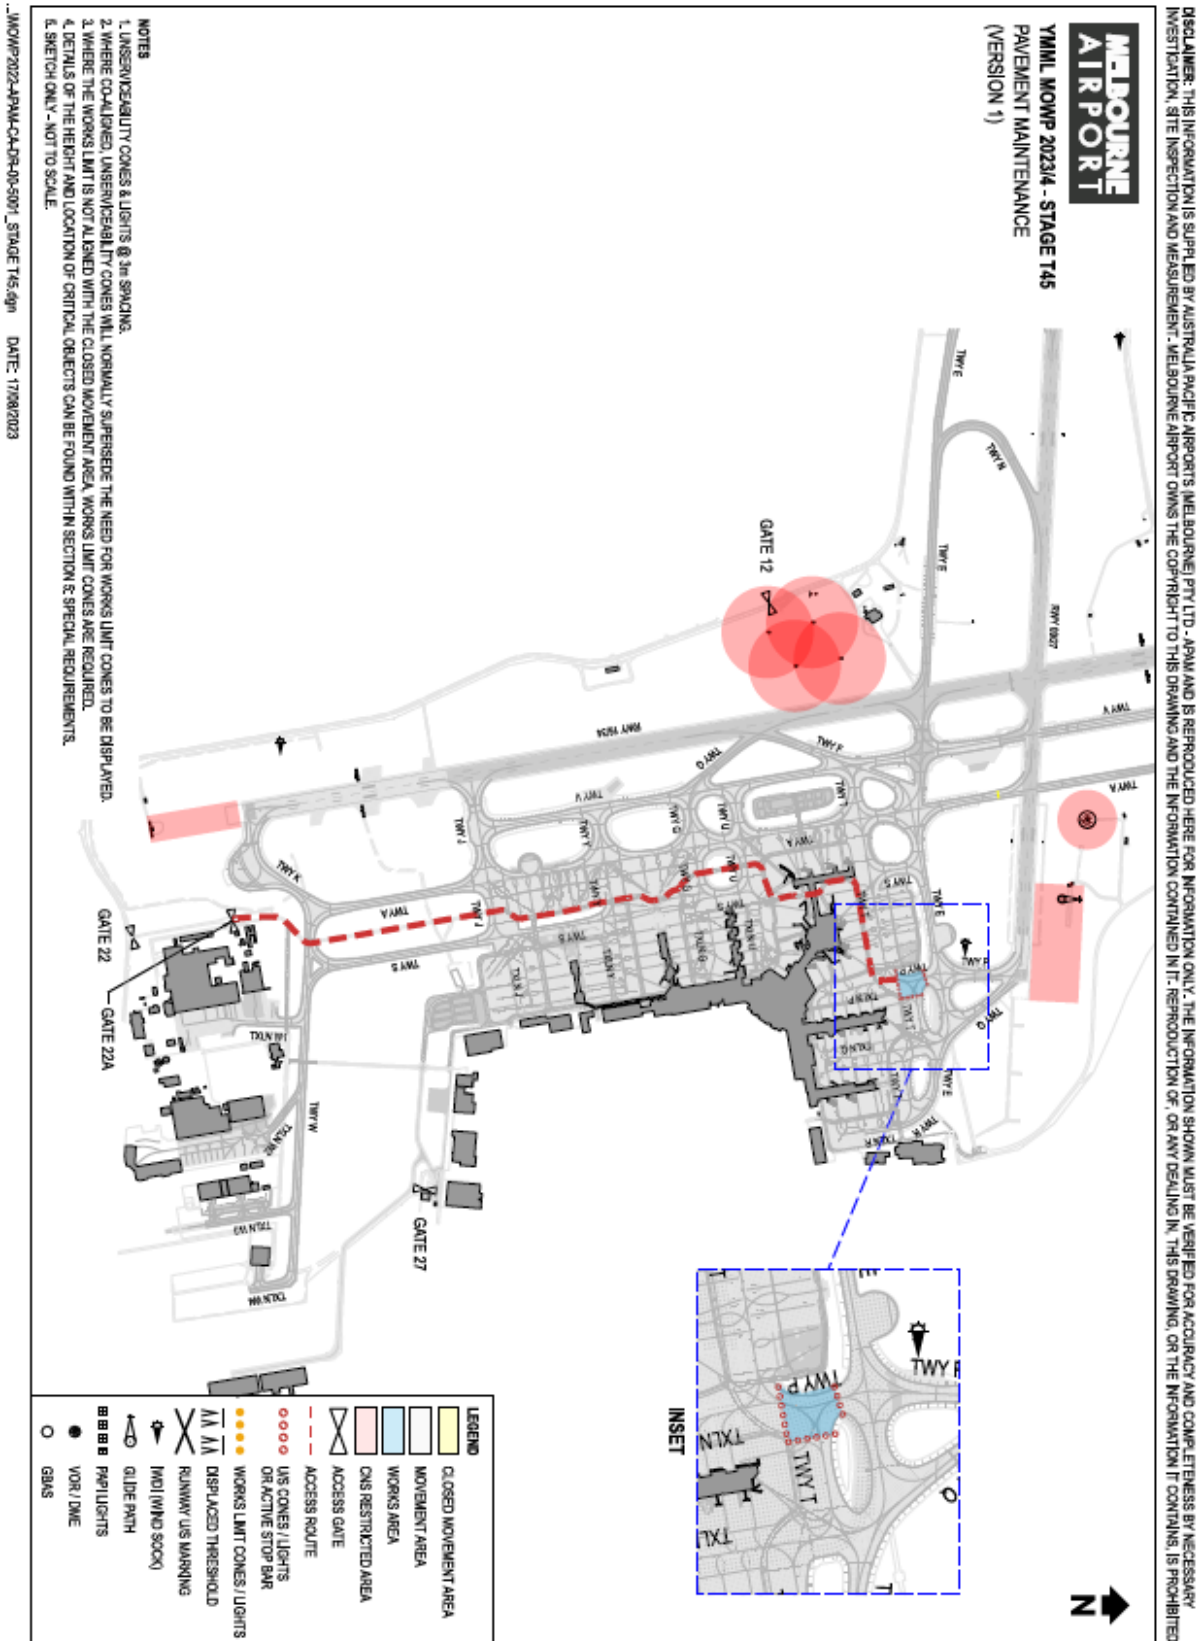


8.51. Stage T46




8.52. Stage T47

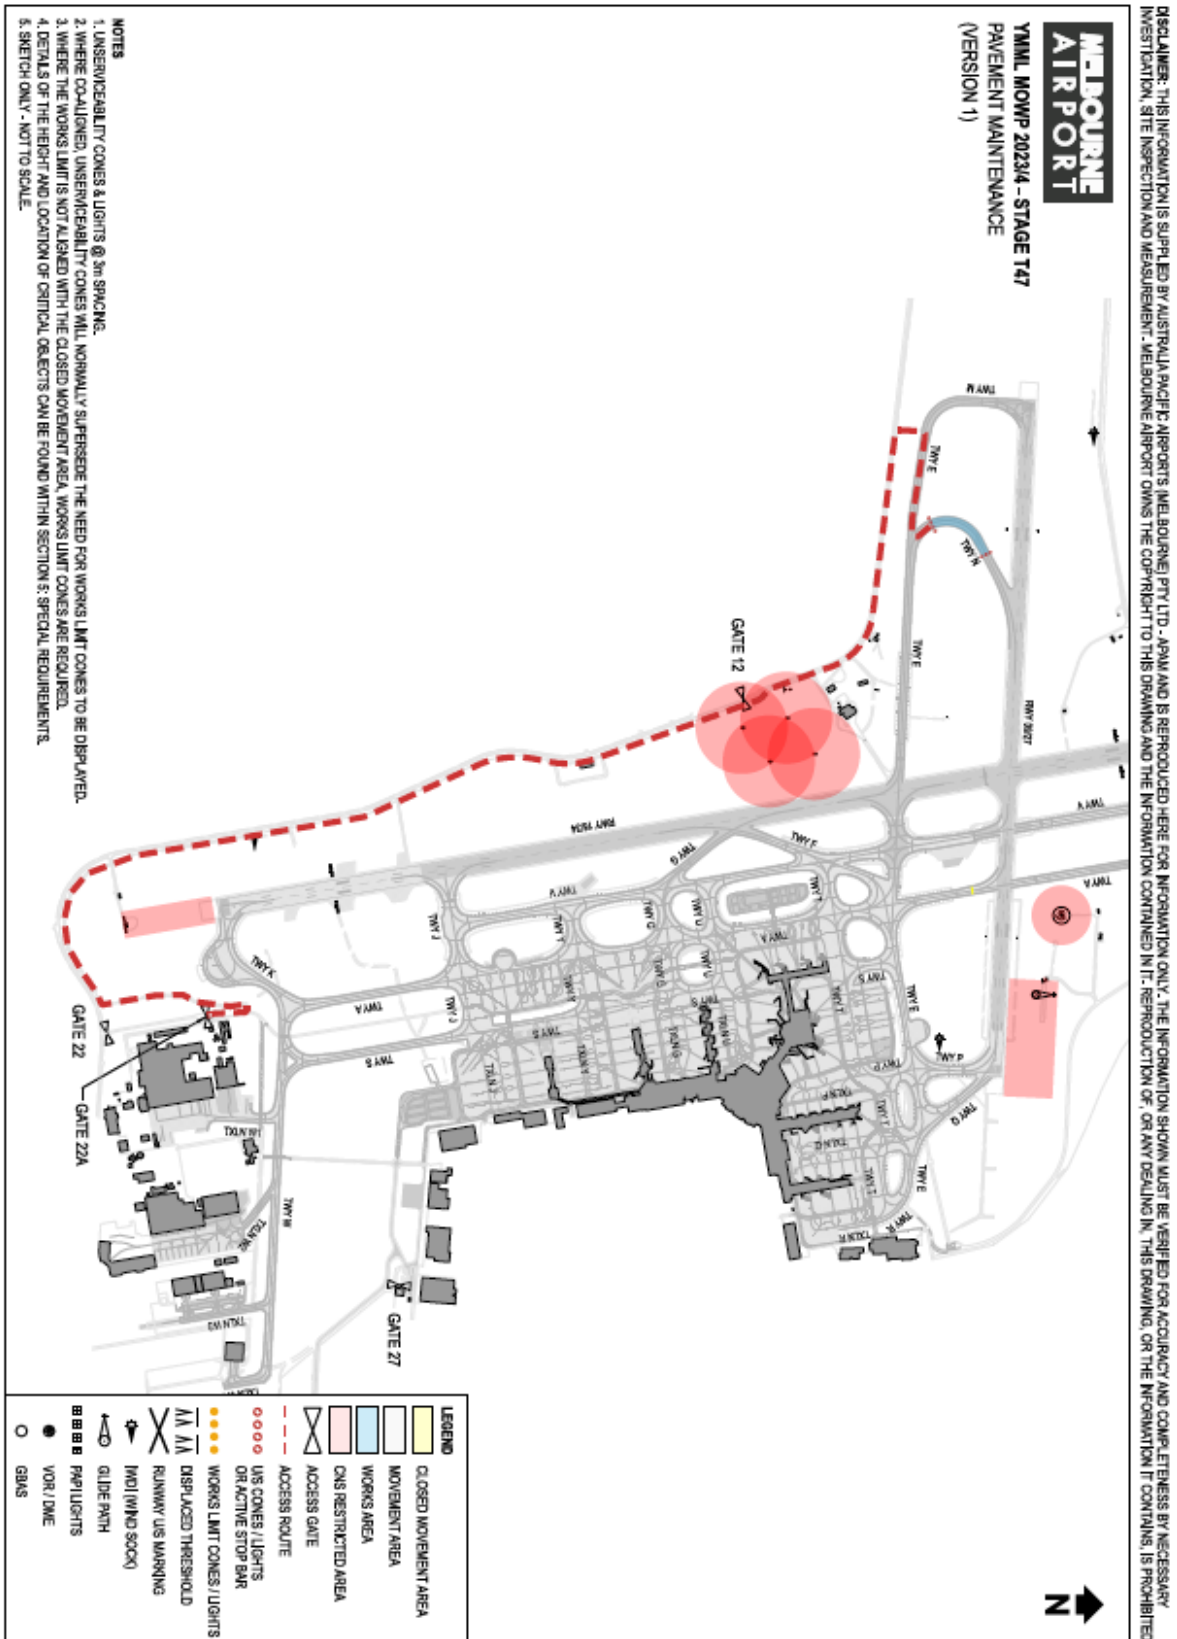


8.53. Stage T48

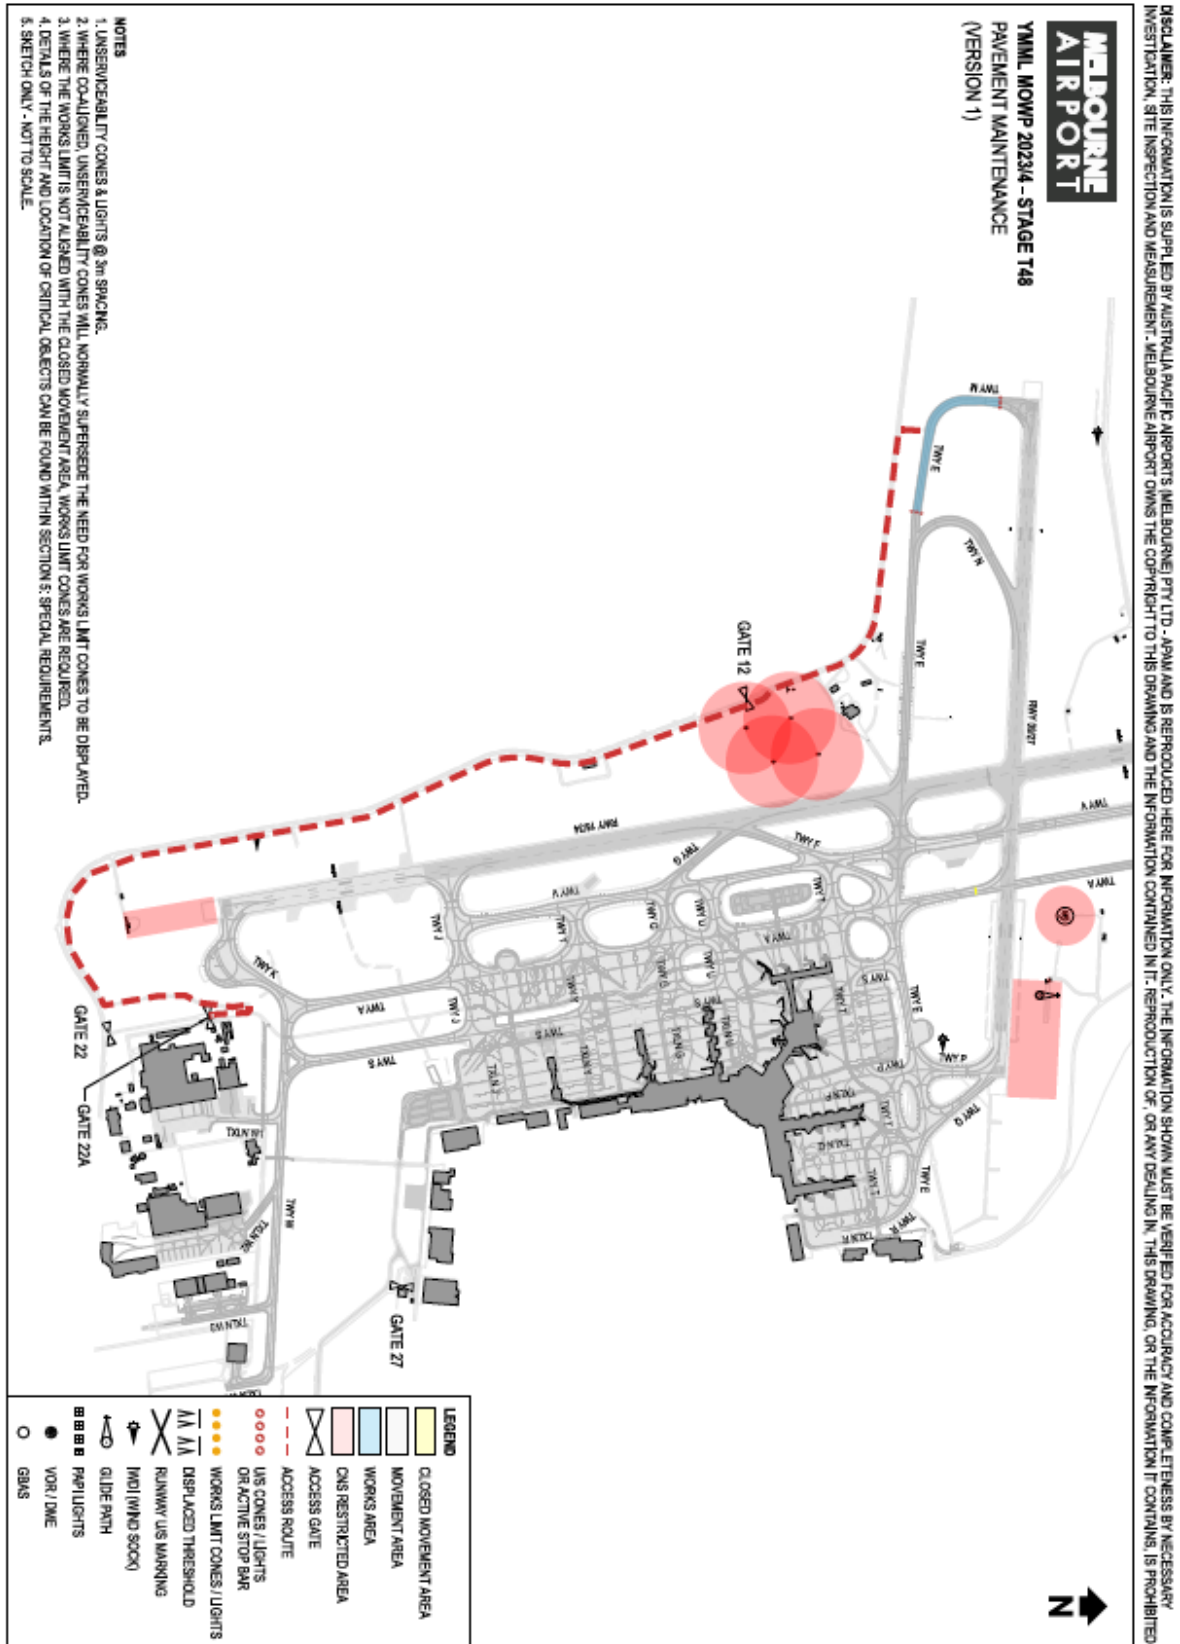


8.54. Stage T49

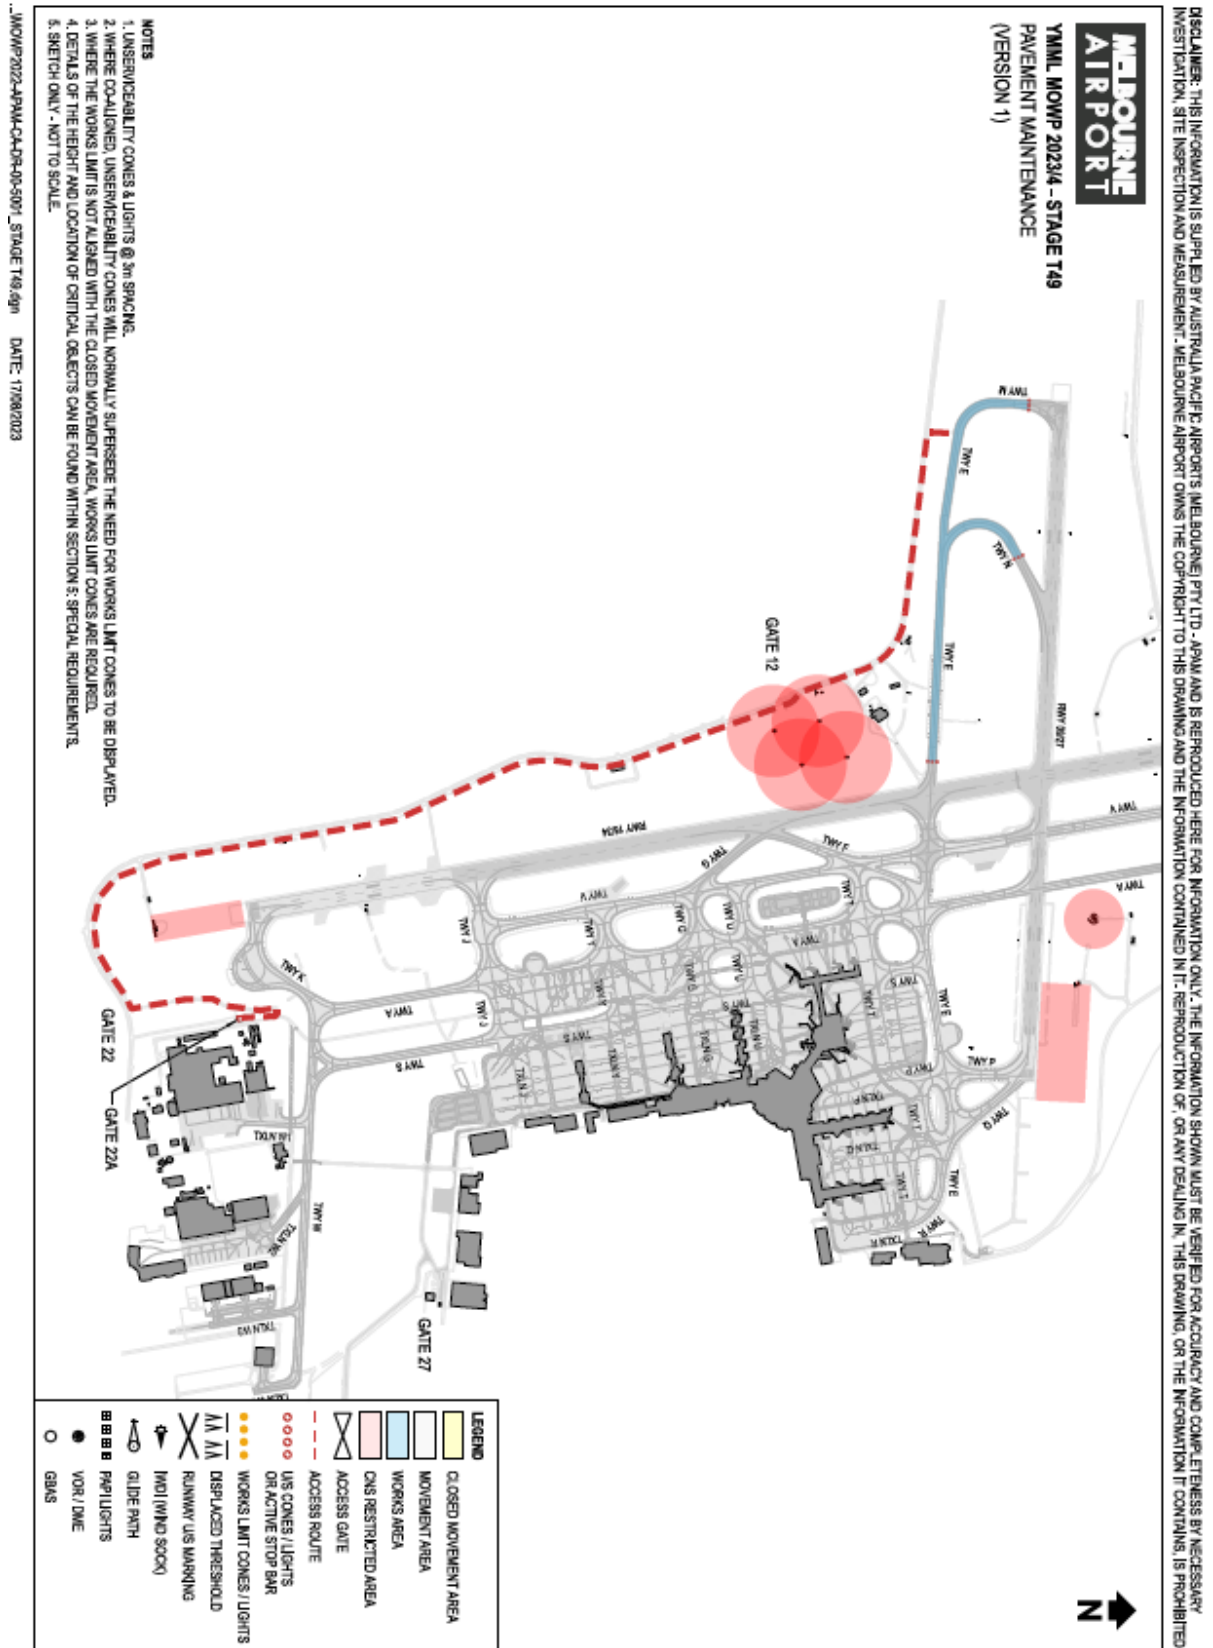


8.55. Stage T50

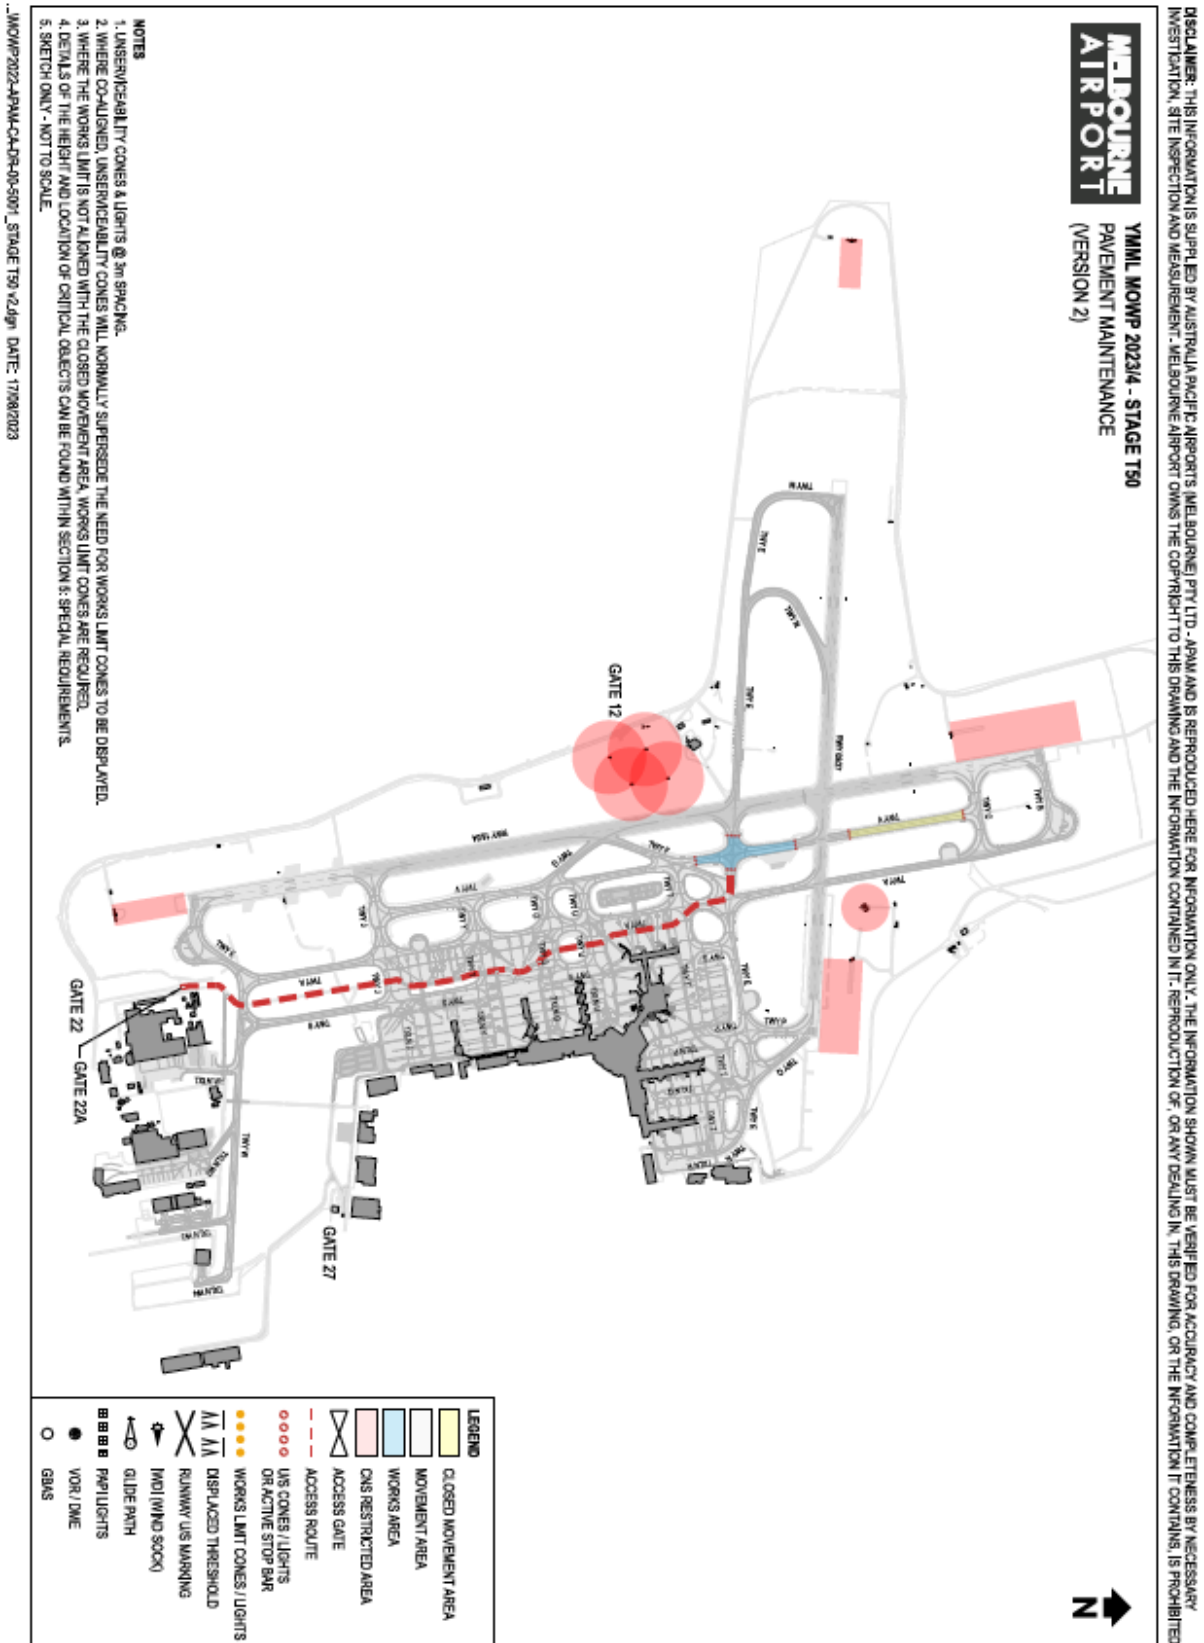


8.56. Stage T51

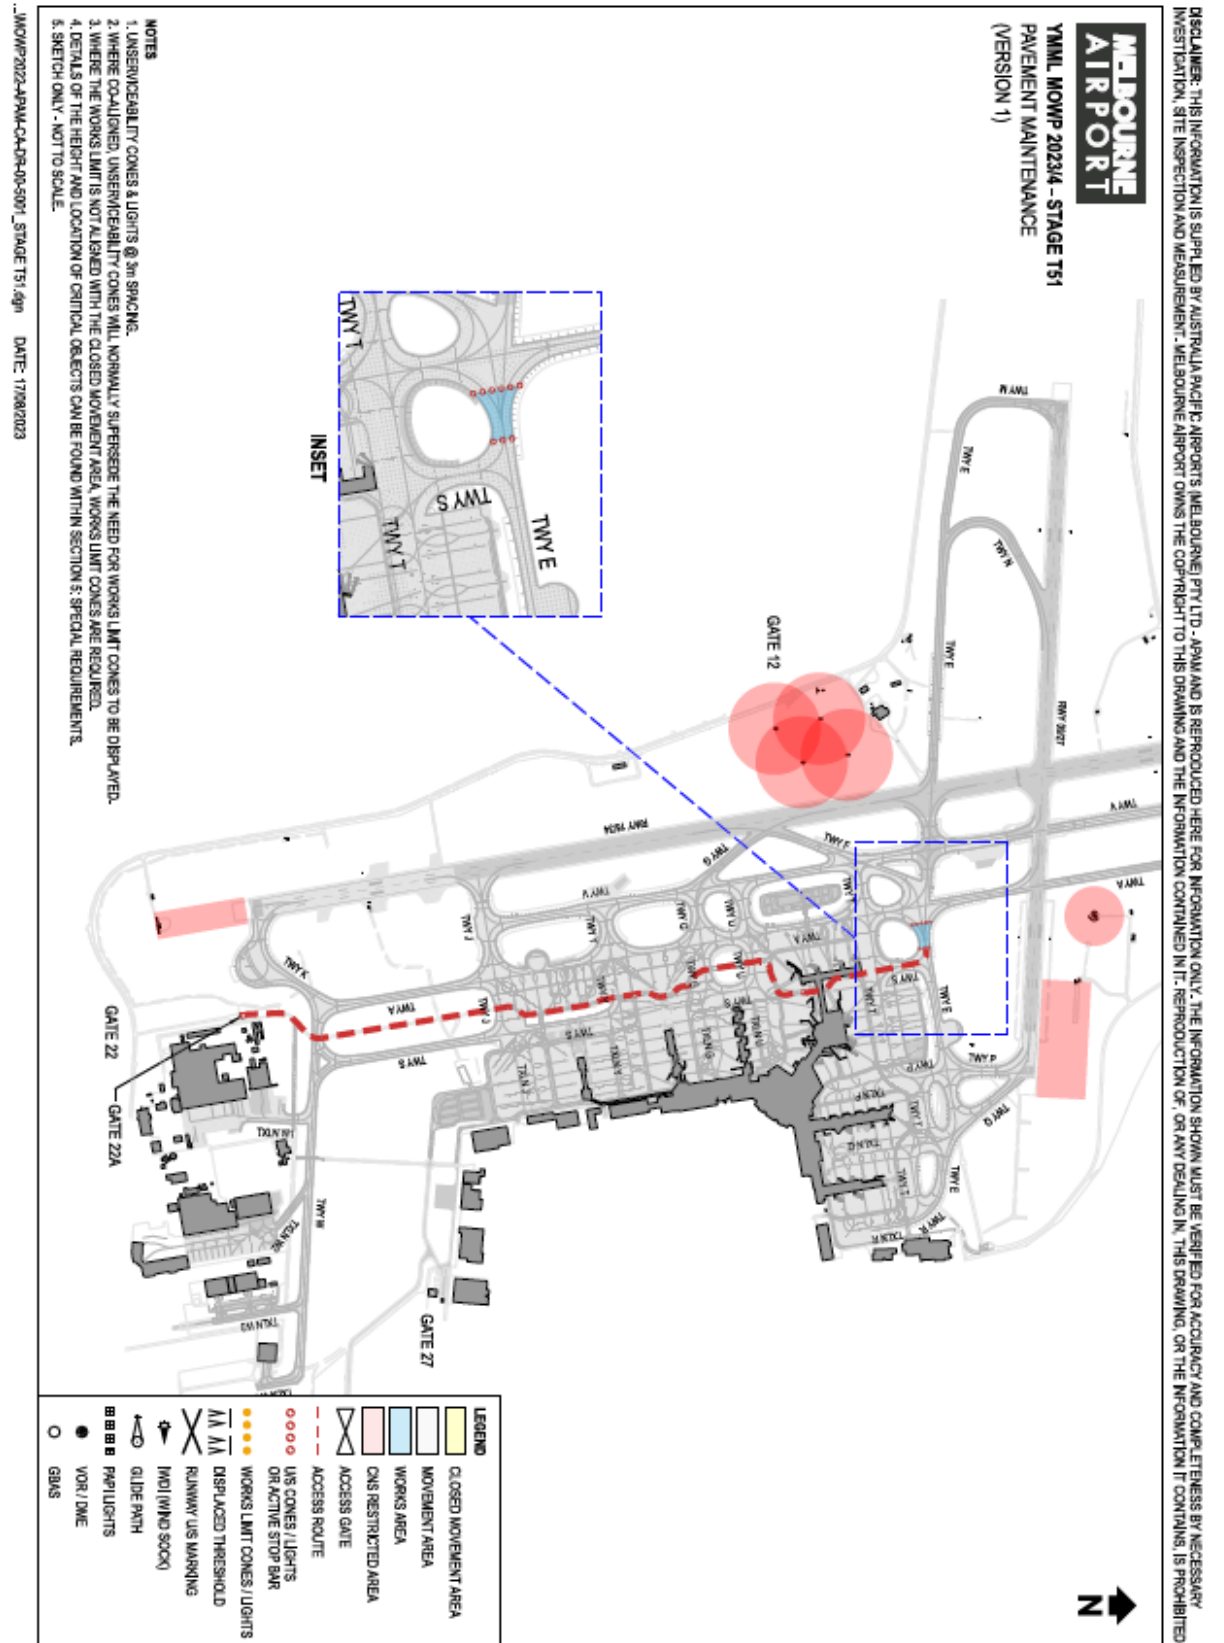


8.57. Stage T52

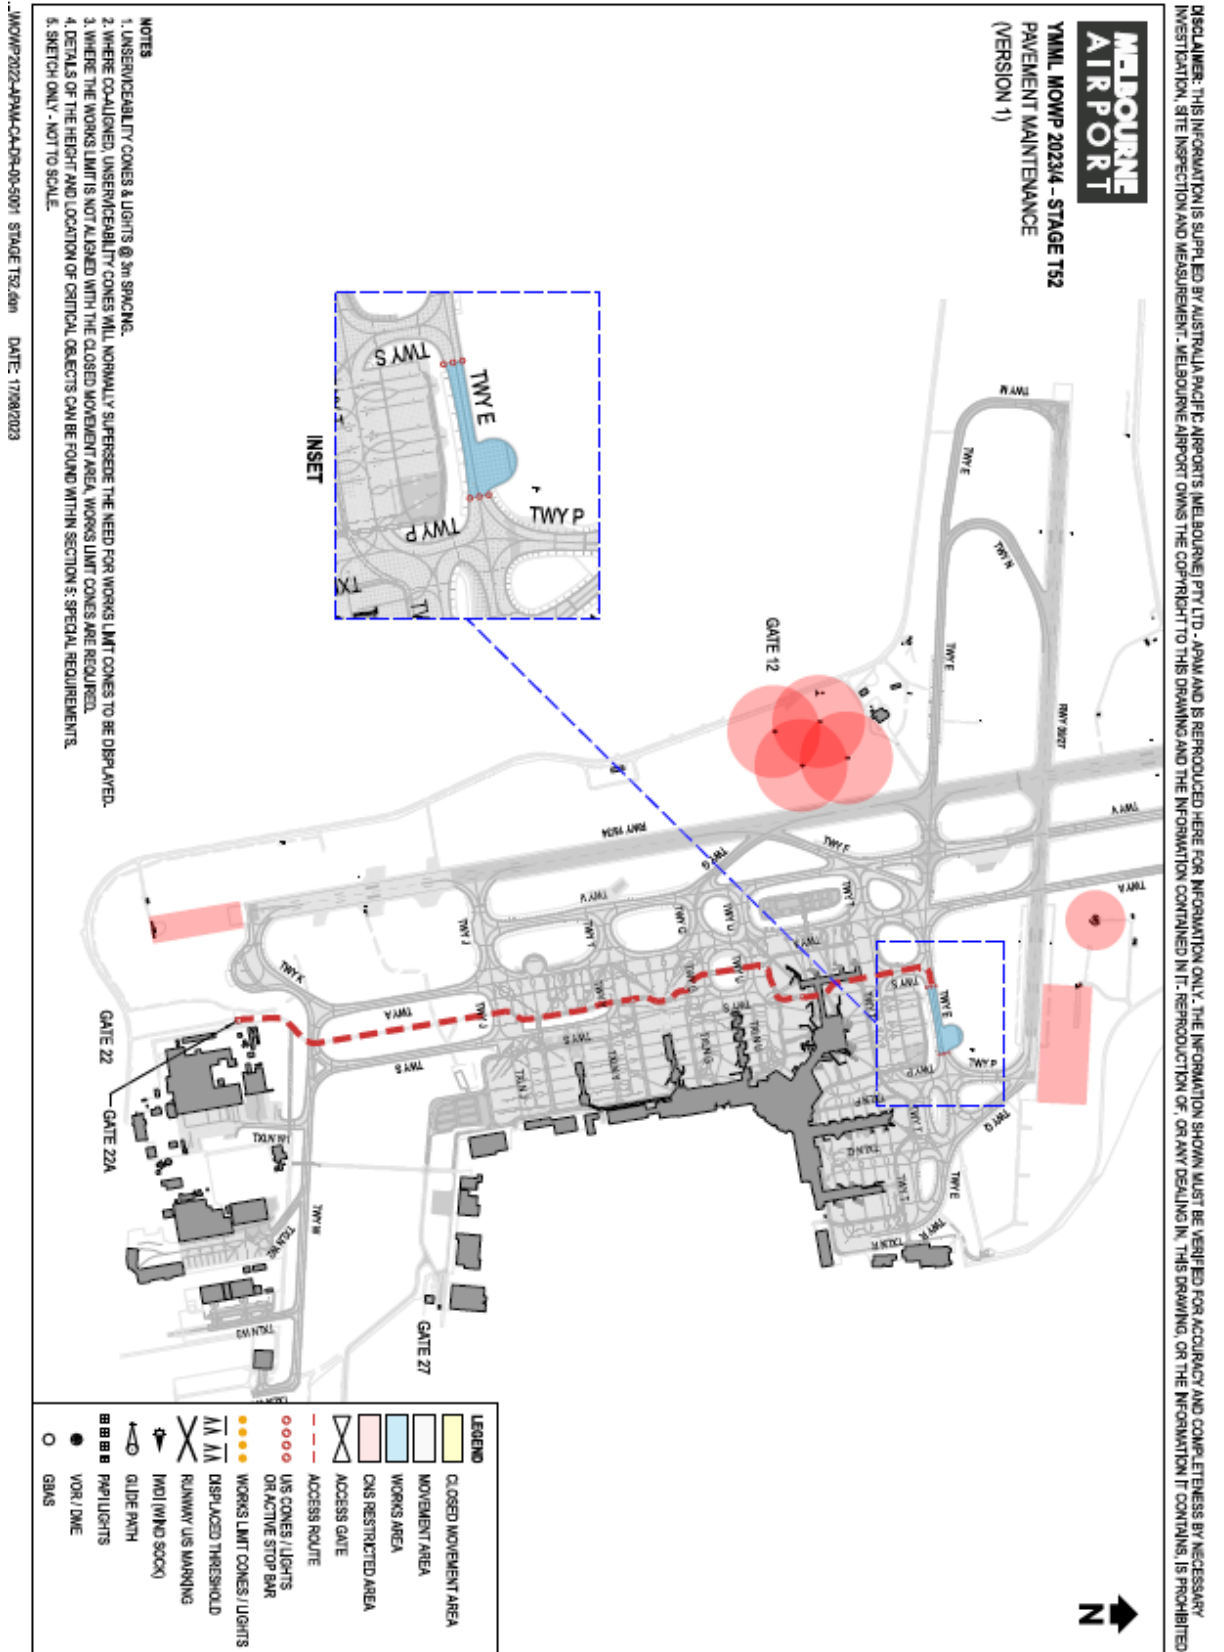


8.58. Stage T53

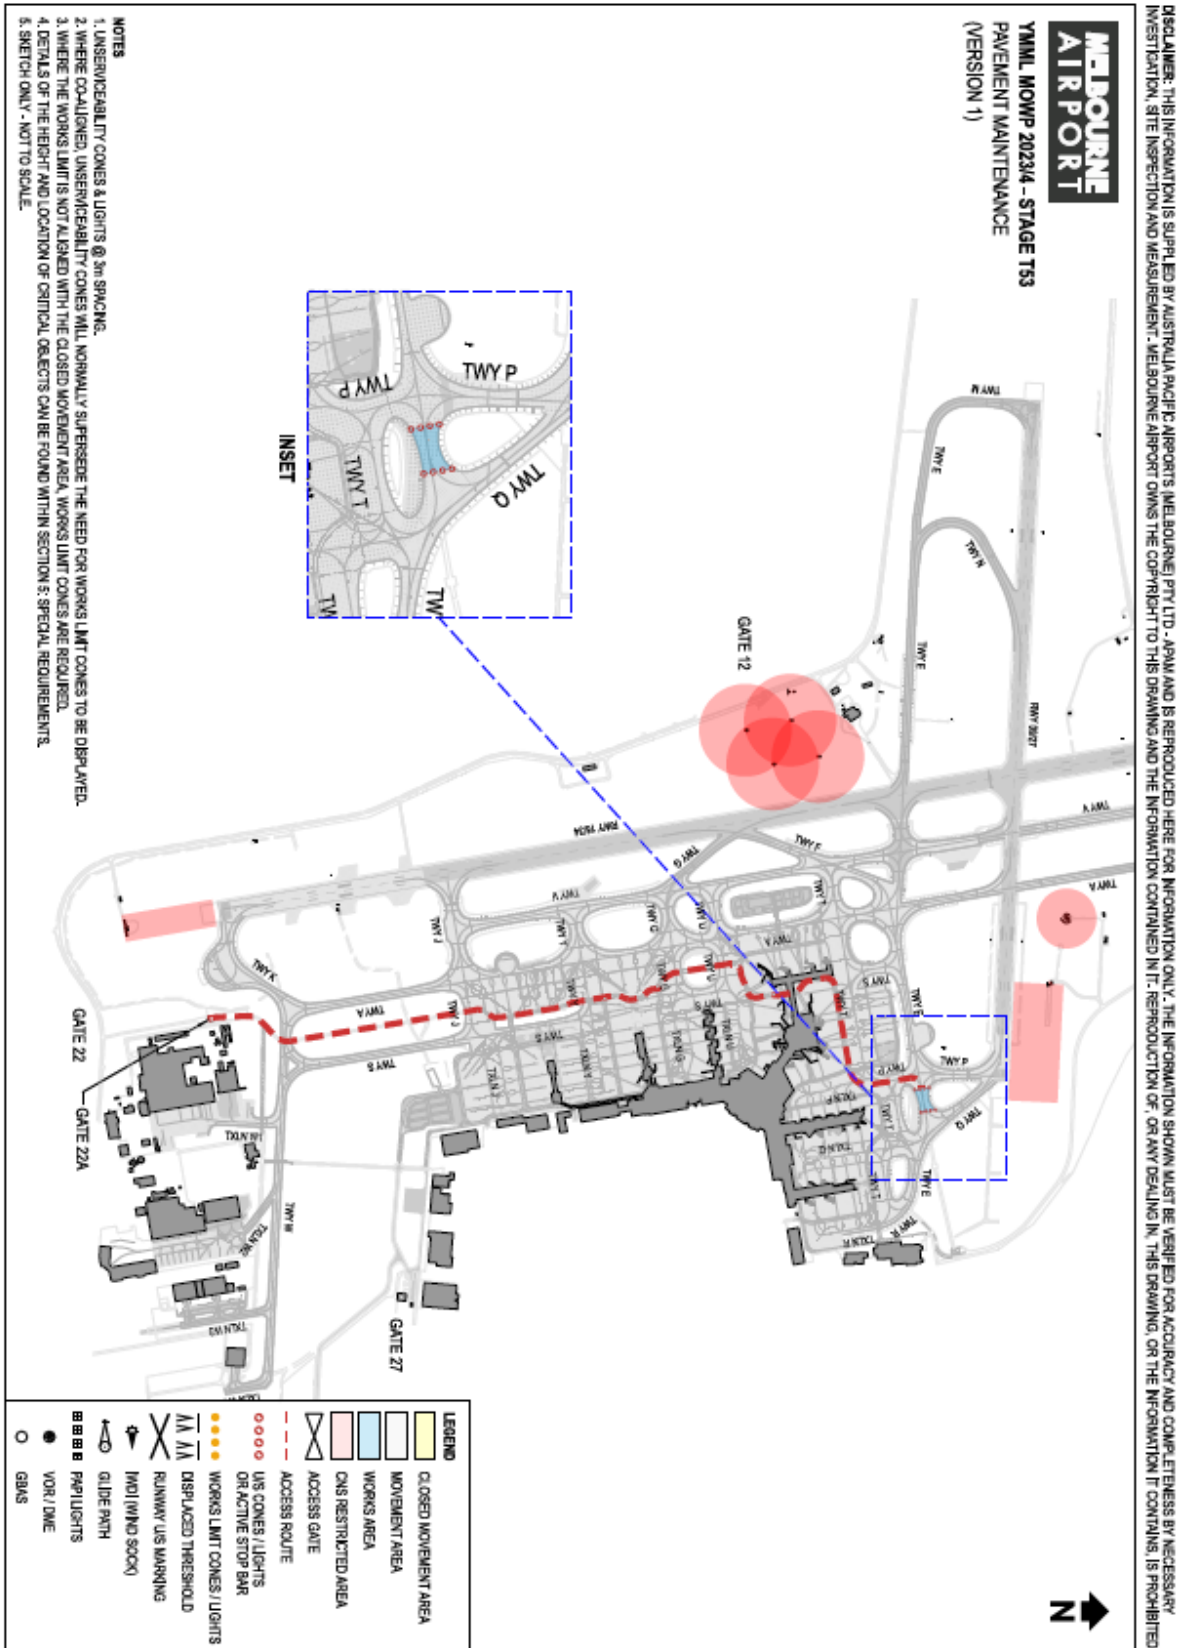


8.59. Stage T54

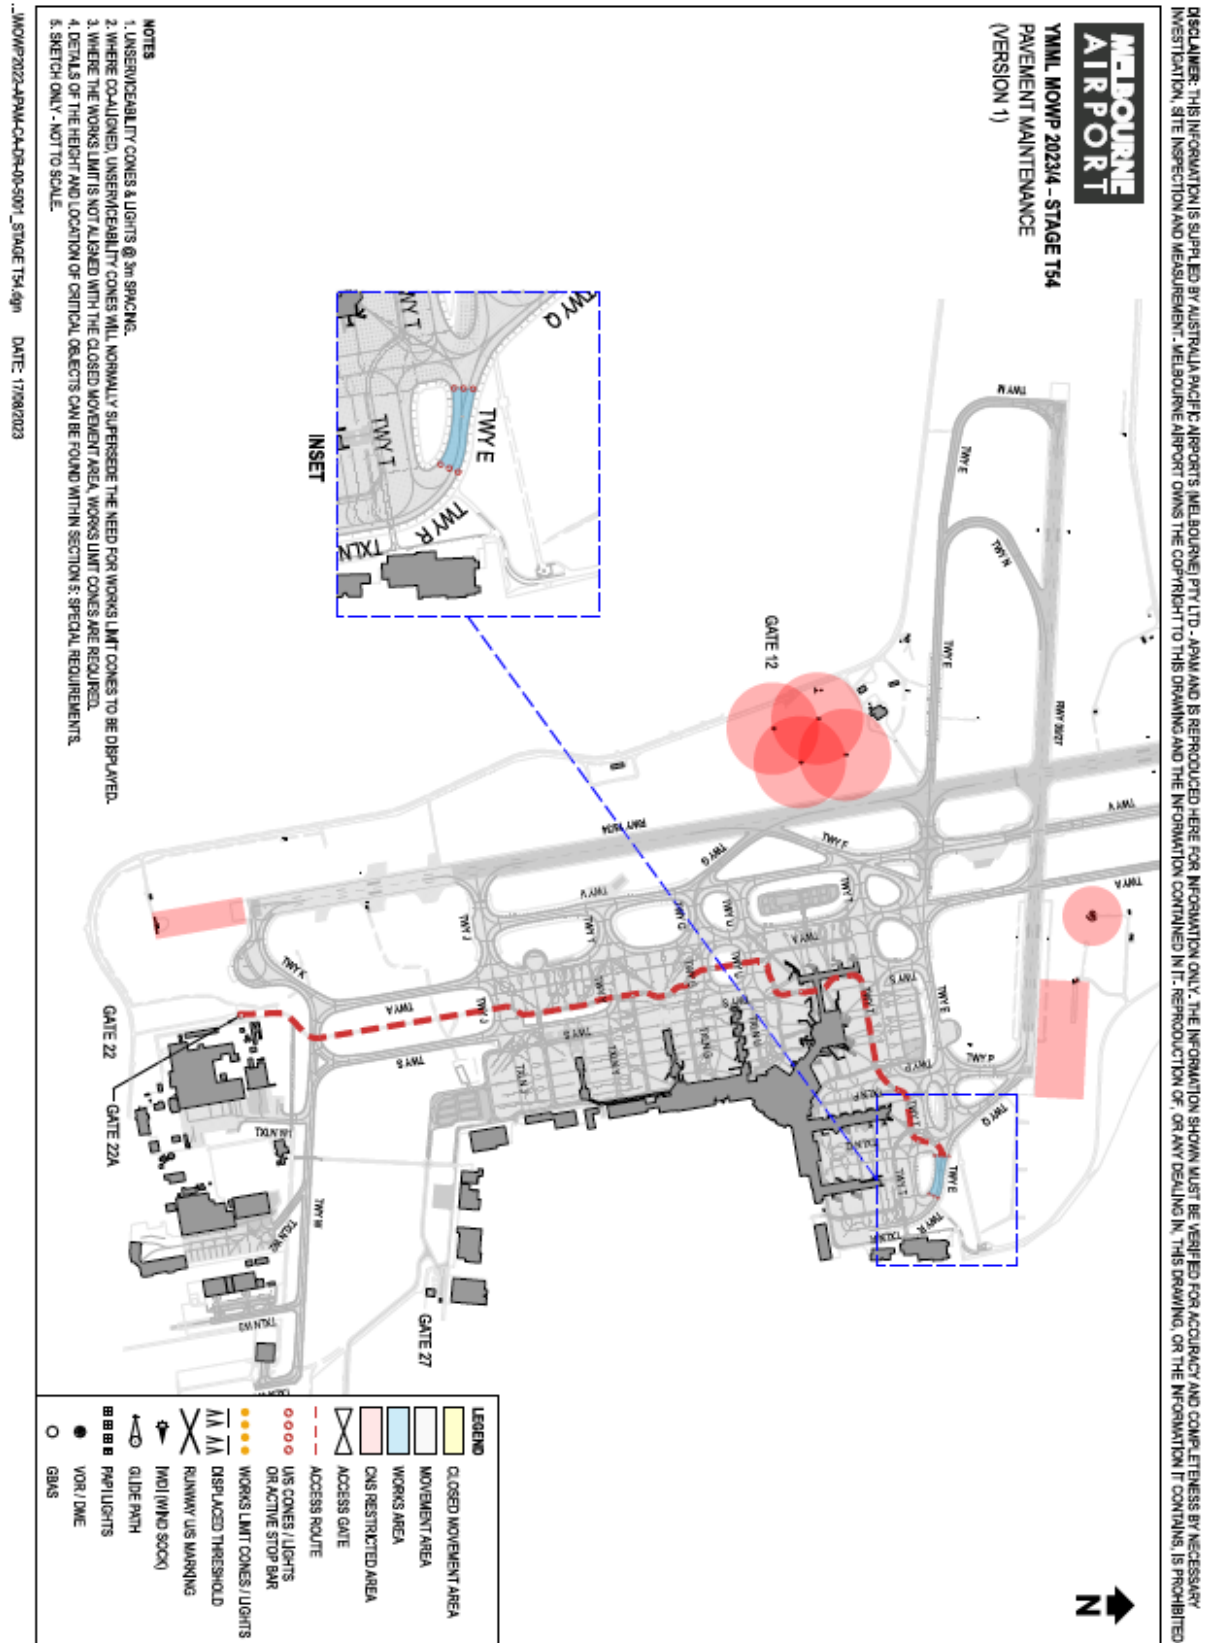


8.60. Stage T55

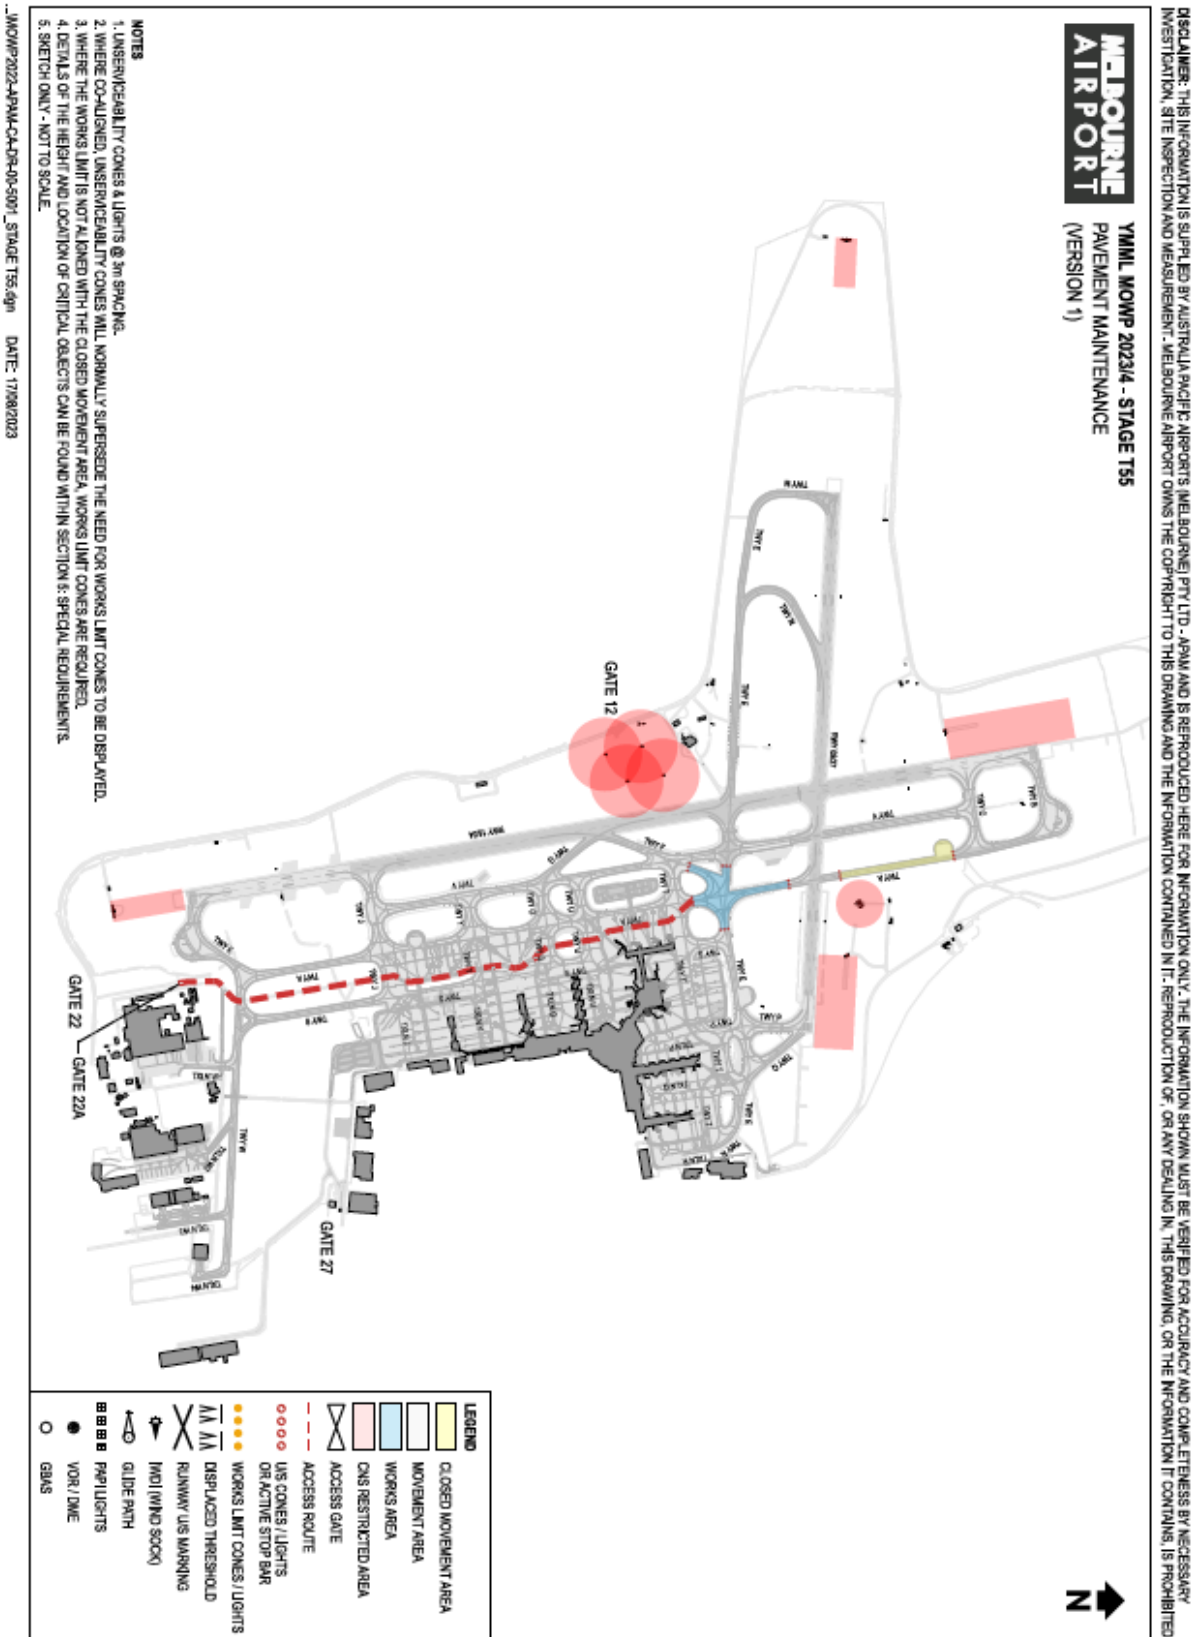


8.61. Stage T56

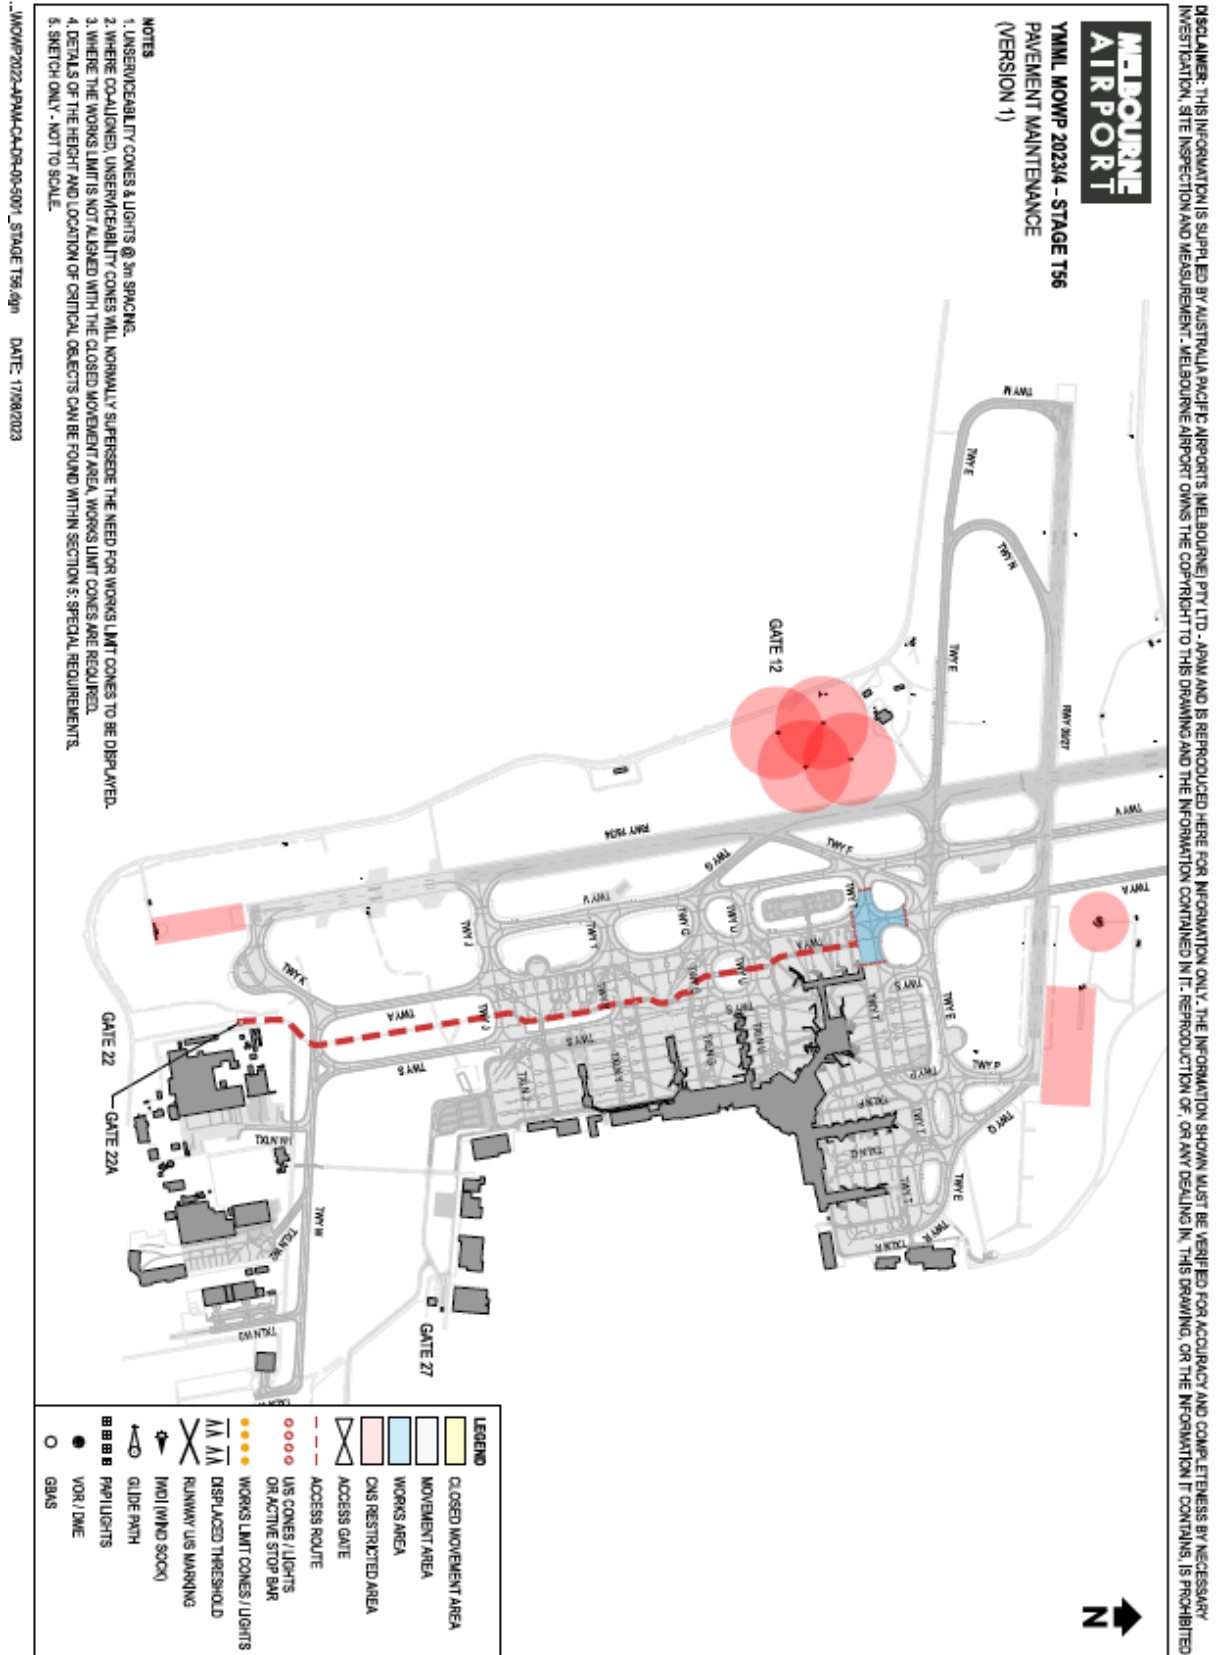


8.62. Stage T57

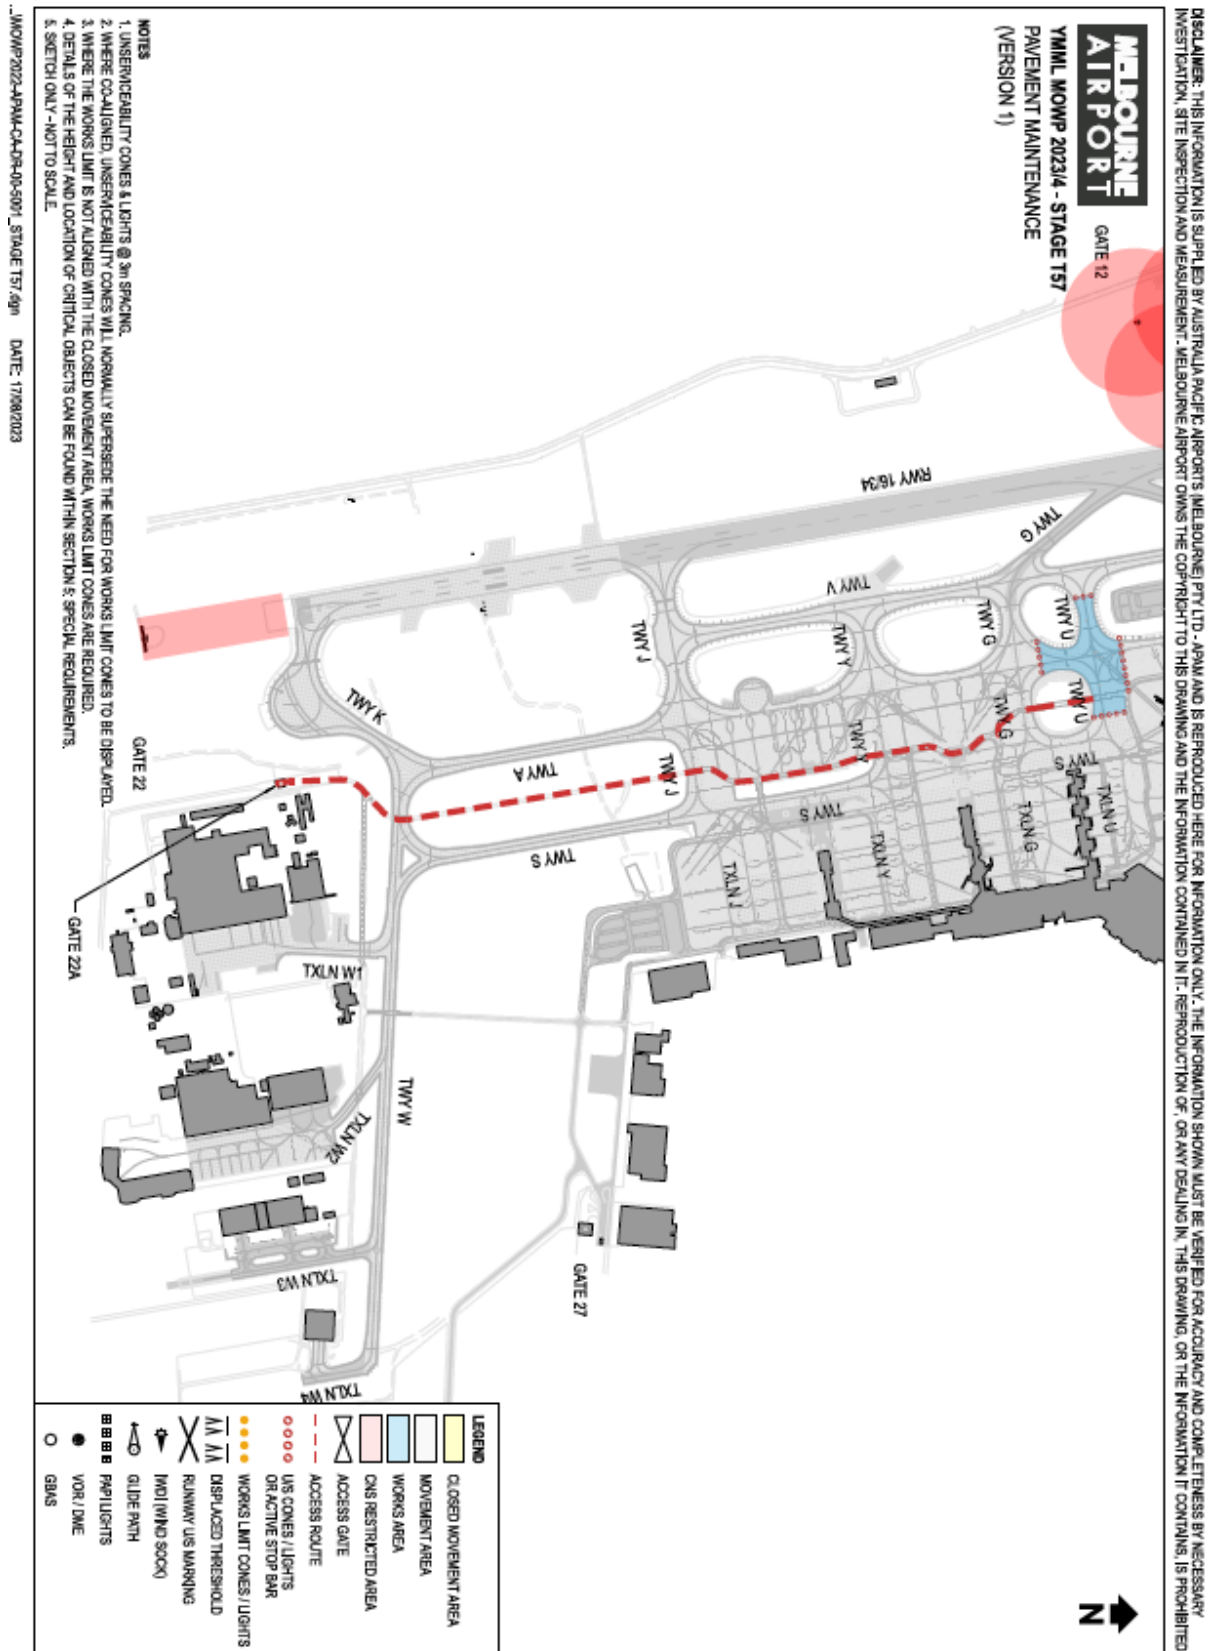


8.63. Stage T58

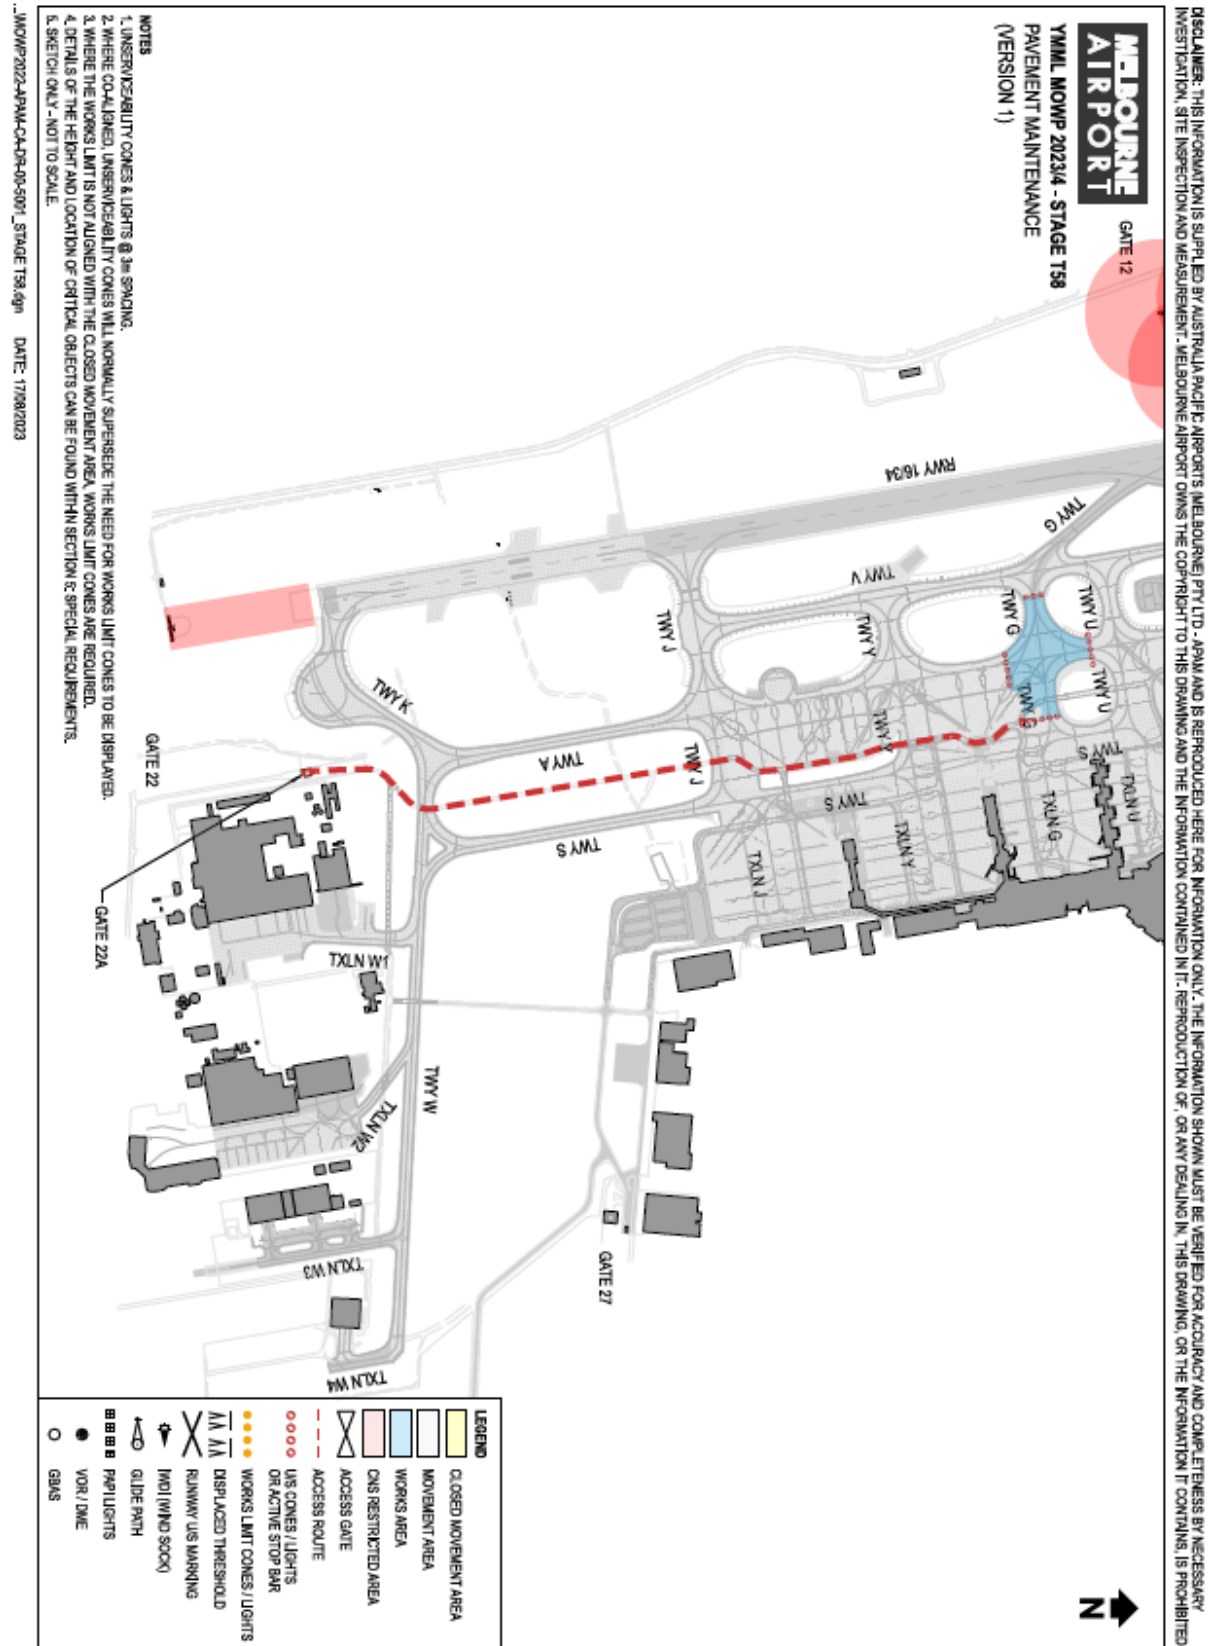


8.64. Stage T59

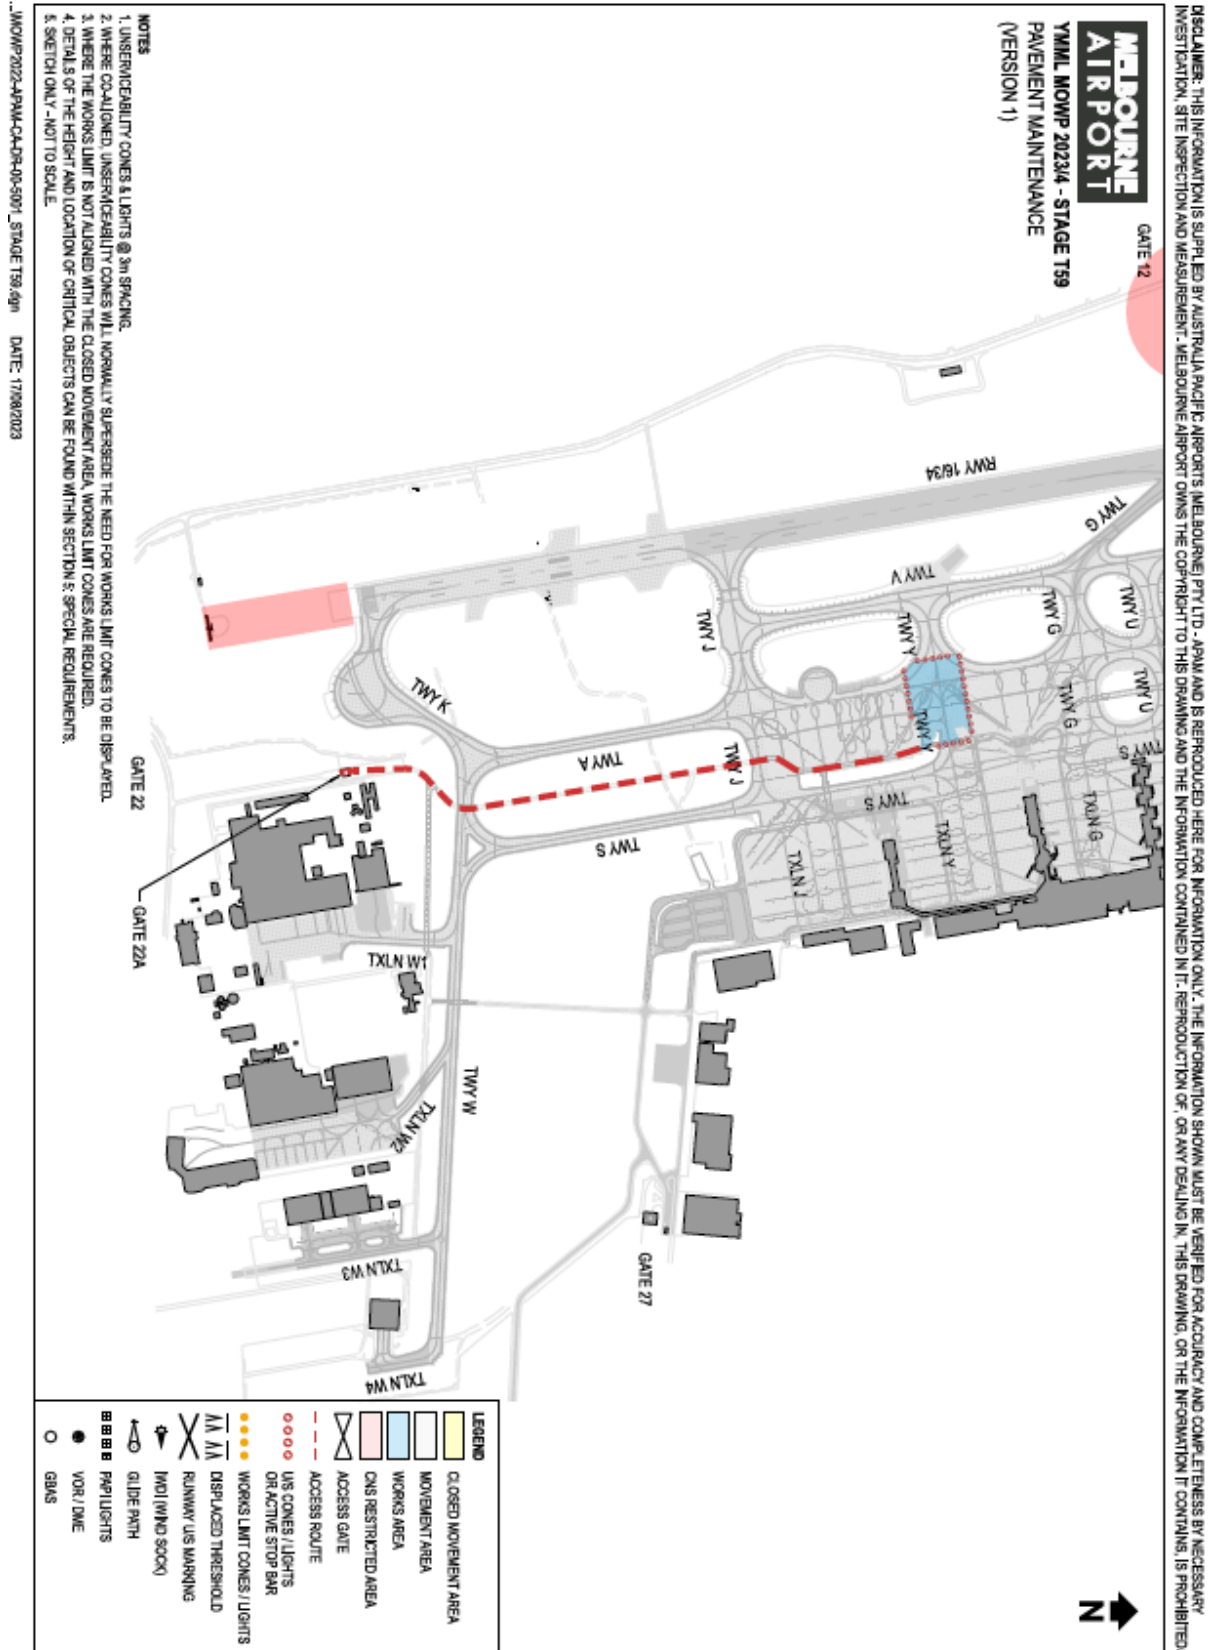


8.65. Stage T60

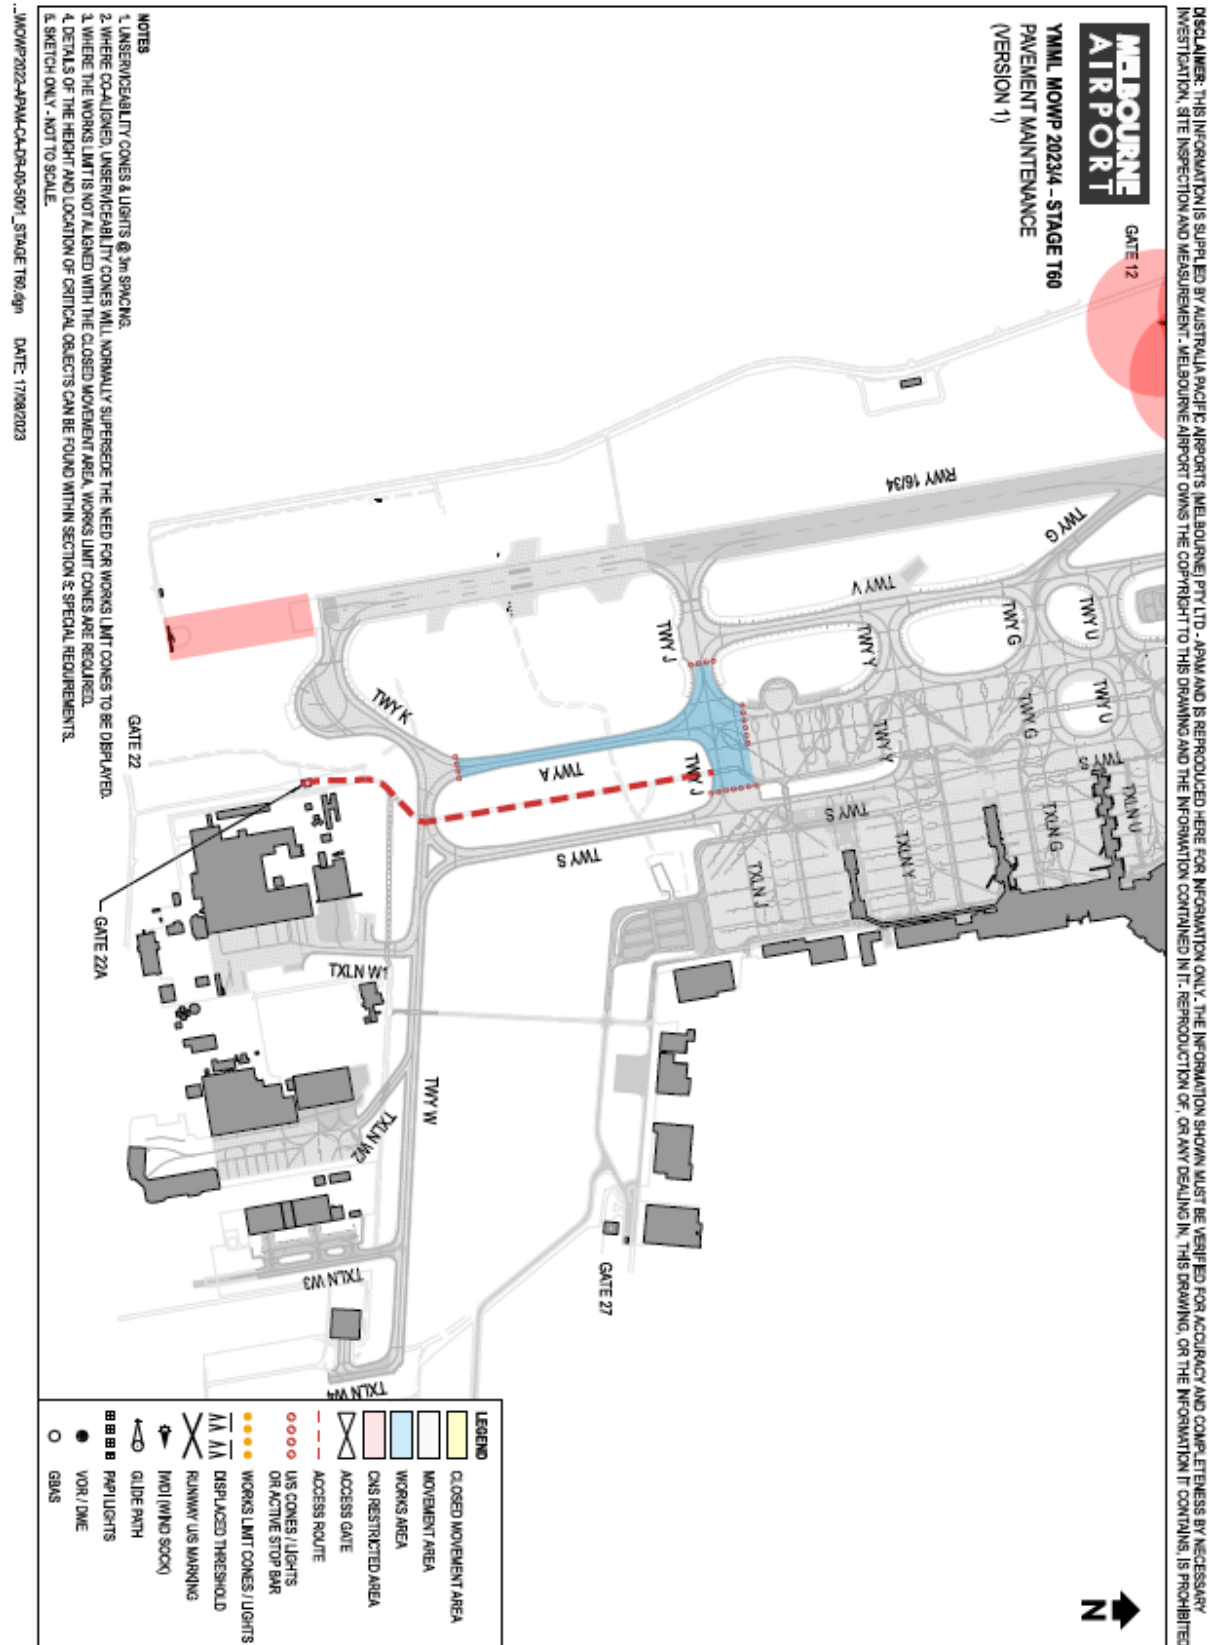


8.66. Stage T61

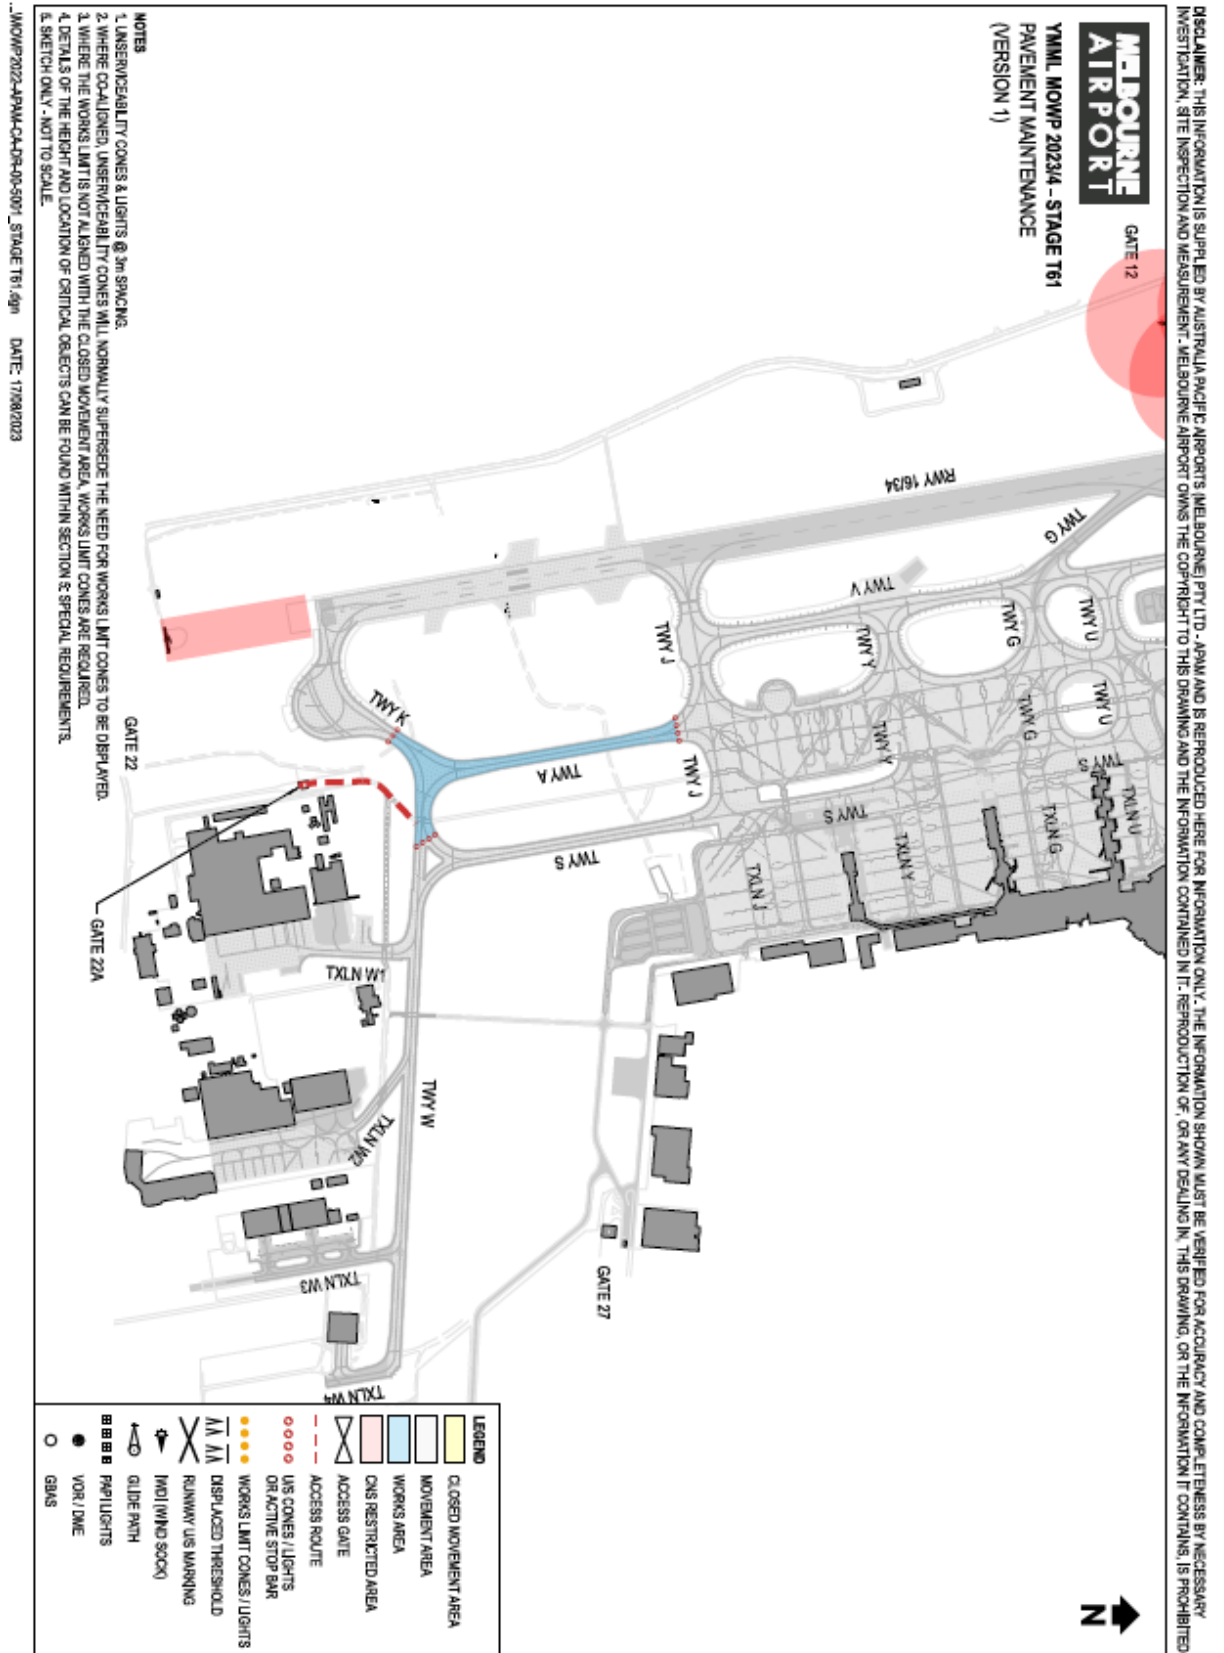


8.67. Stage T62

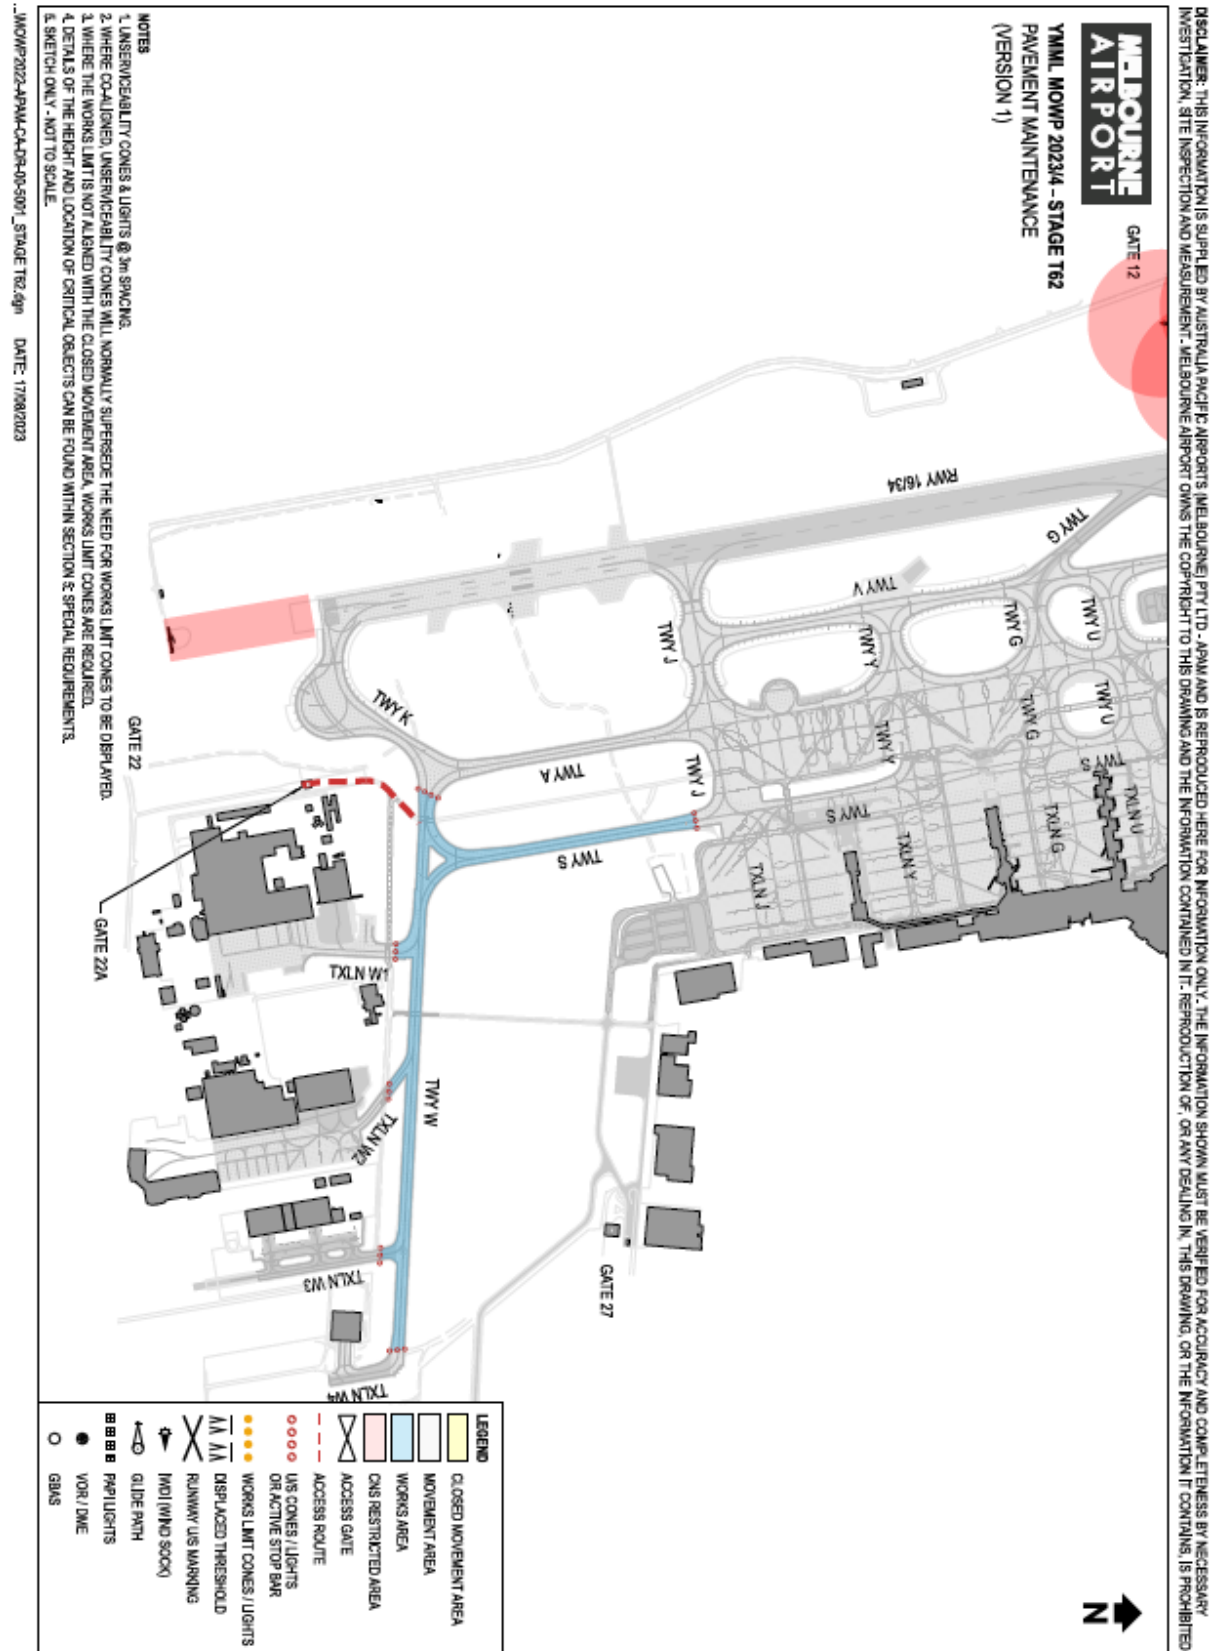


8.68. Stage T63

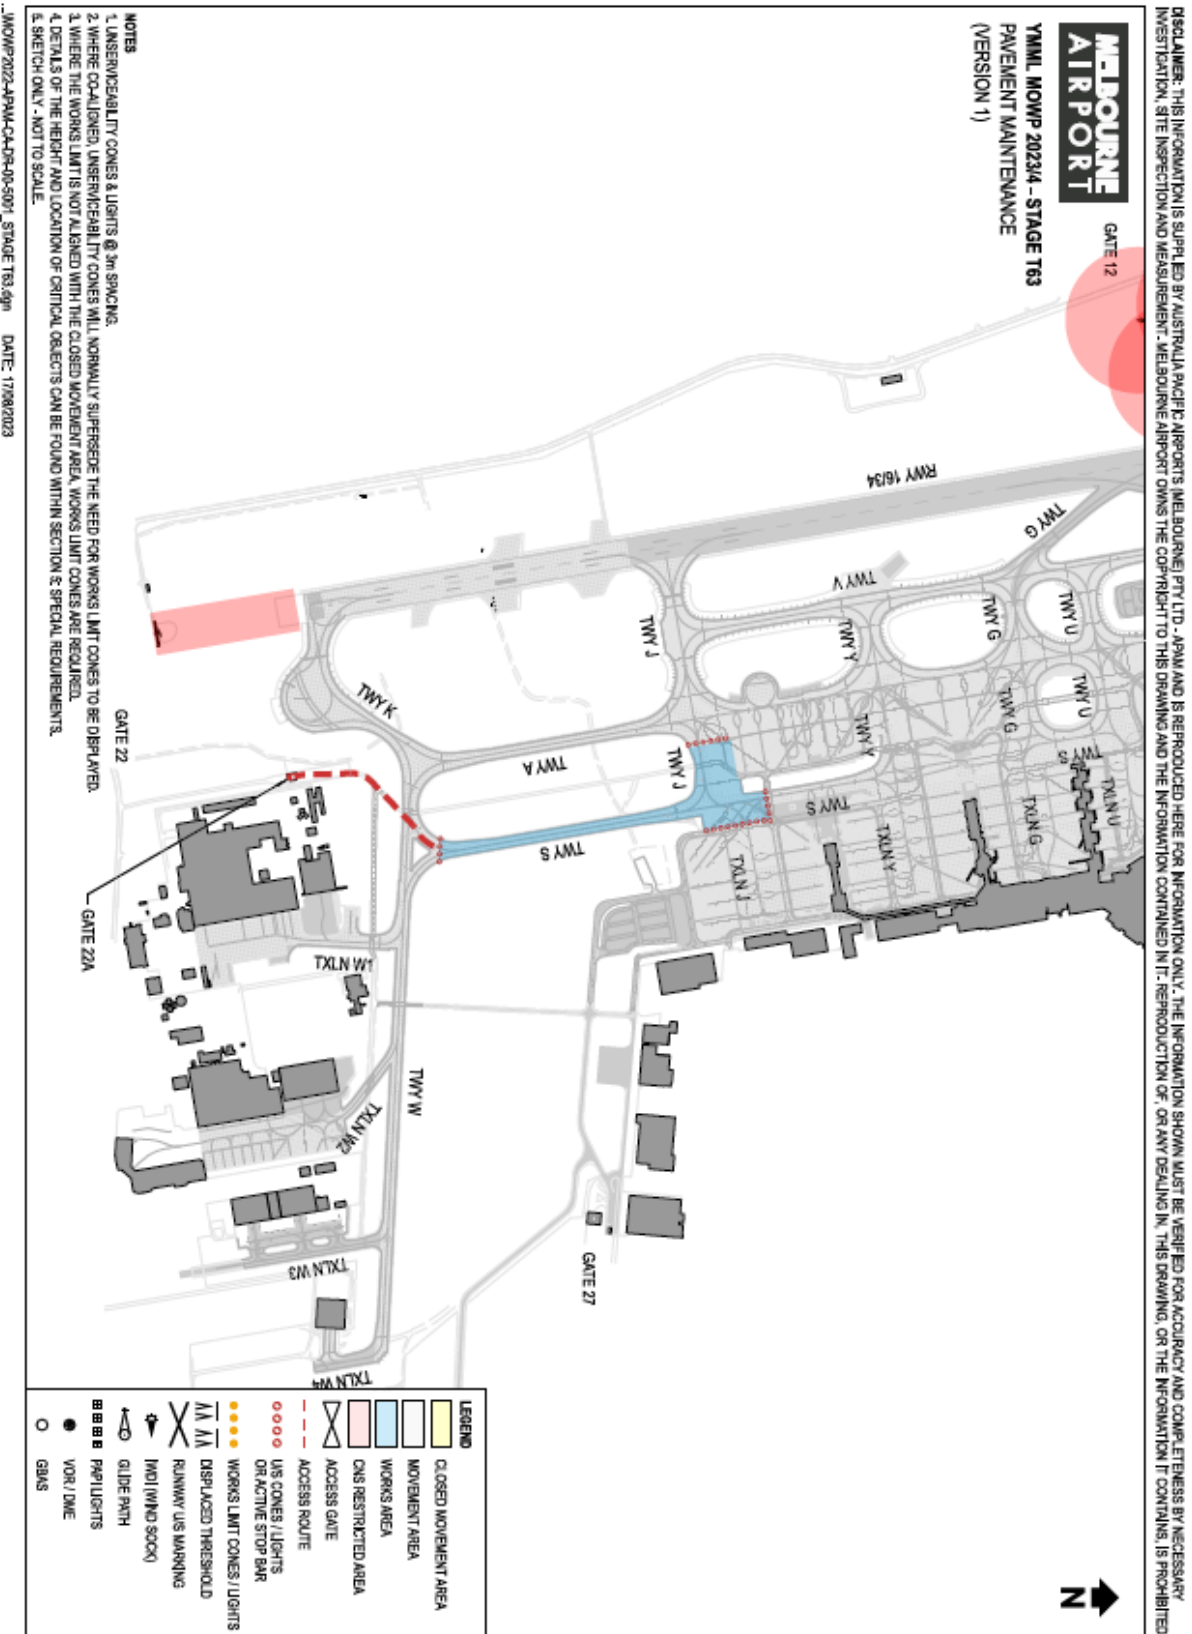


8.69. Stage T64

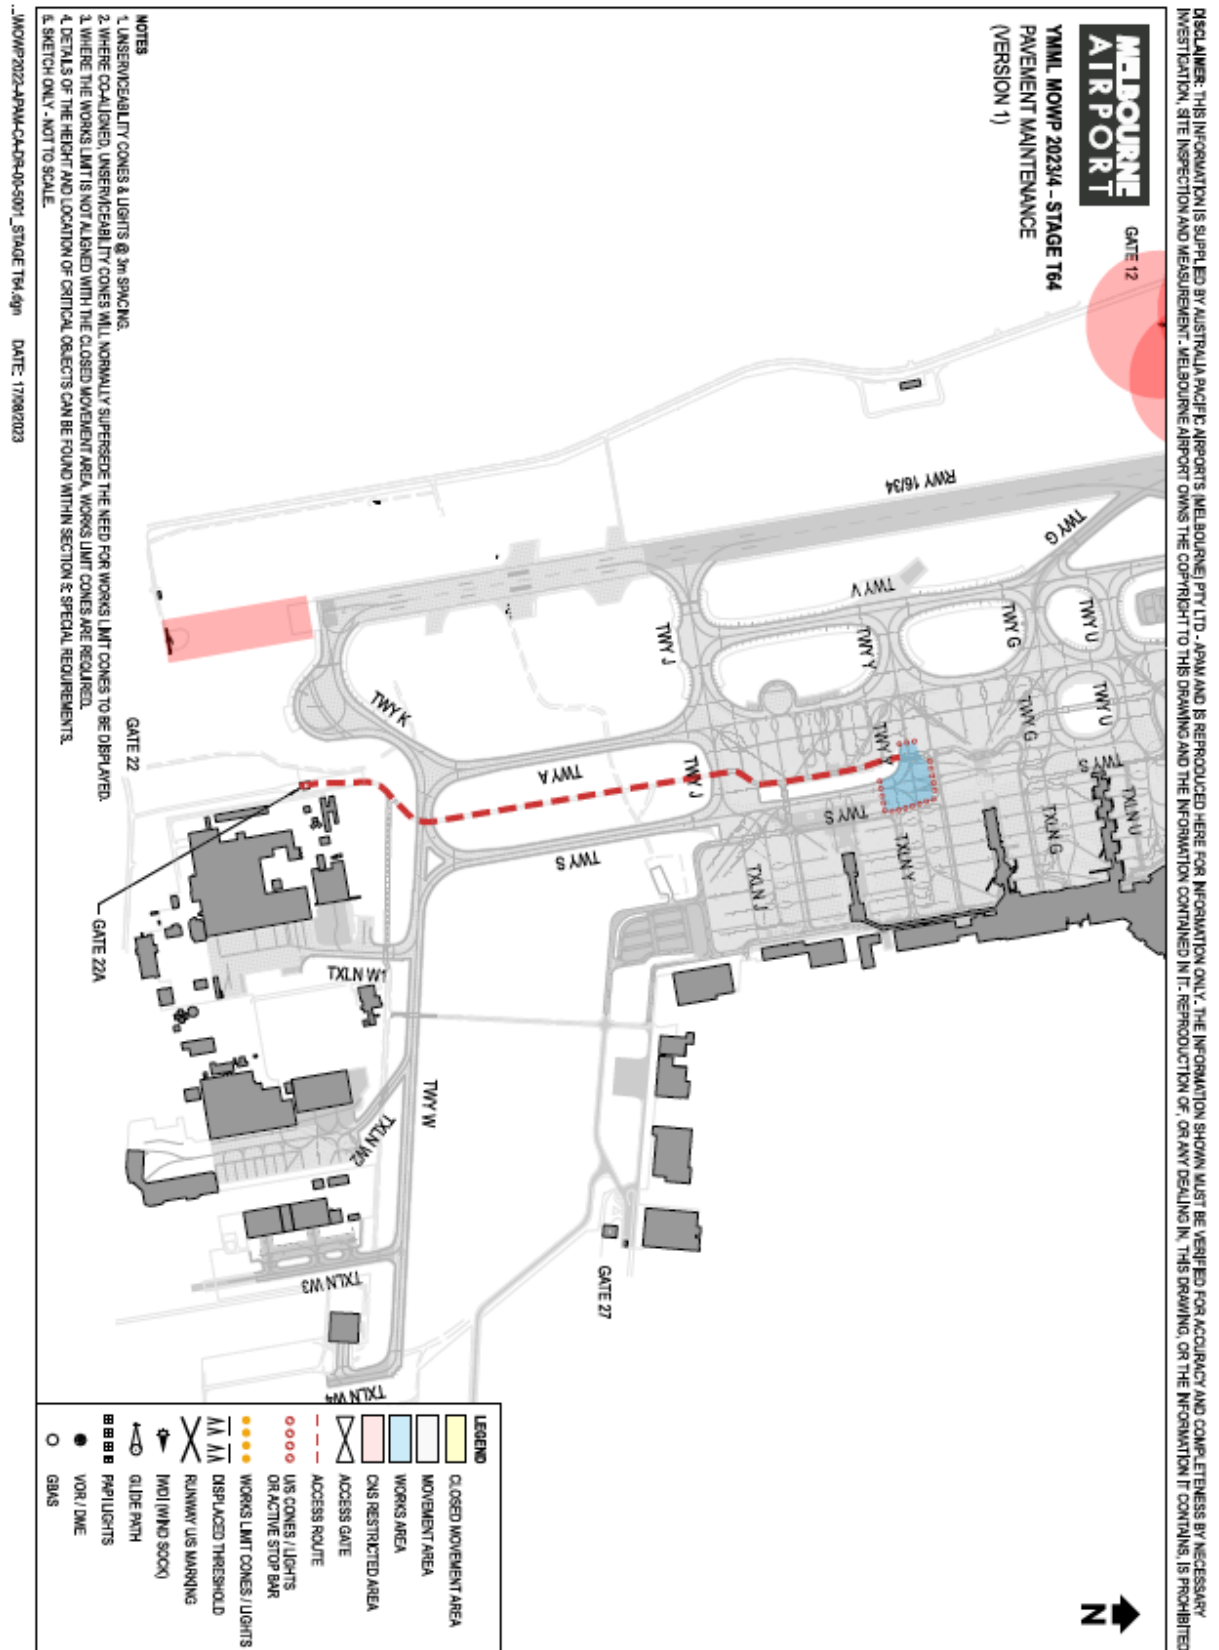


8.70. Stage T65

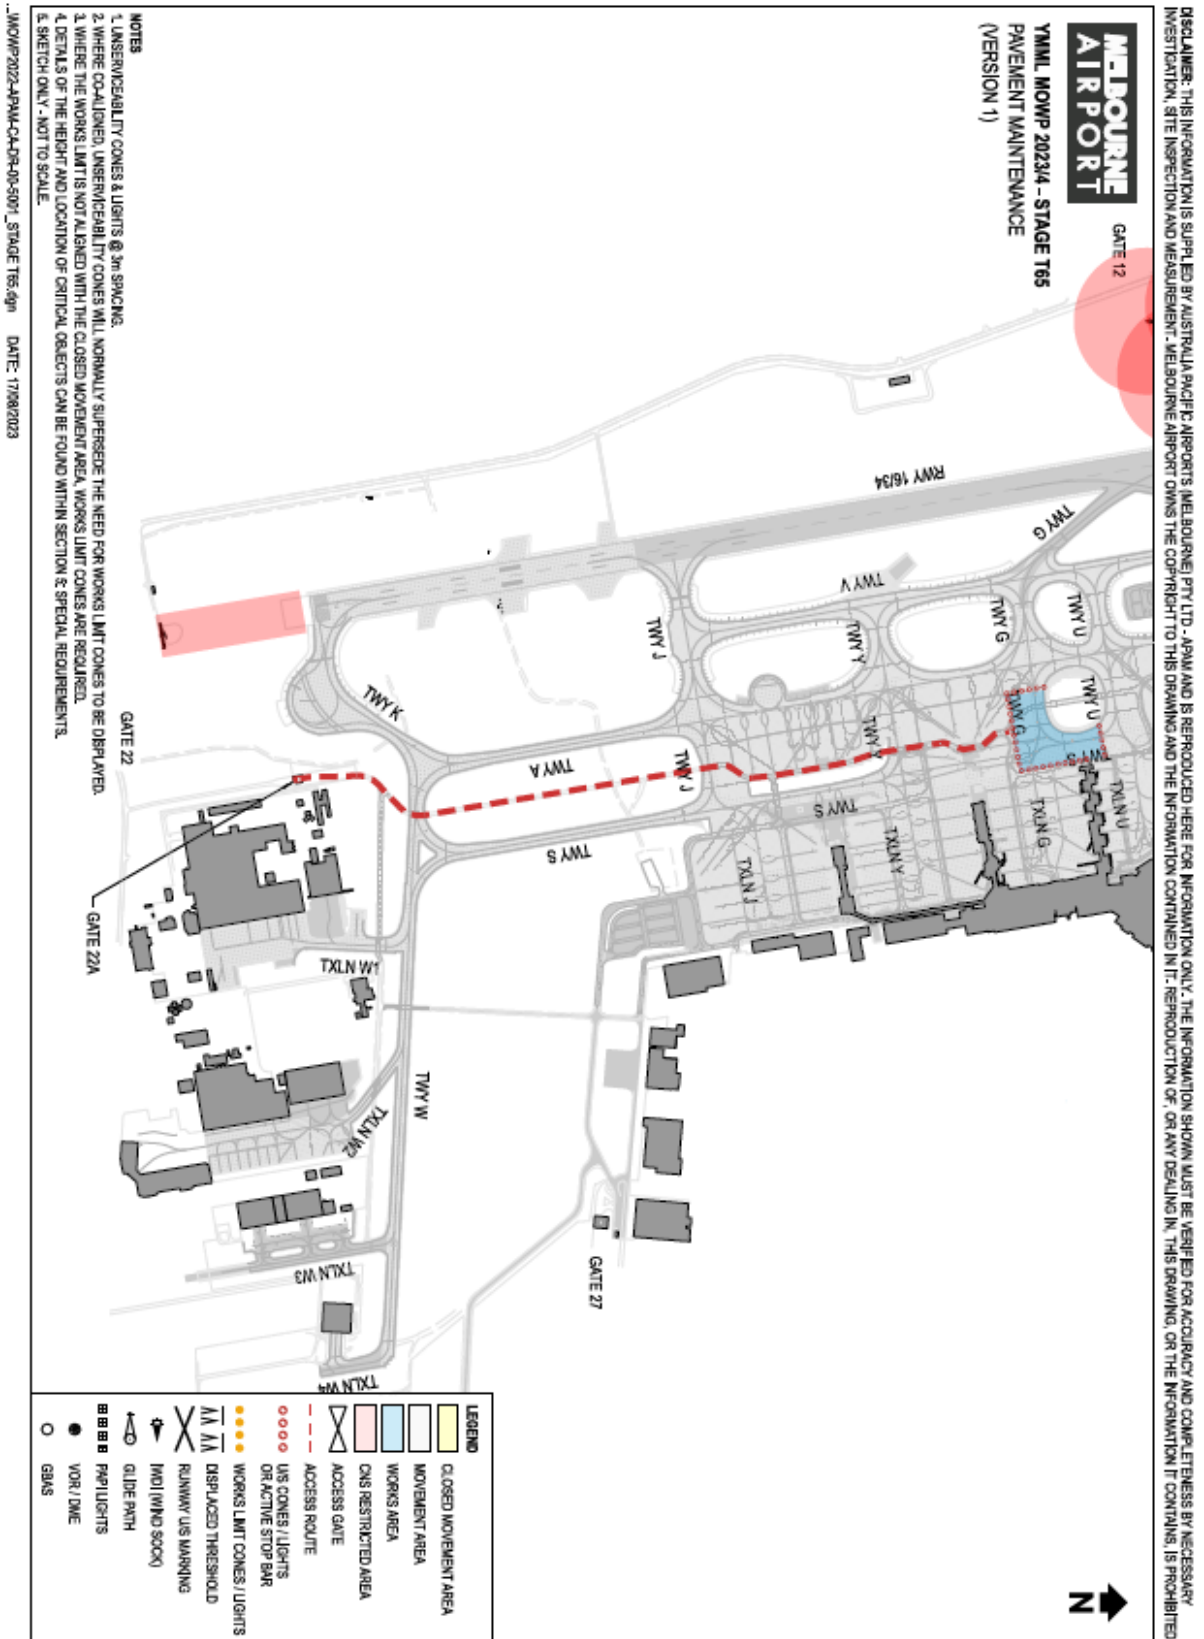


8.71. Stage T66

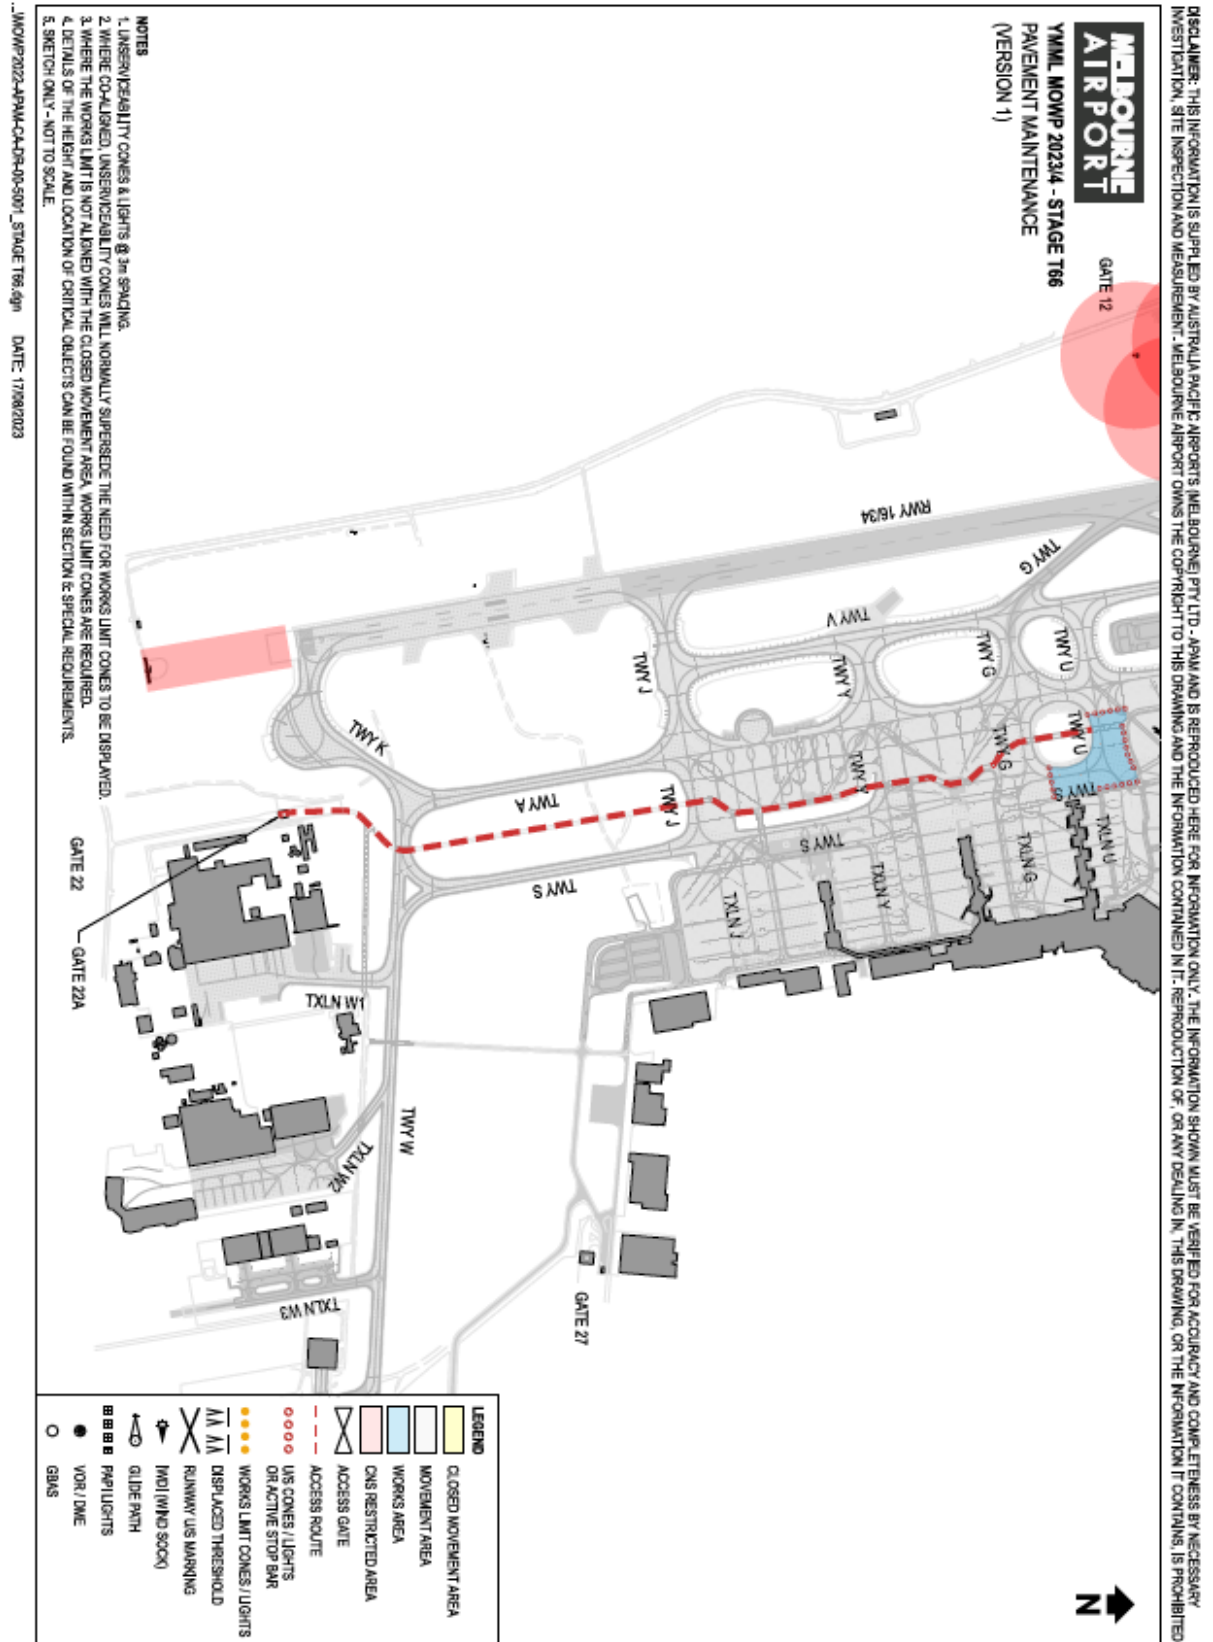

8.72. Stage T67

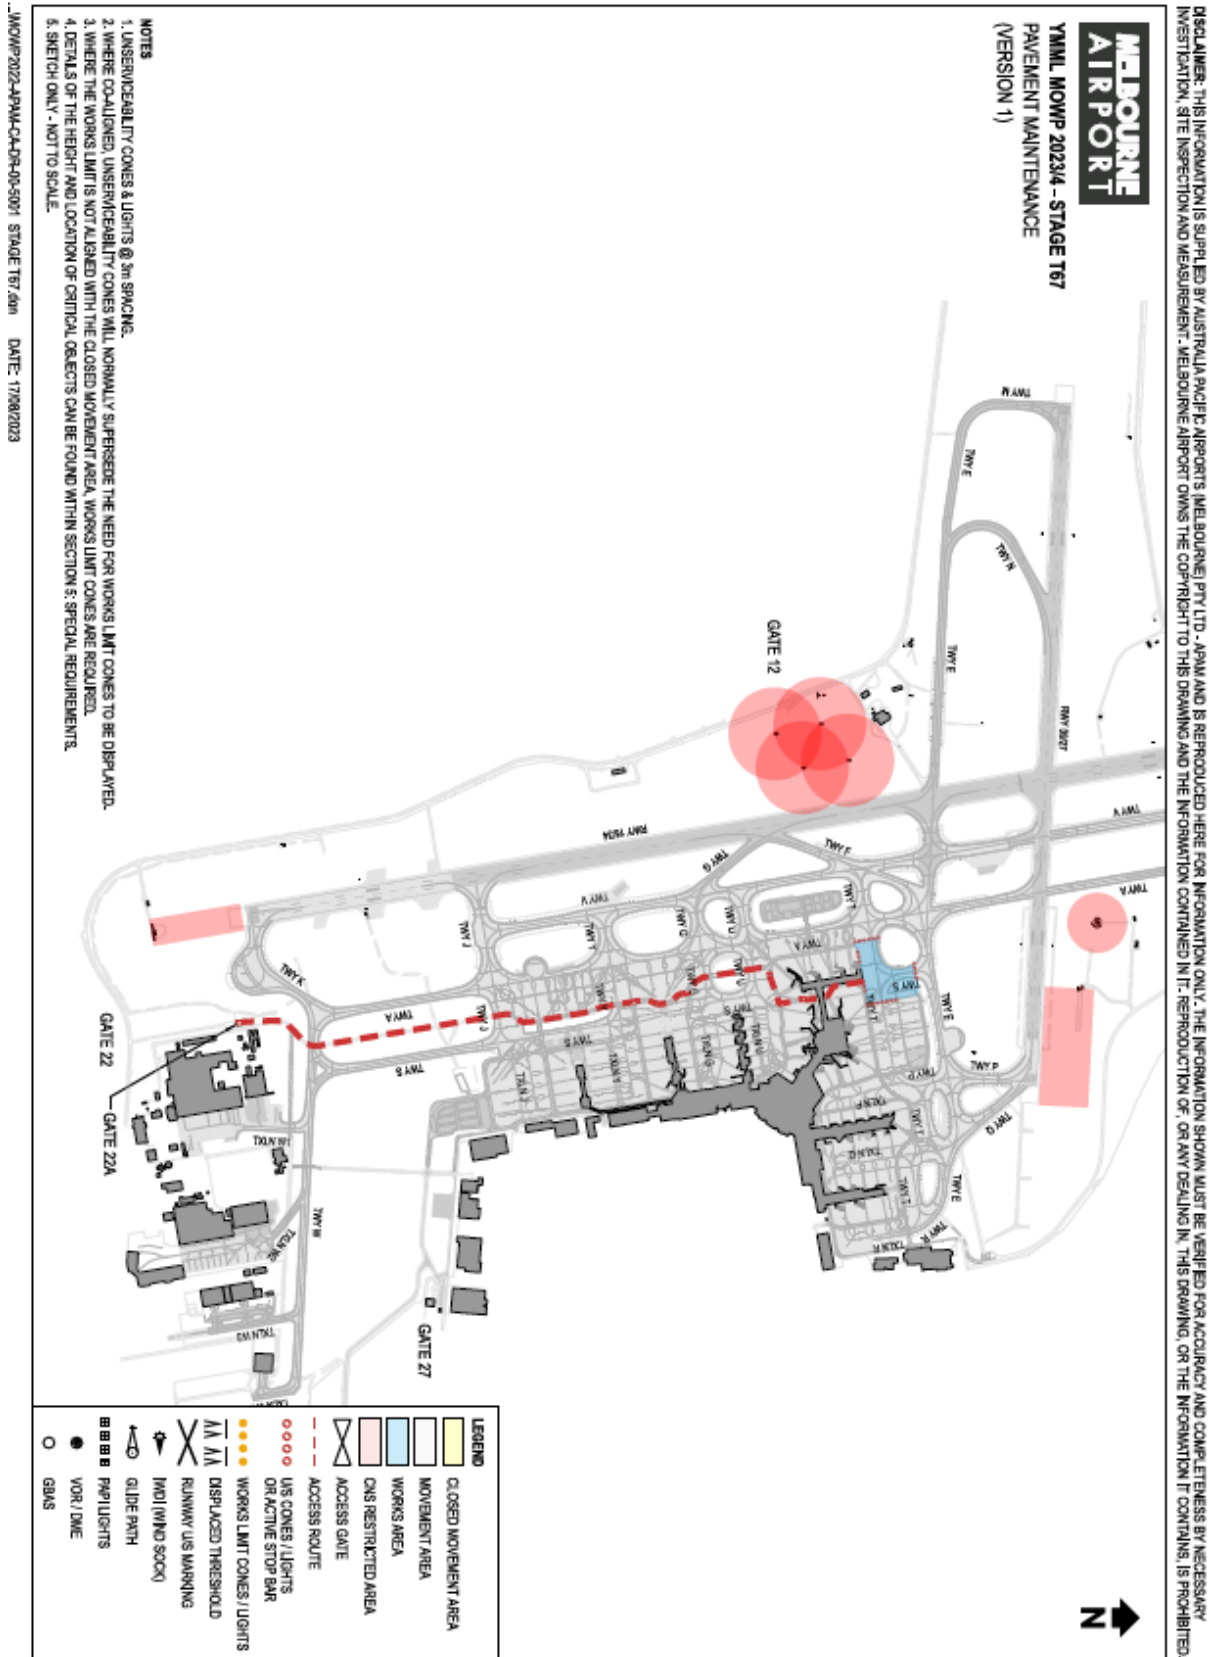

8.73. Stage T68

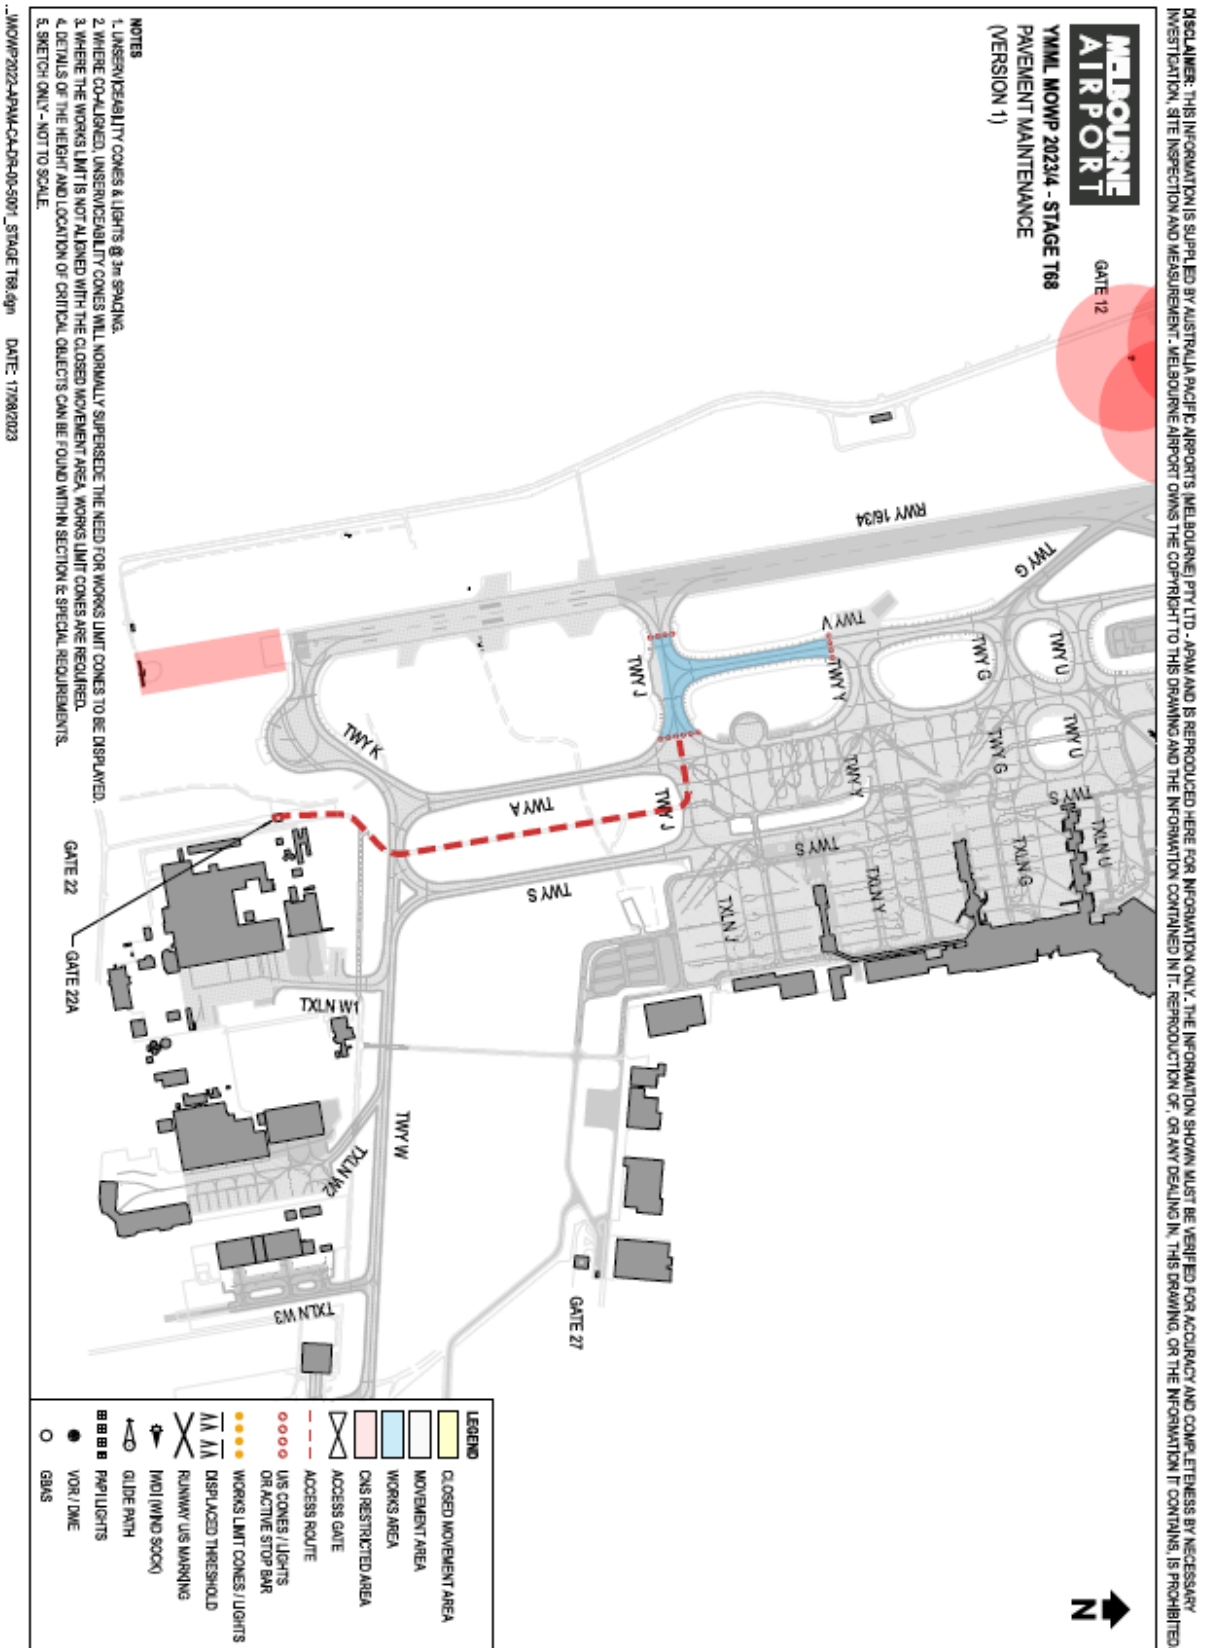


8.74. Stage T69




DISCLAIMER: THIS INFORMATION IS SUPPLIED BY AUSTRALIA PACIFIC AIRPORTS (MELBOURNE) PTY LTD. APAM AND IS REPRODUCED HERE FOR INFORMATION ONLY. THE INFORMATION SHOWN MUST BE VERIFIED FOR ACCURACY AND COMPLETENESS BY NECESSARY INVESTIGATION. SITE INSPECTION AND MEASUREMENT. MELBOURNE AIRPORT OWNS THE COPYRIGHT TO THIS DRAWING AND THE INFORMATION CONTAINED IN IT. REPRODUCTION OF, OR ANY DEALING IN, THIS DRAWING, OR THE INFORMATION IT CONTAINS, IS PROHIBITED.


8.75. Stage T70

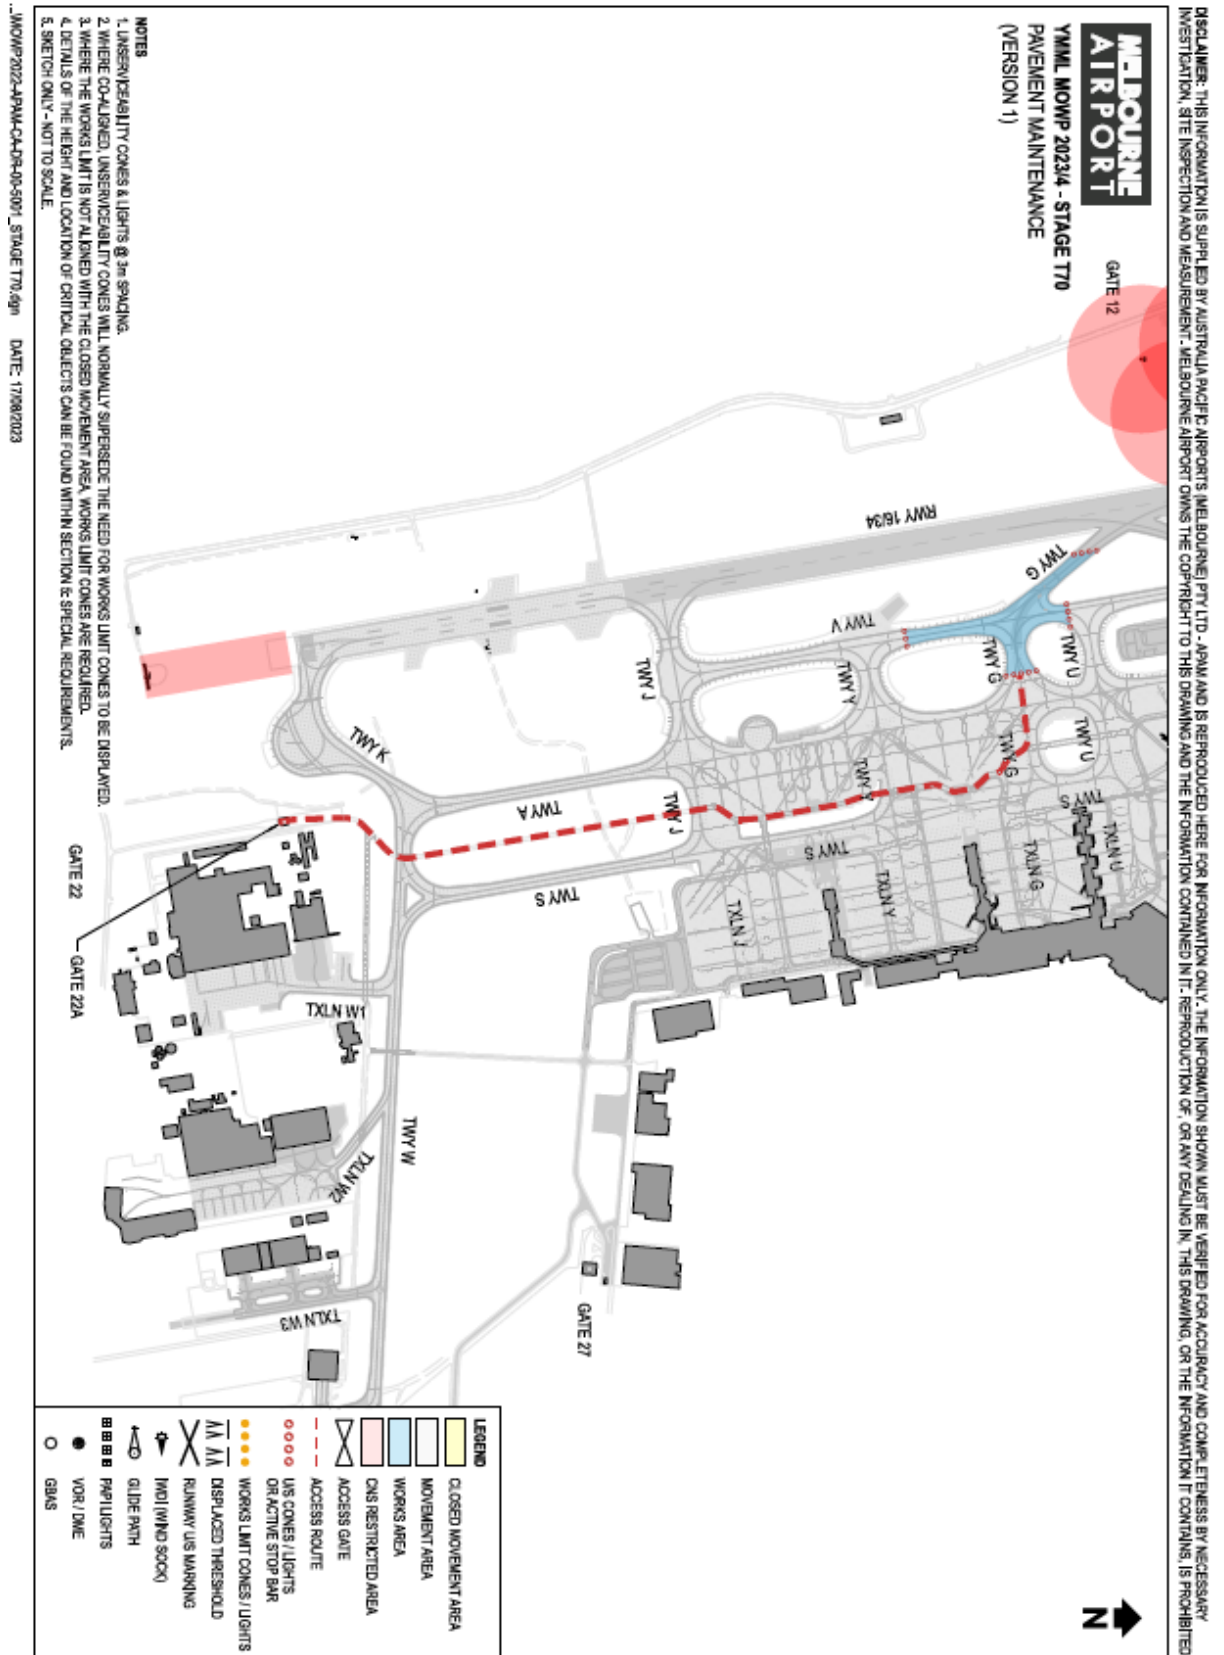

8.76. Stage T71

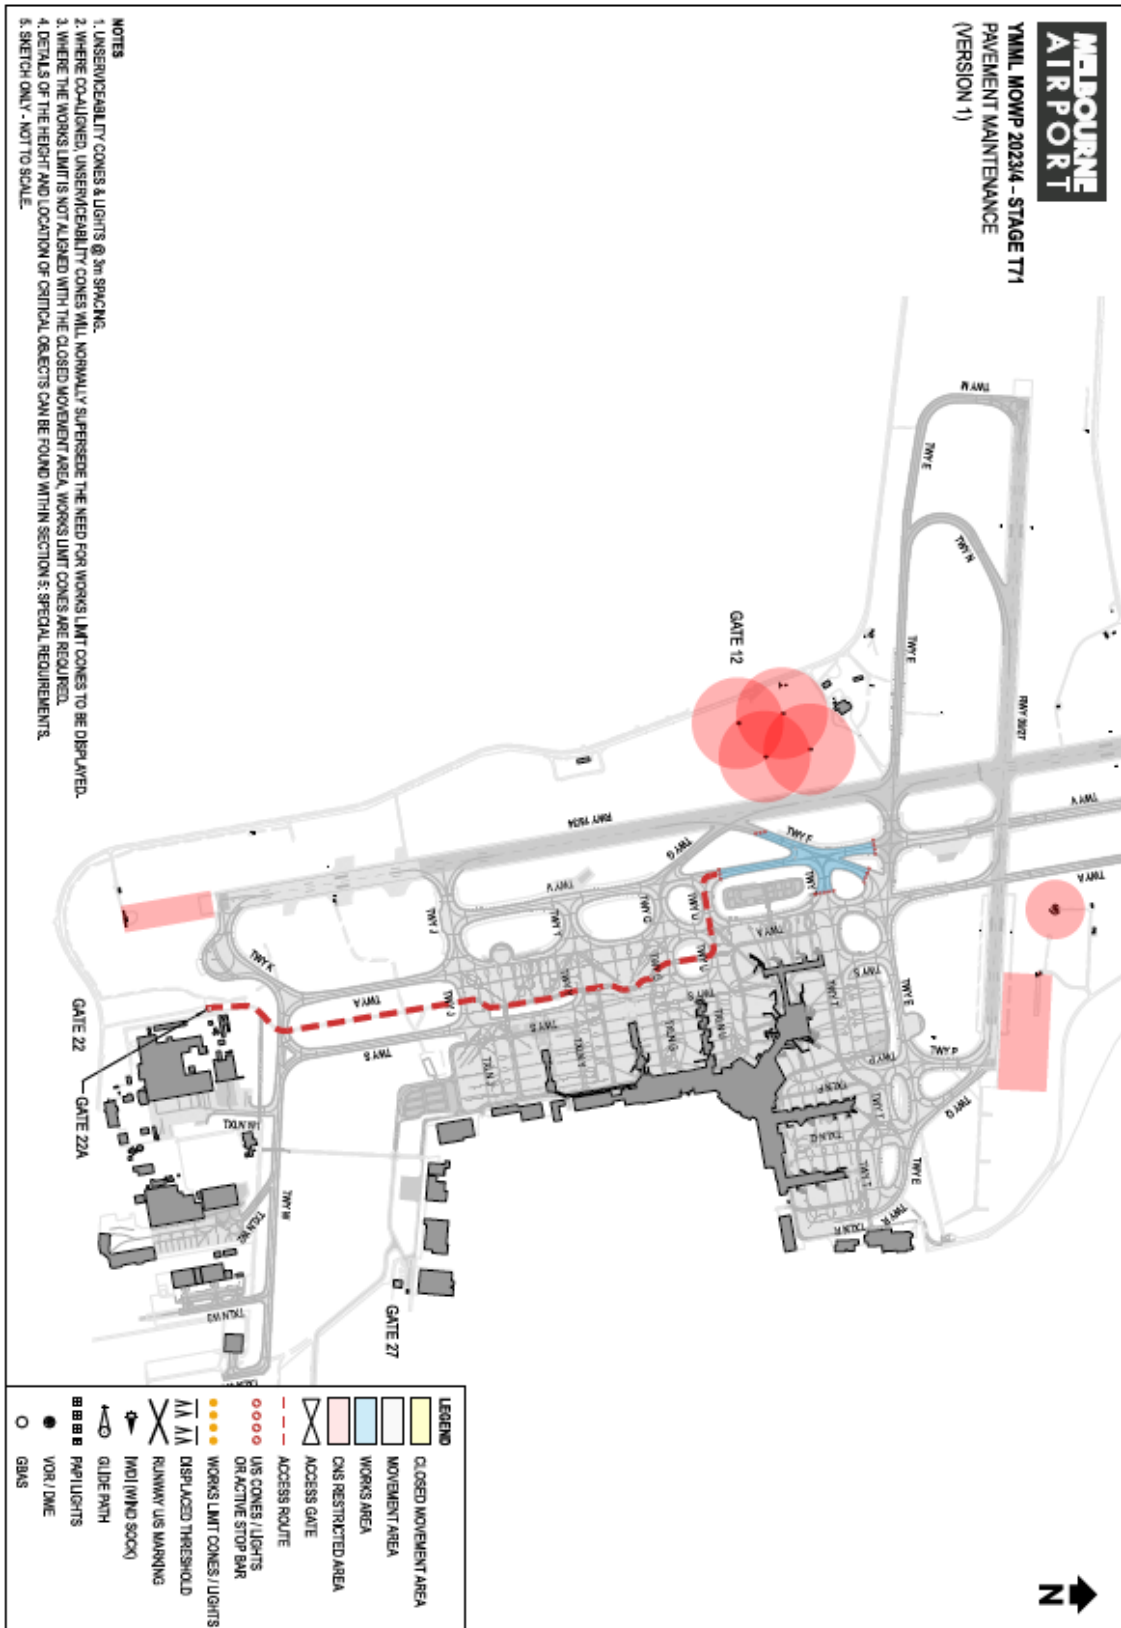


8.77. Stage T72

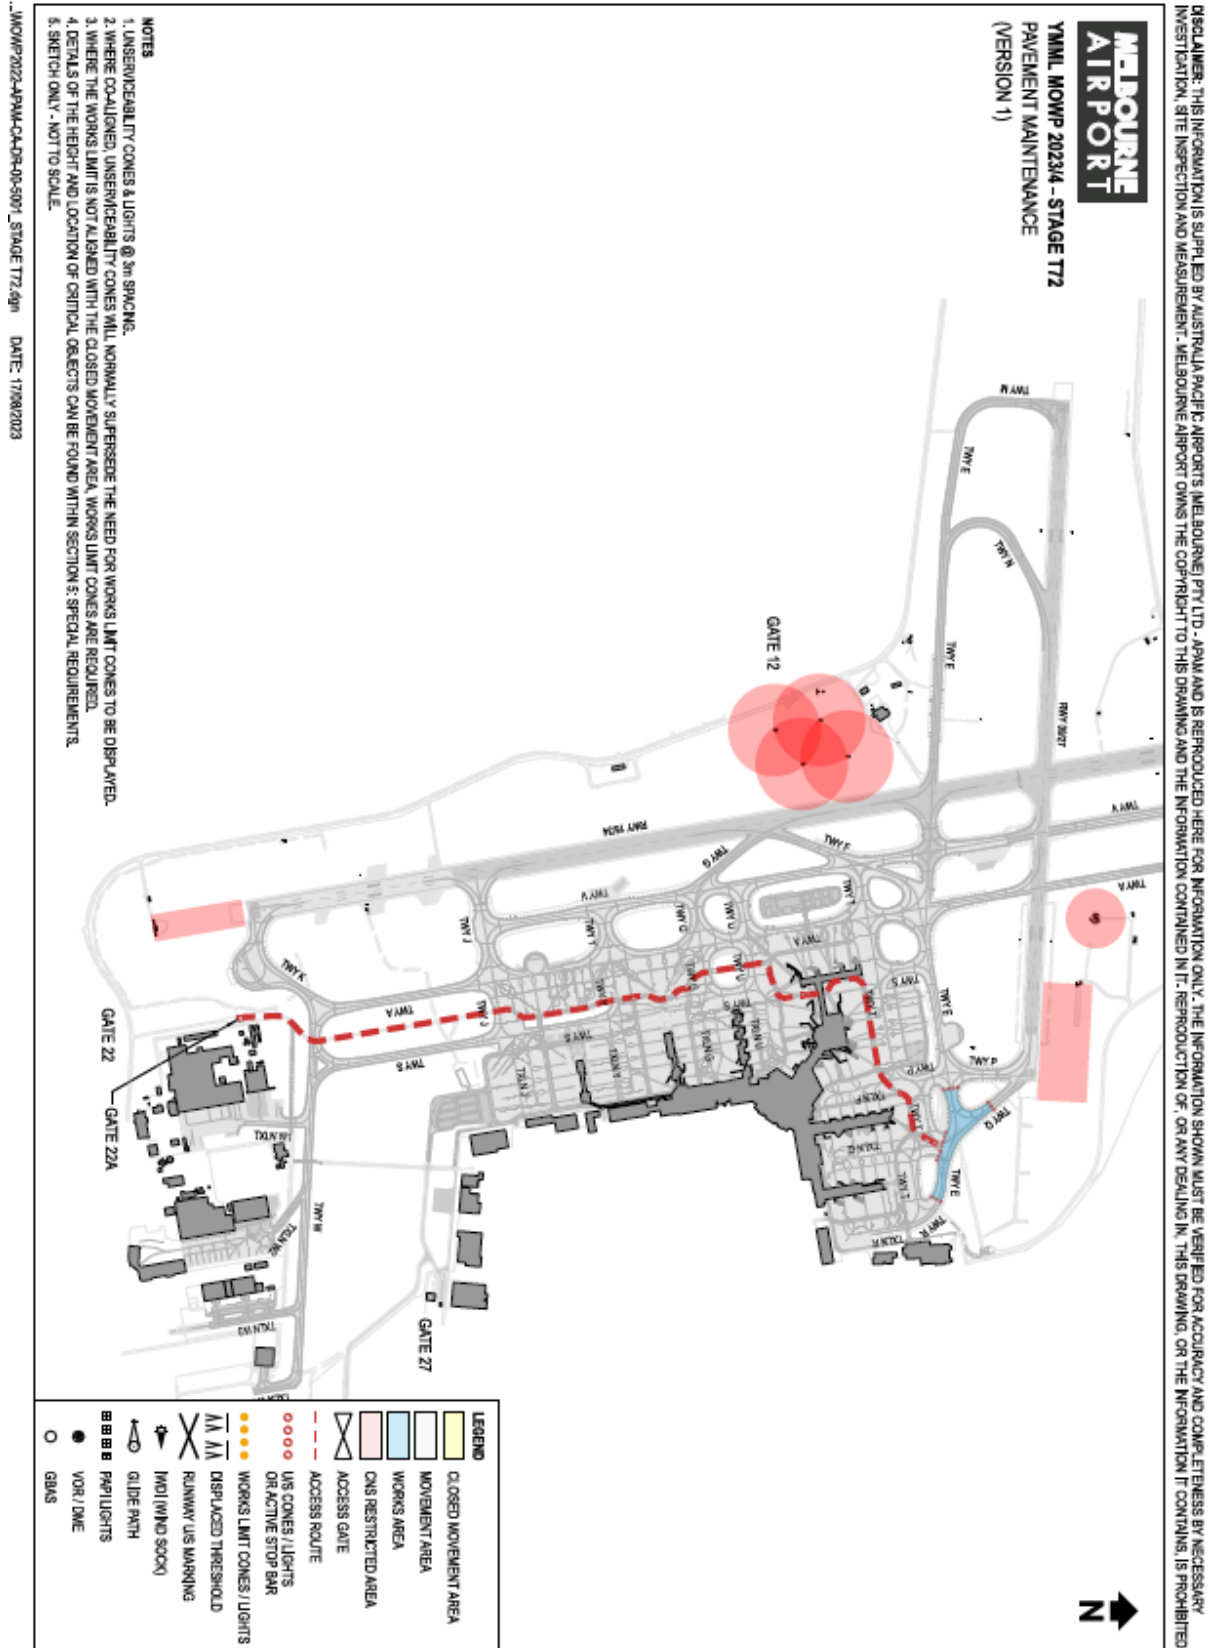


8.78. Stage T73




8.79. Stage T74

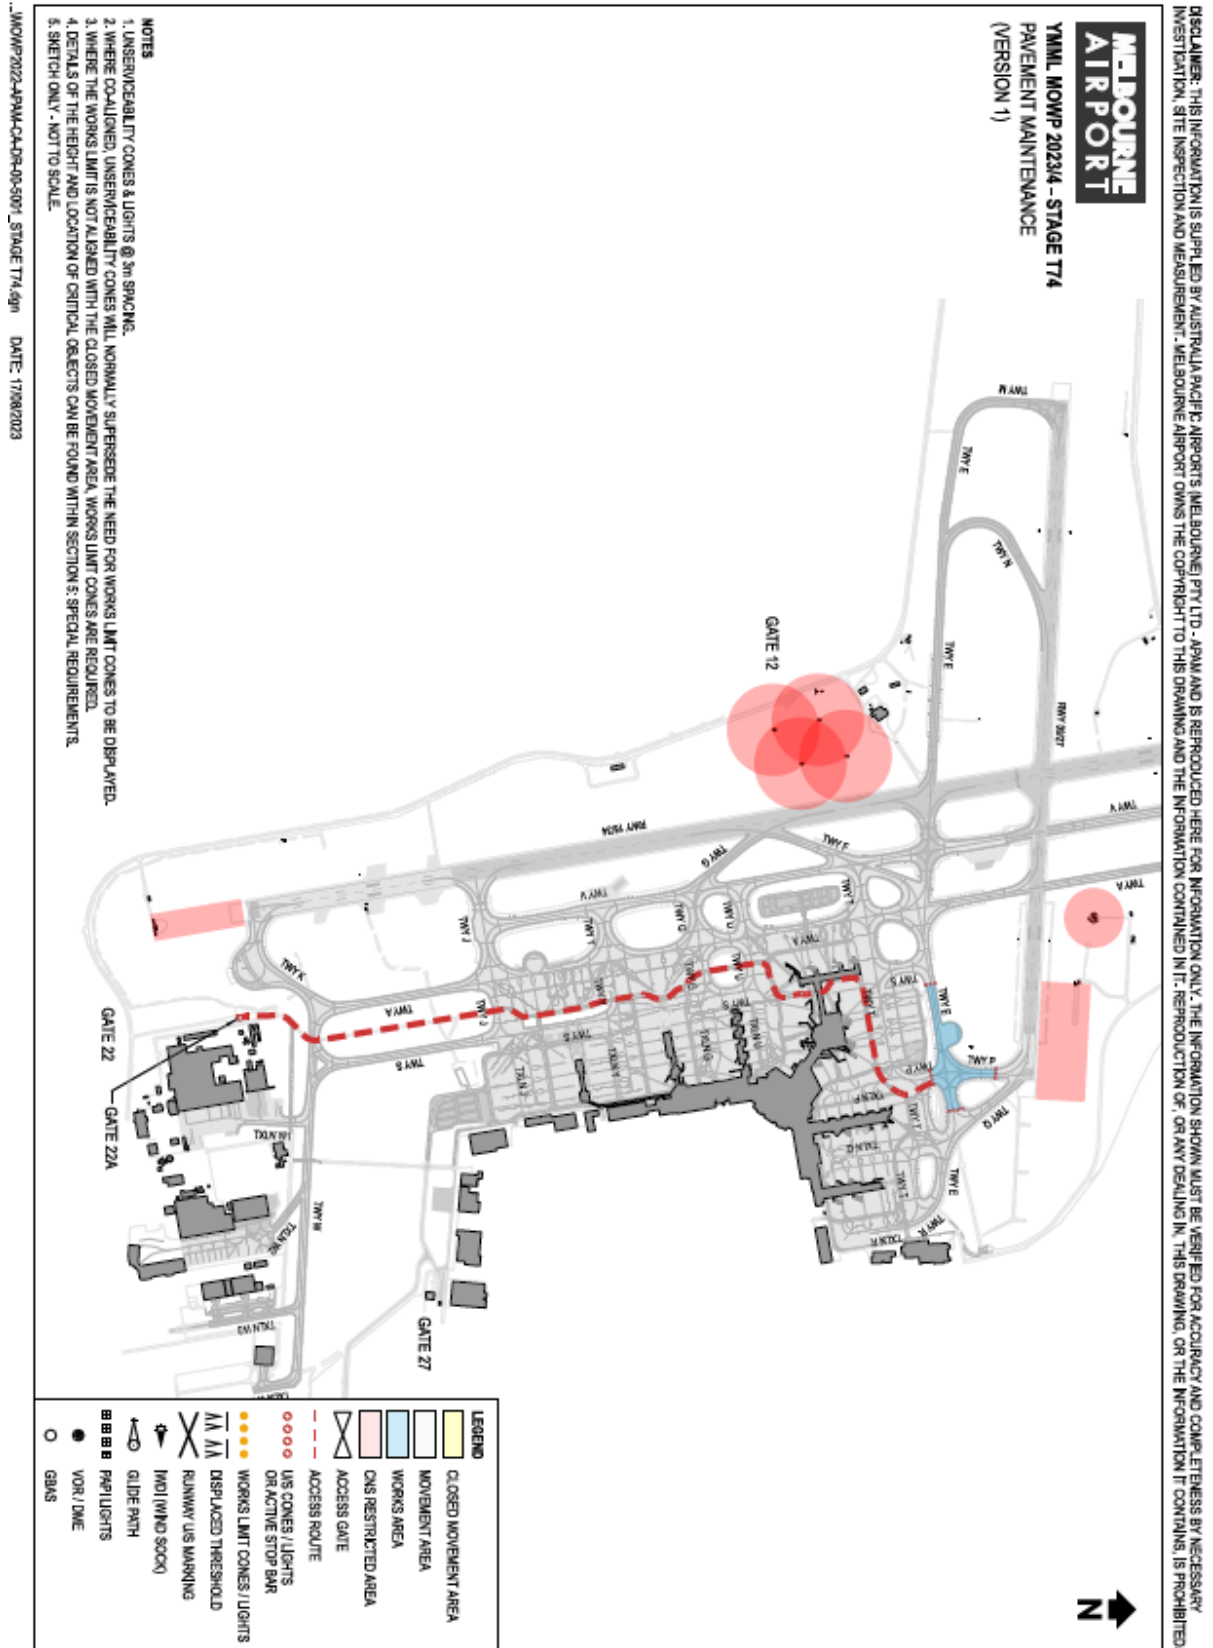


8.80. Stage T75

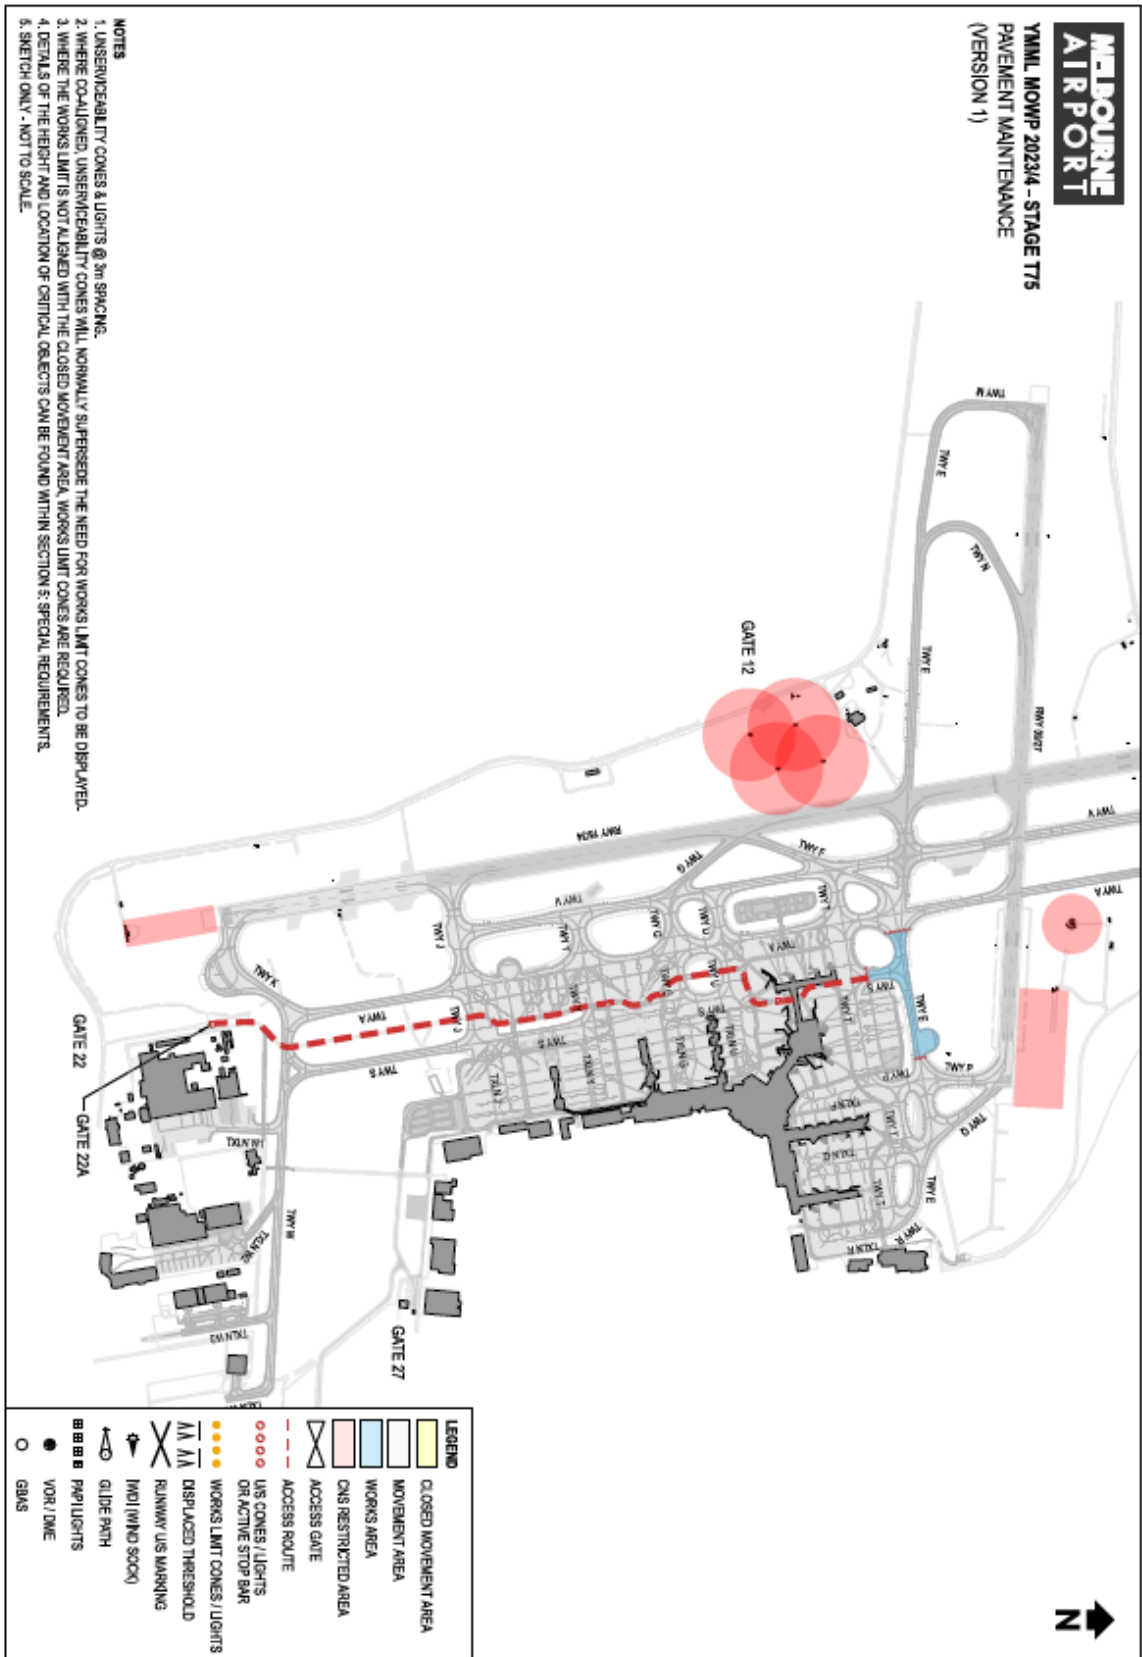


8.81. Stage T76

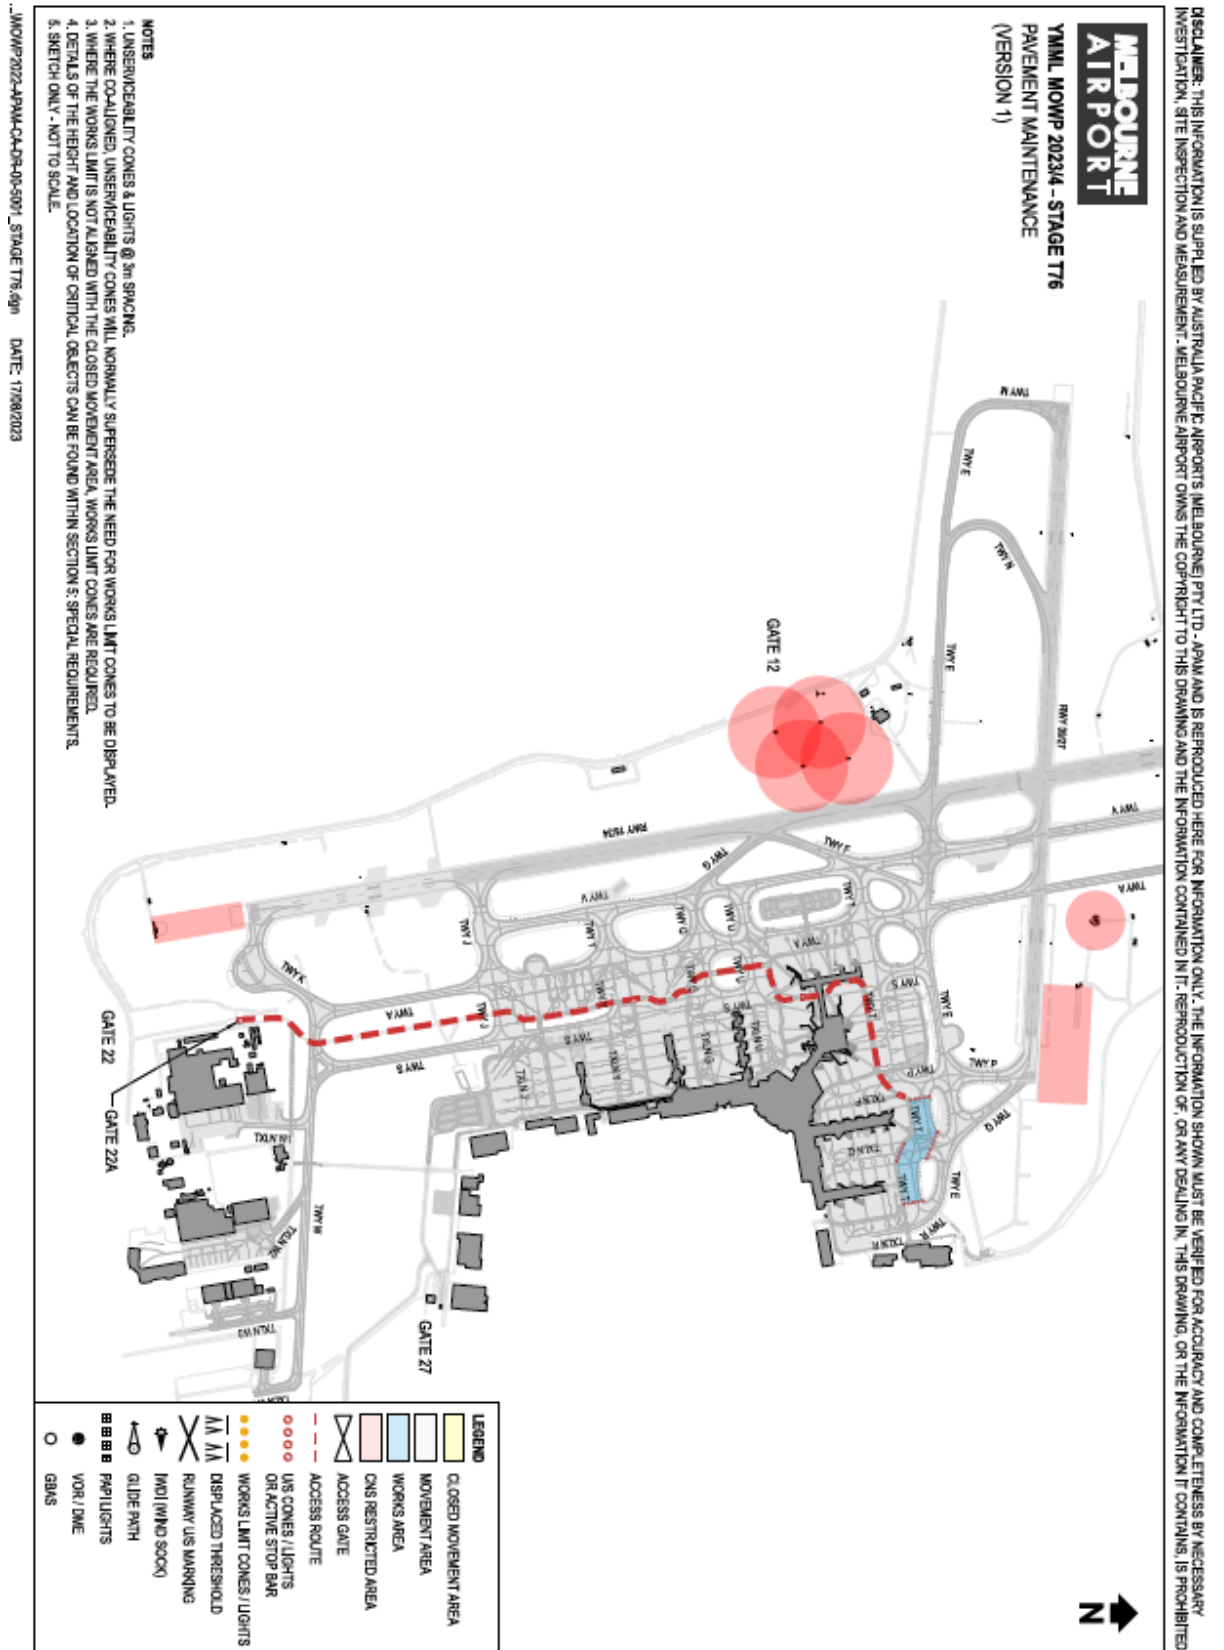


8.82. Stage T77

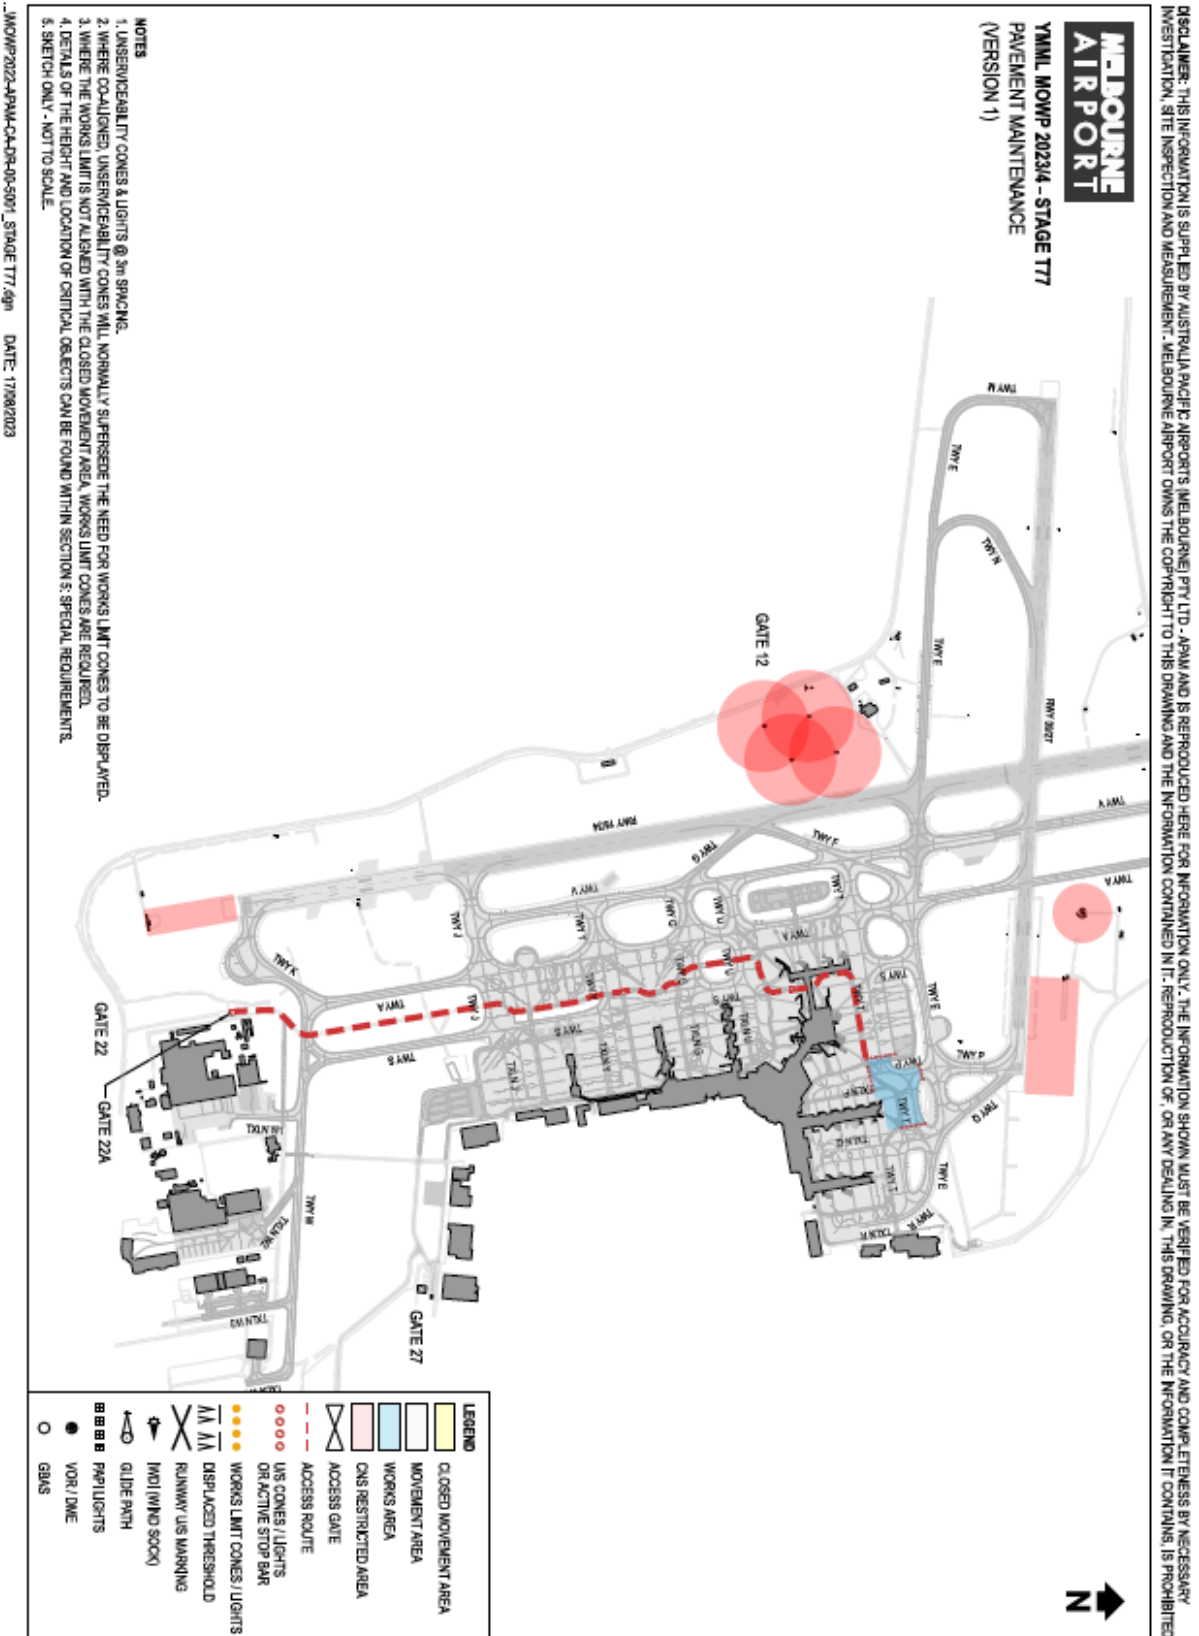


8.83. Stage T78

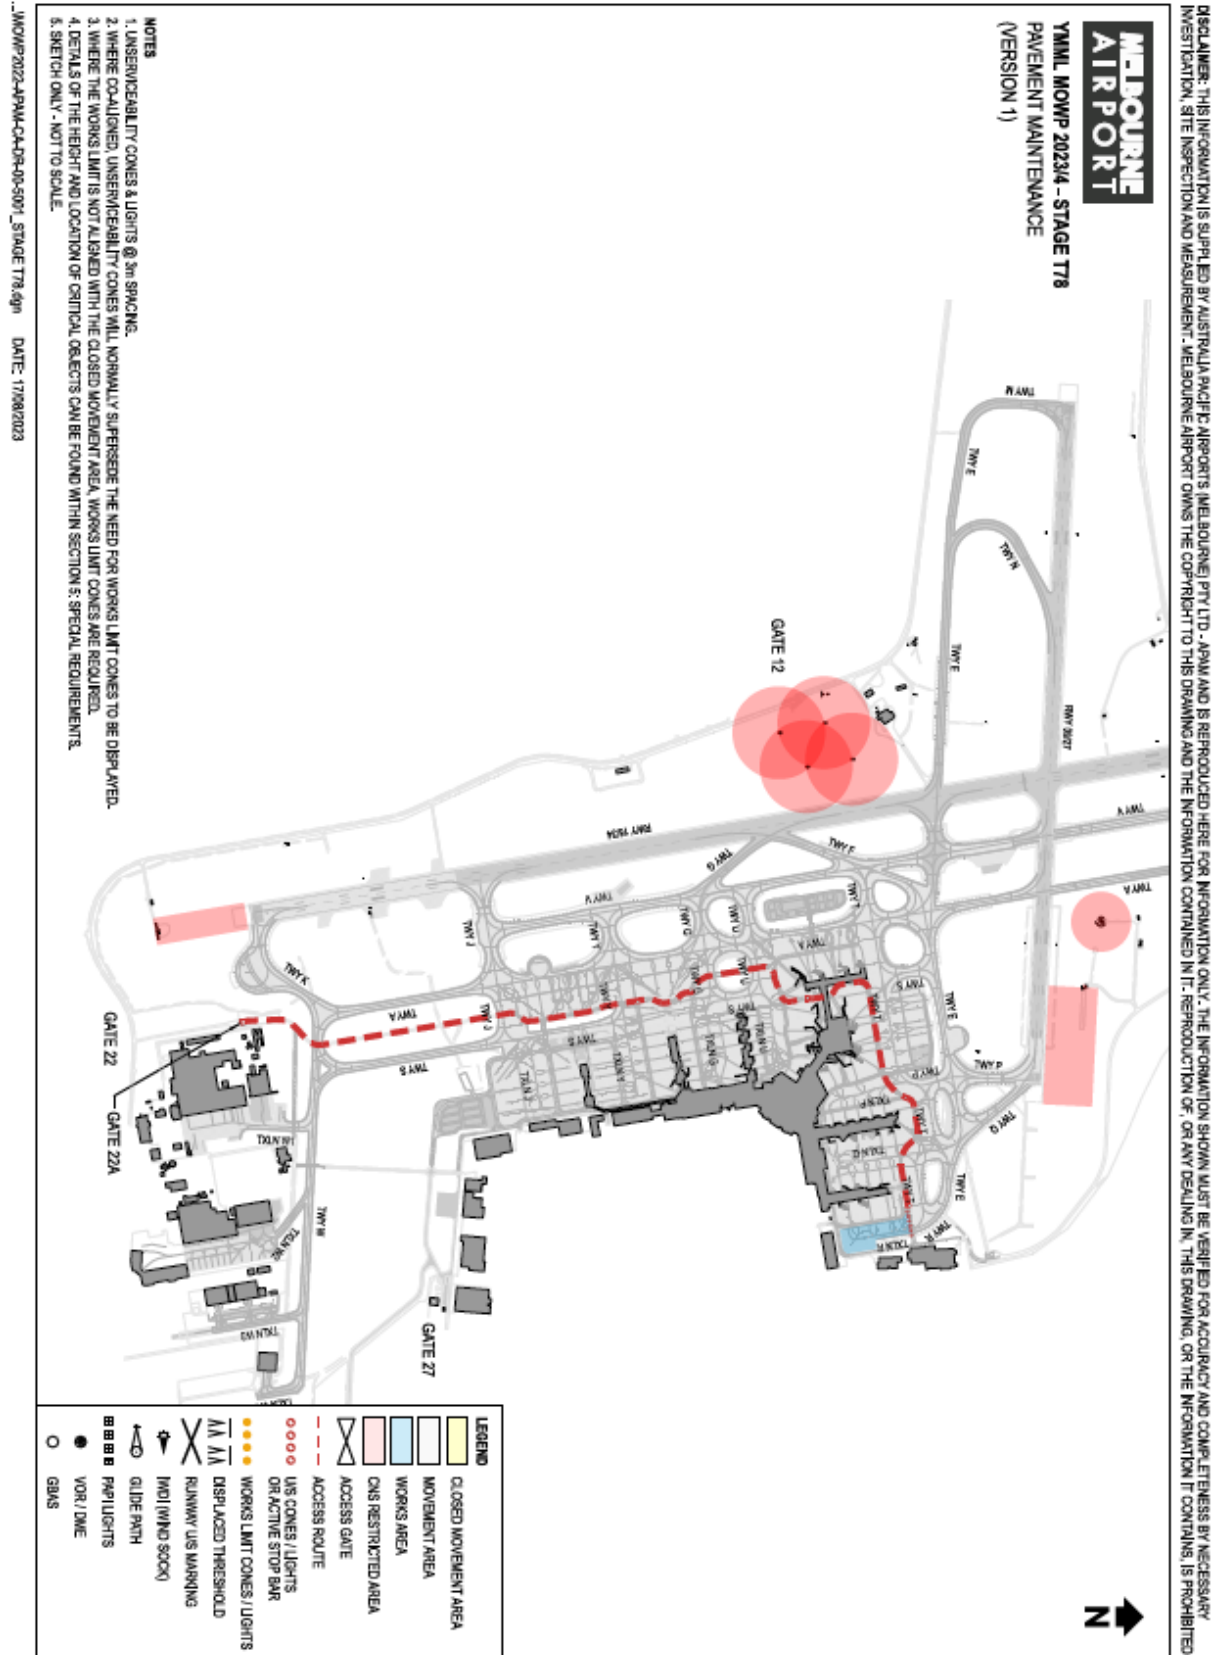


8.84. Stage T79

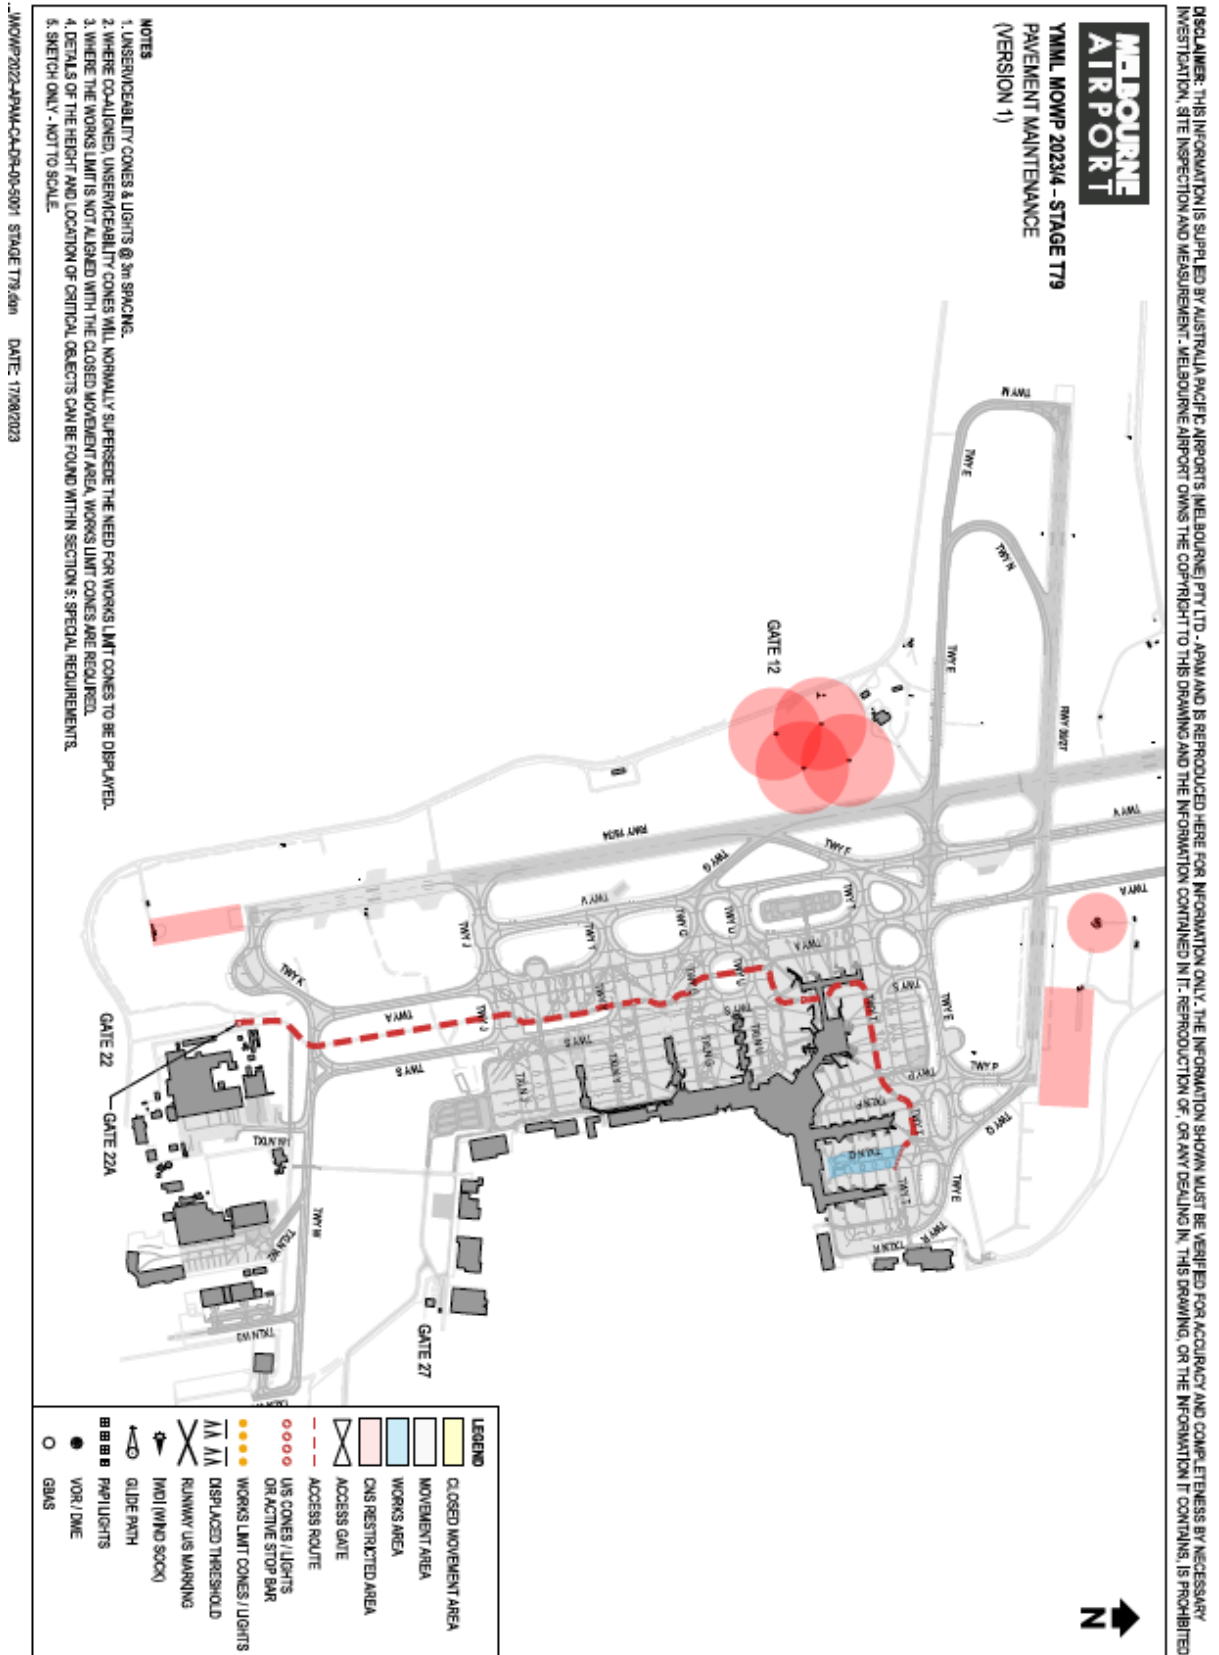


8.85. Stage T80

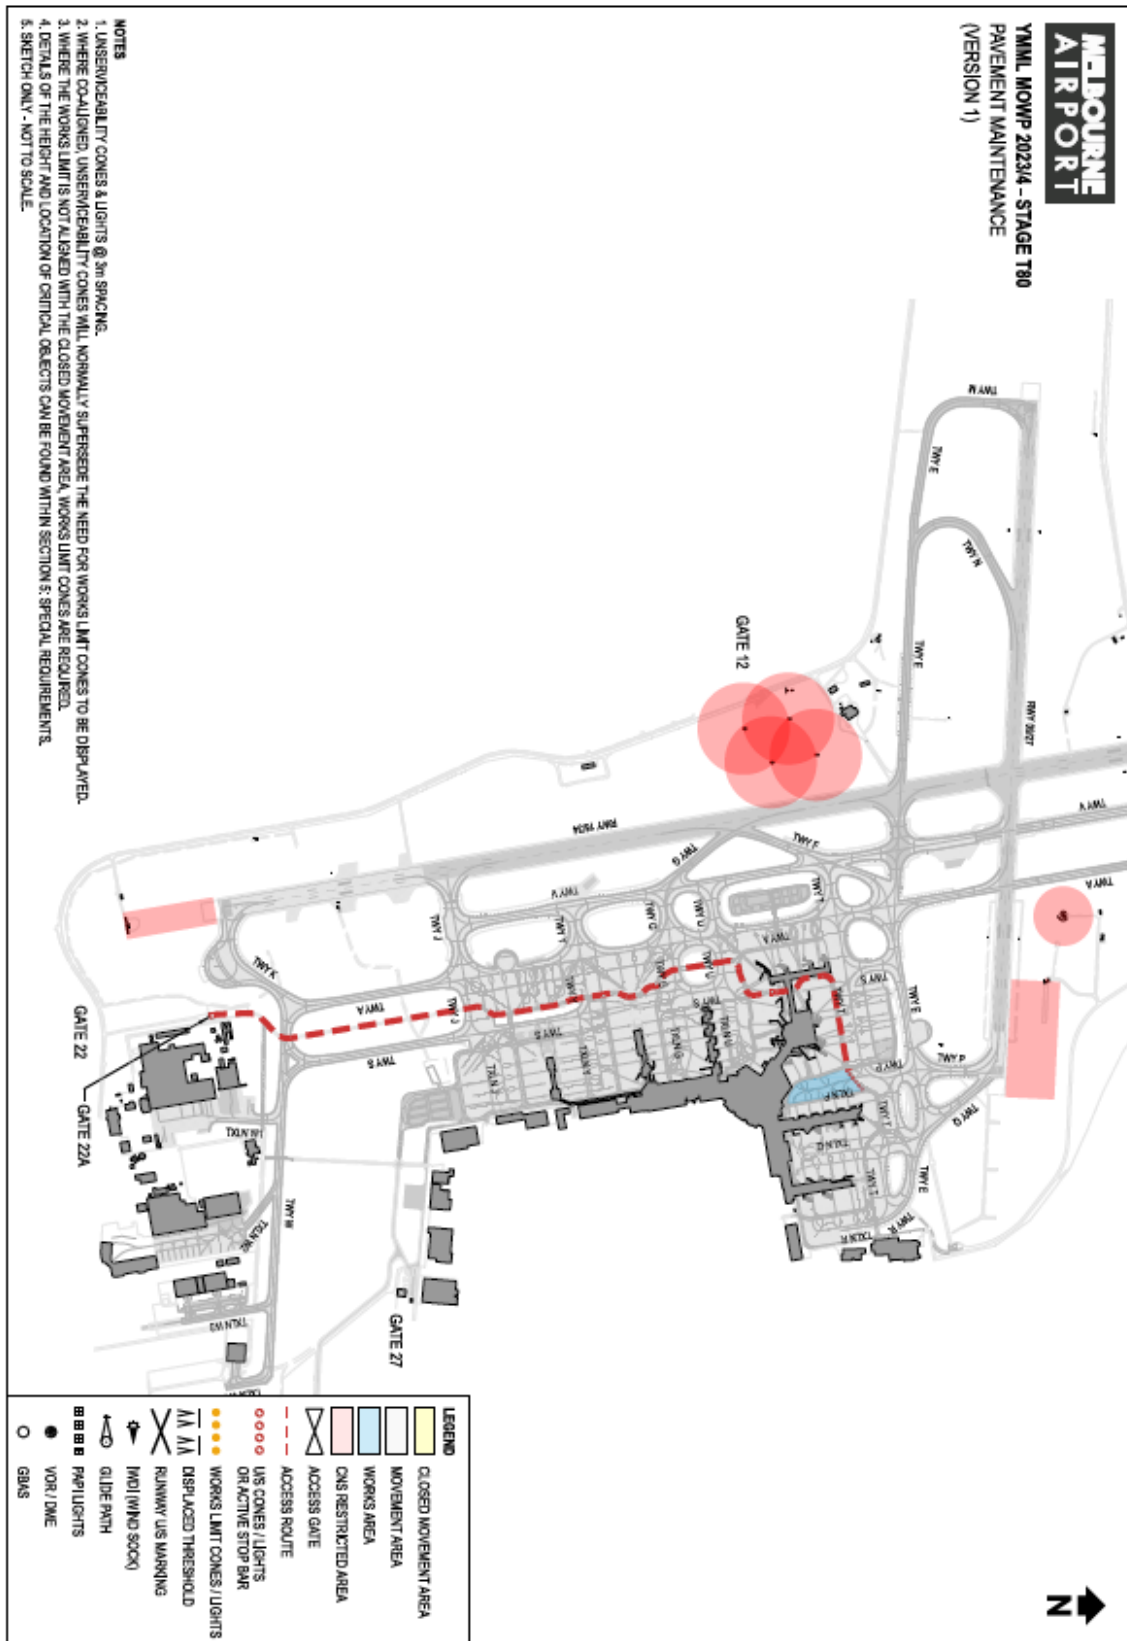


8.86. Stage T81

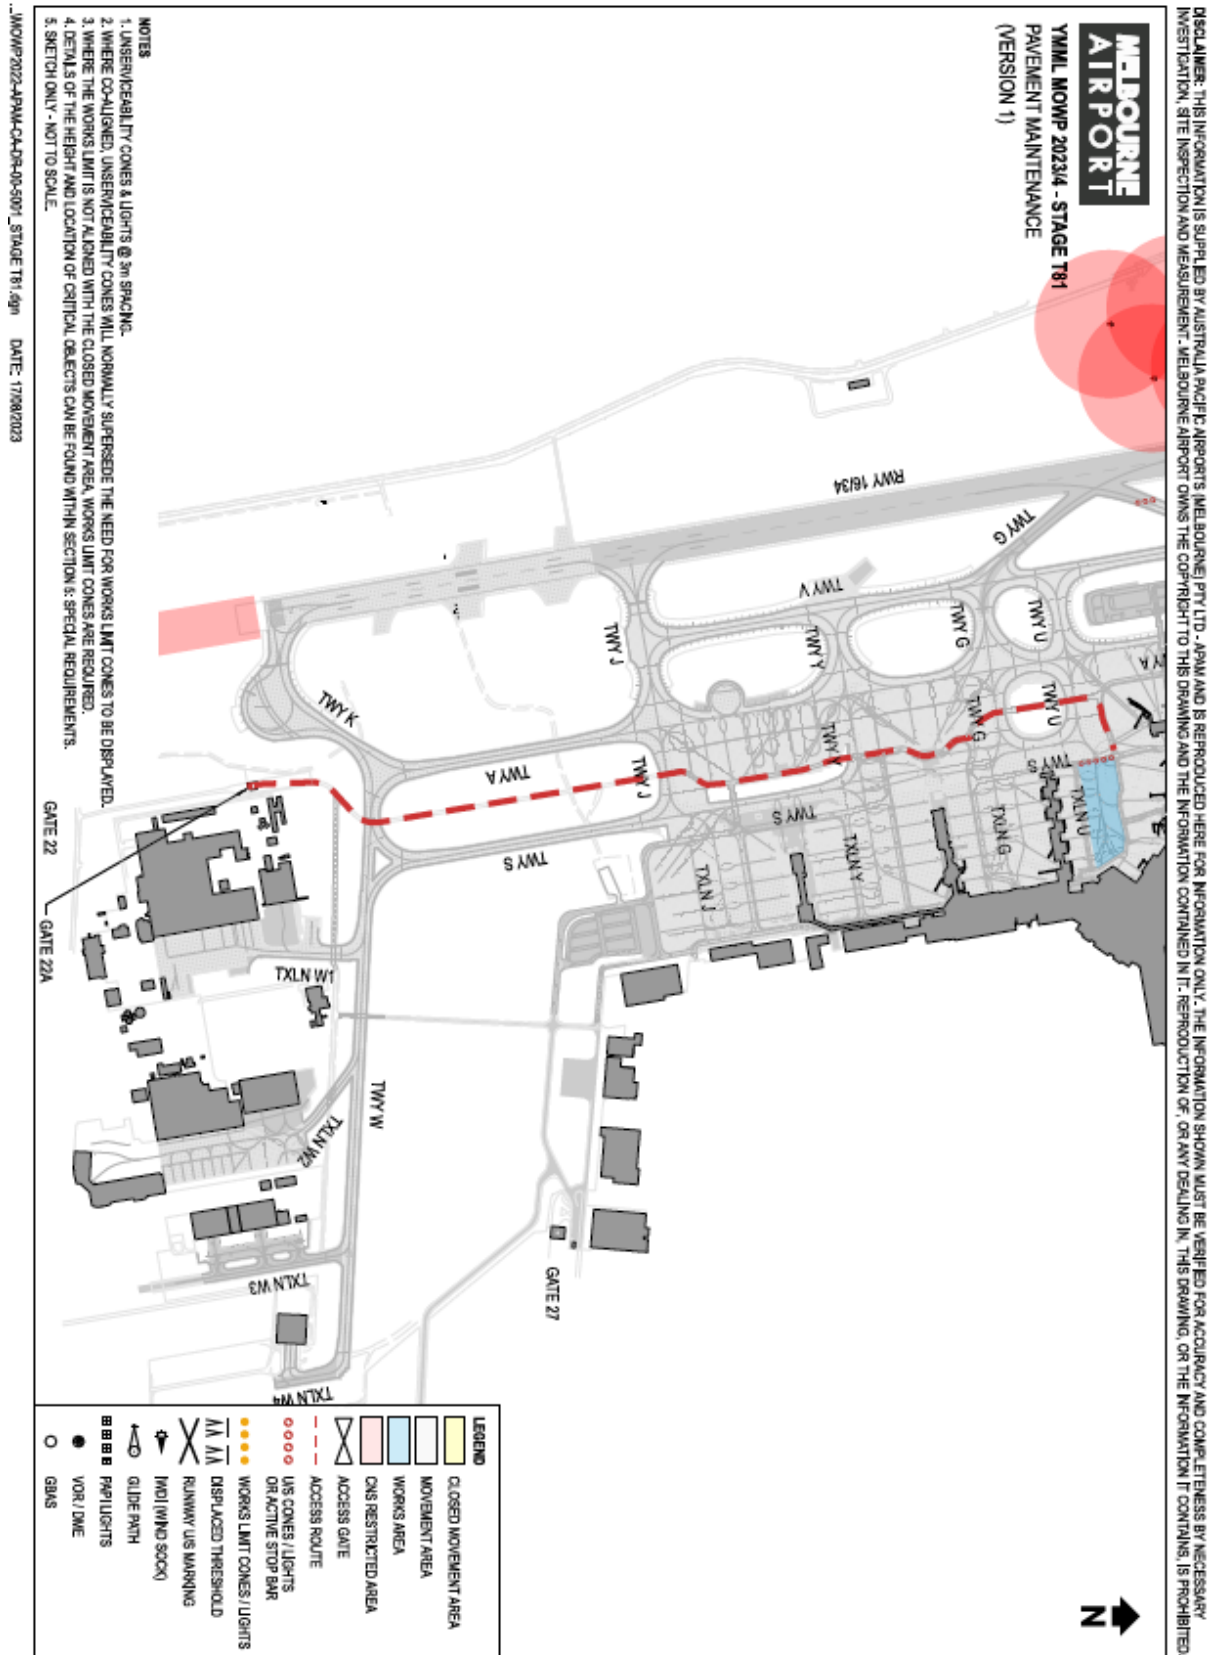


8.87. Stage T82

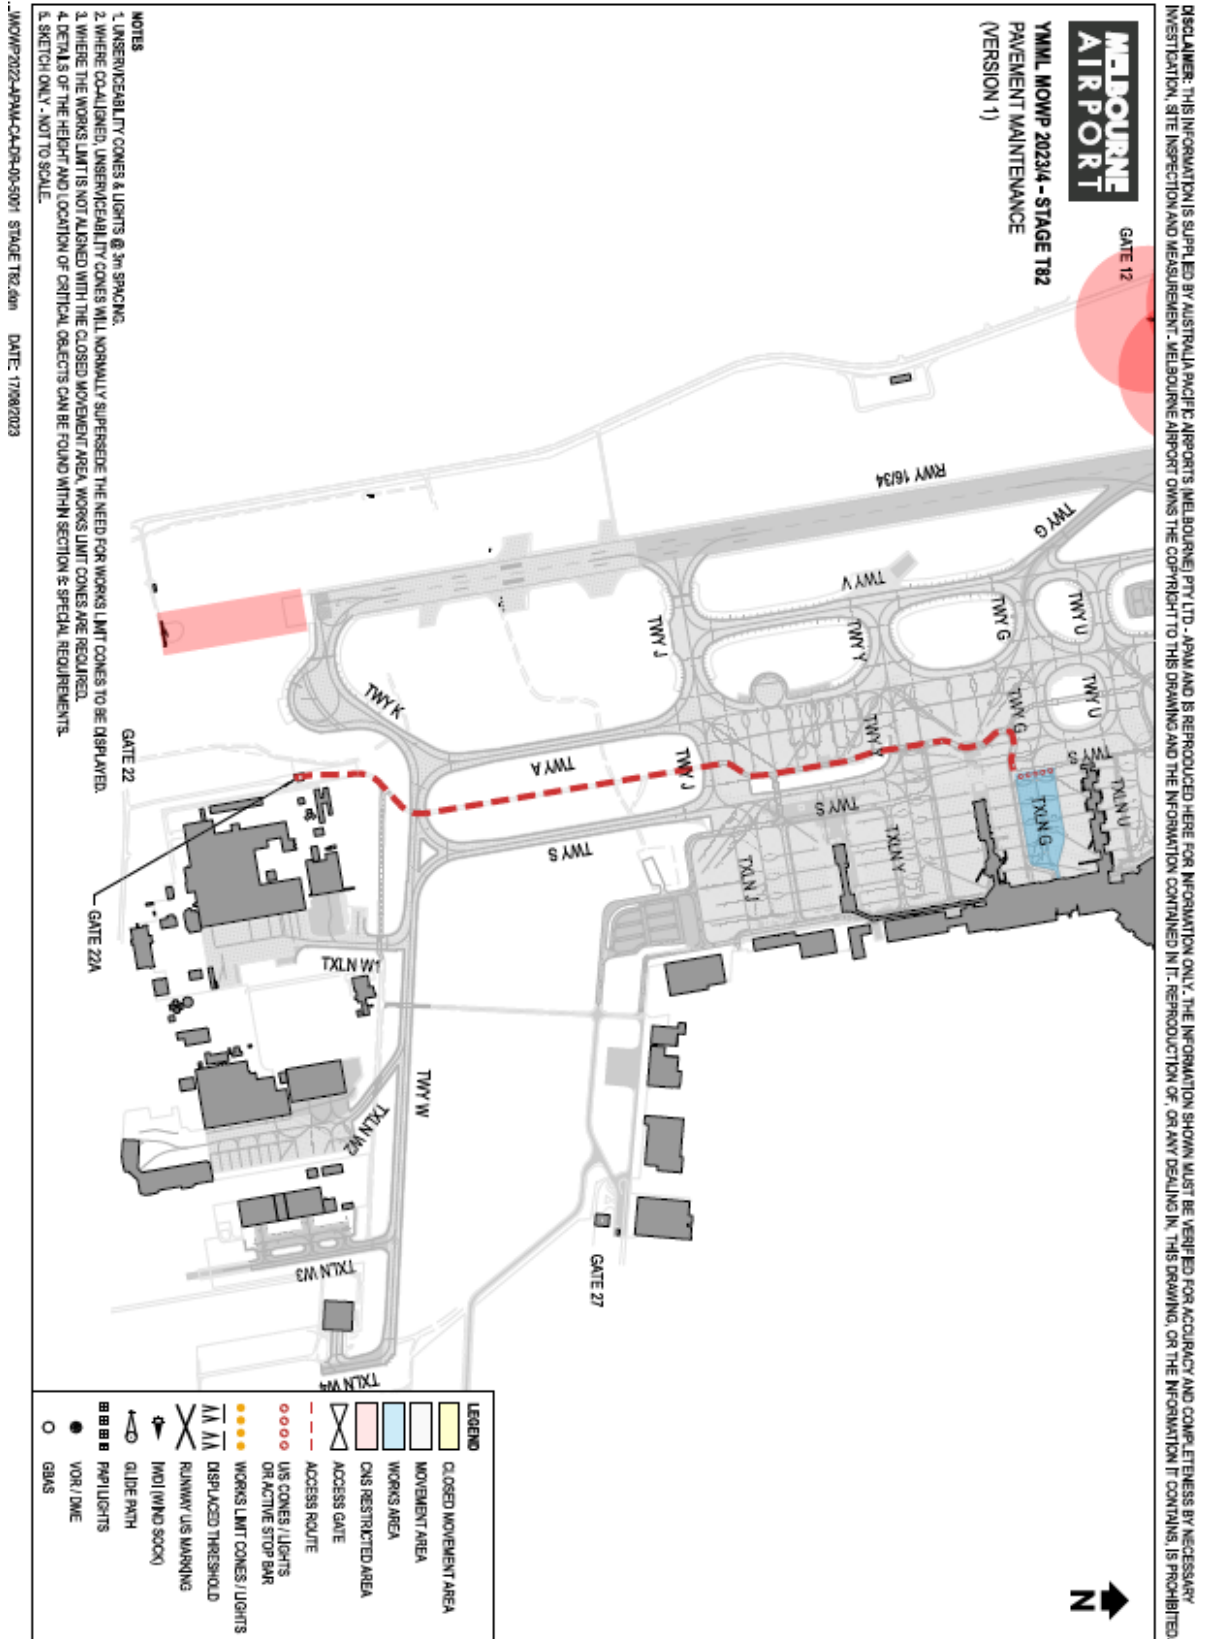


8.88. Stage T83

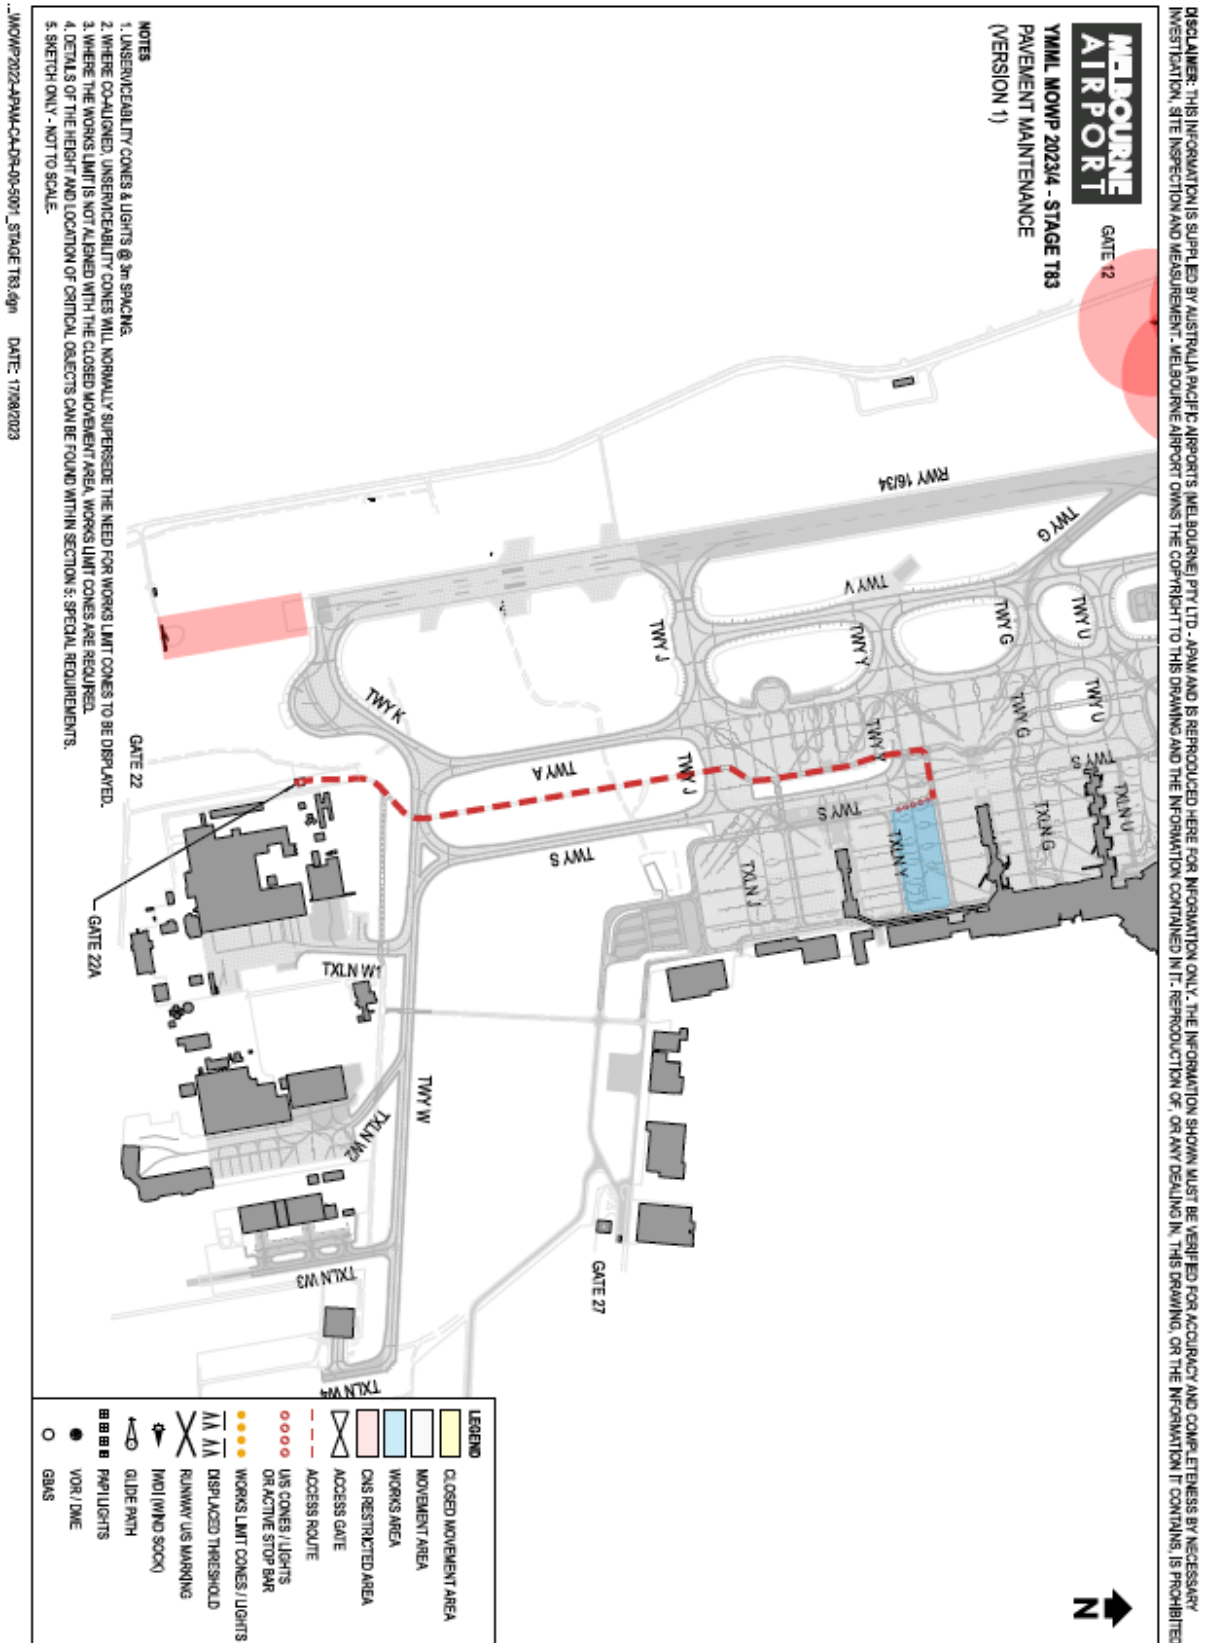


8.89. Stage T84

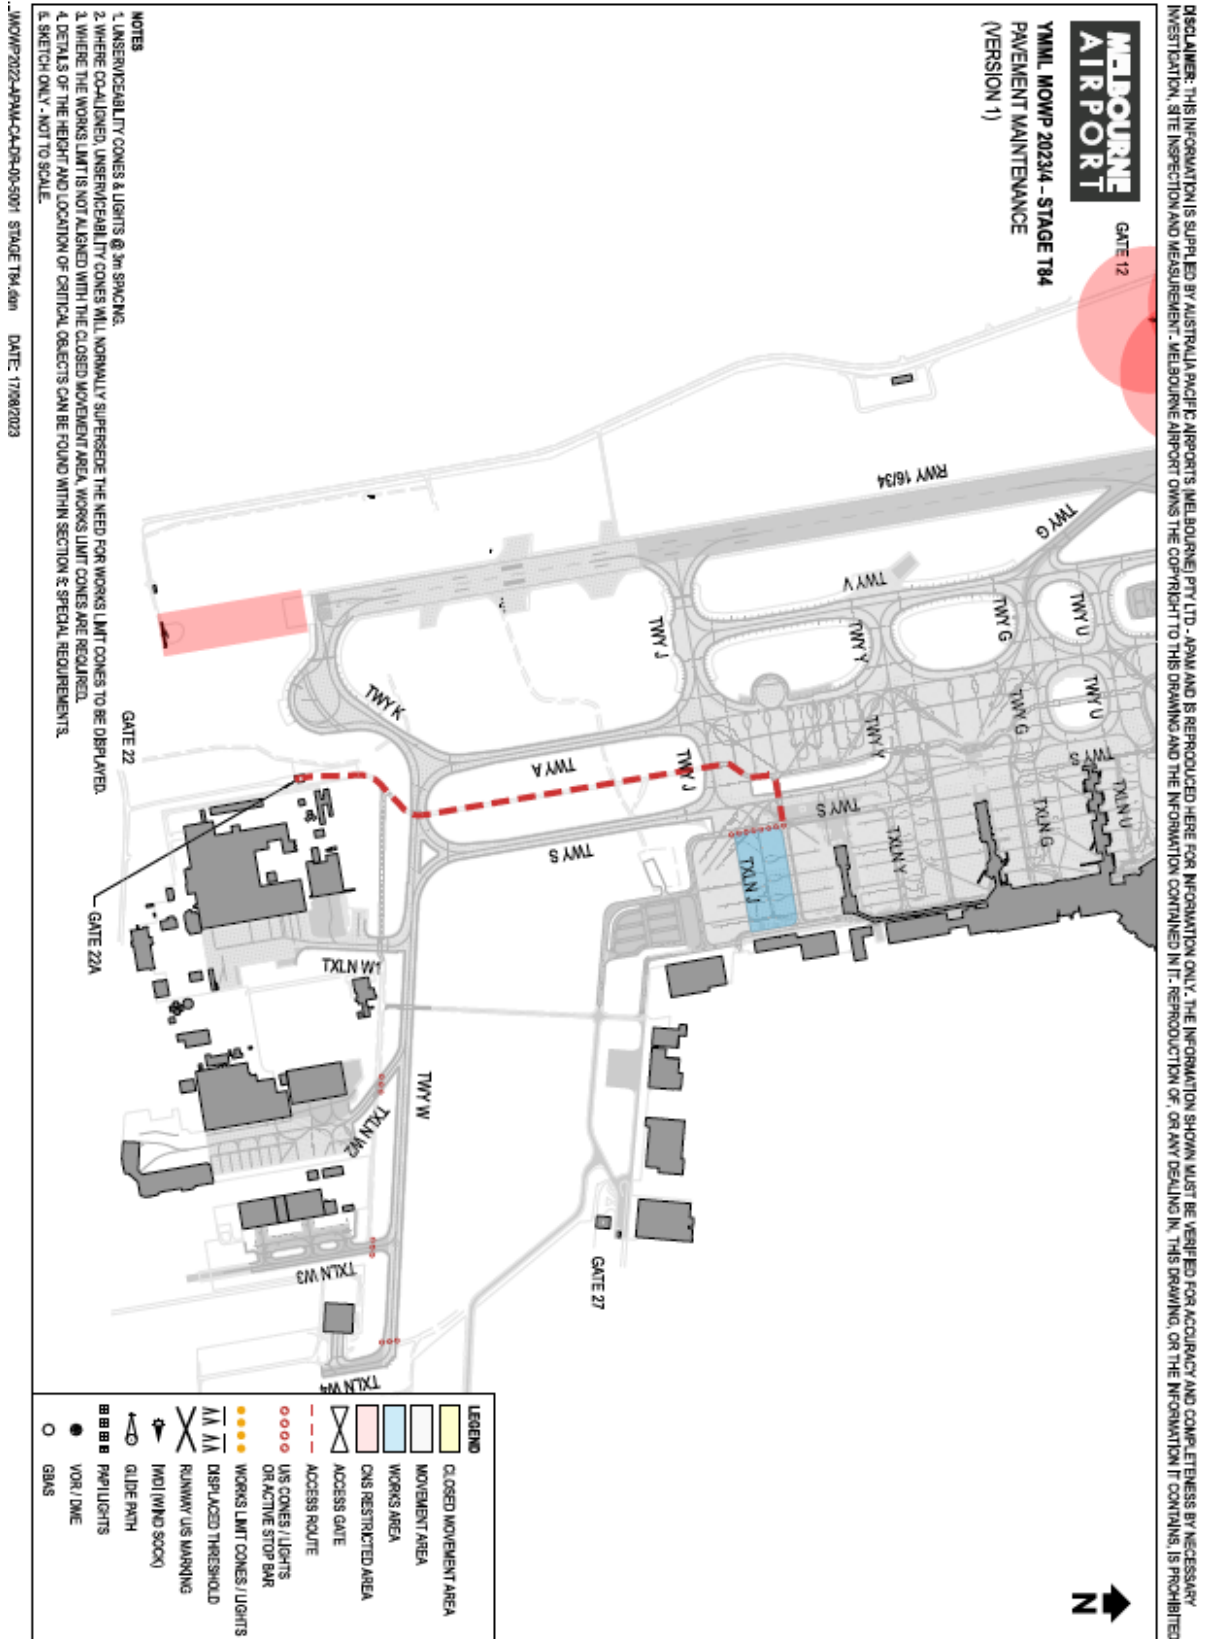


8.90. Stage T85

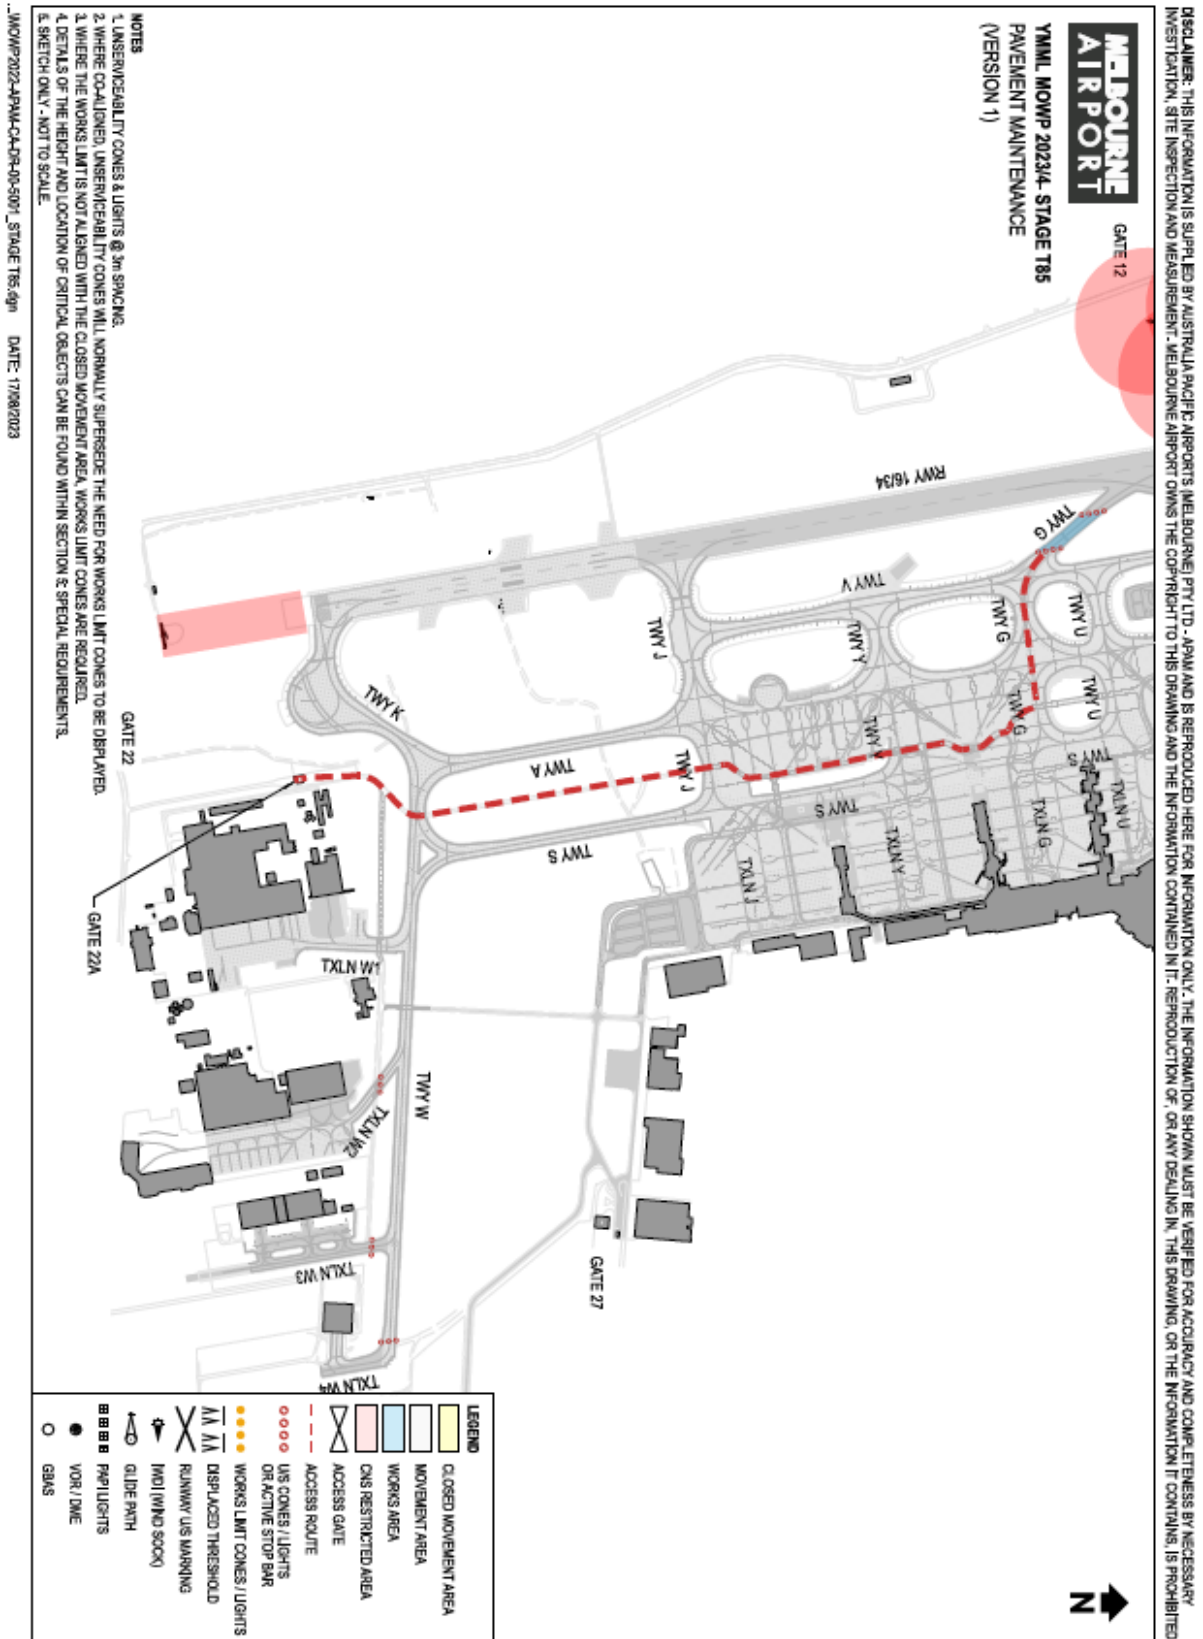


8.91. Stage T86

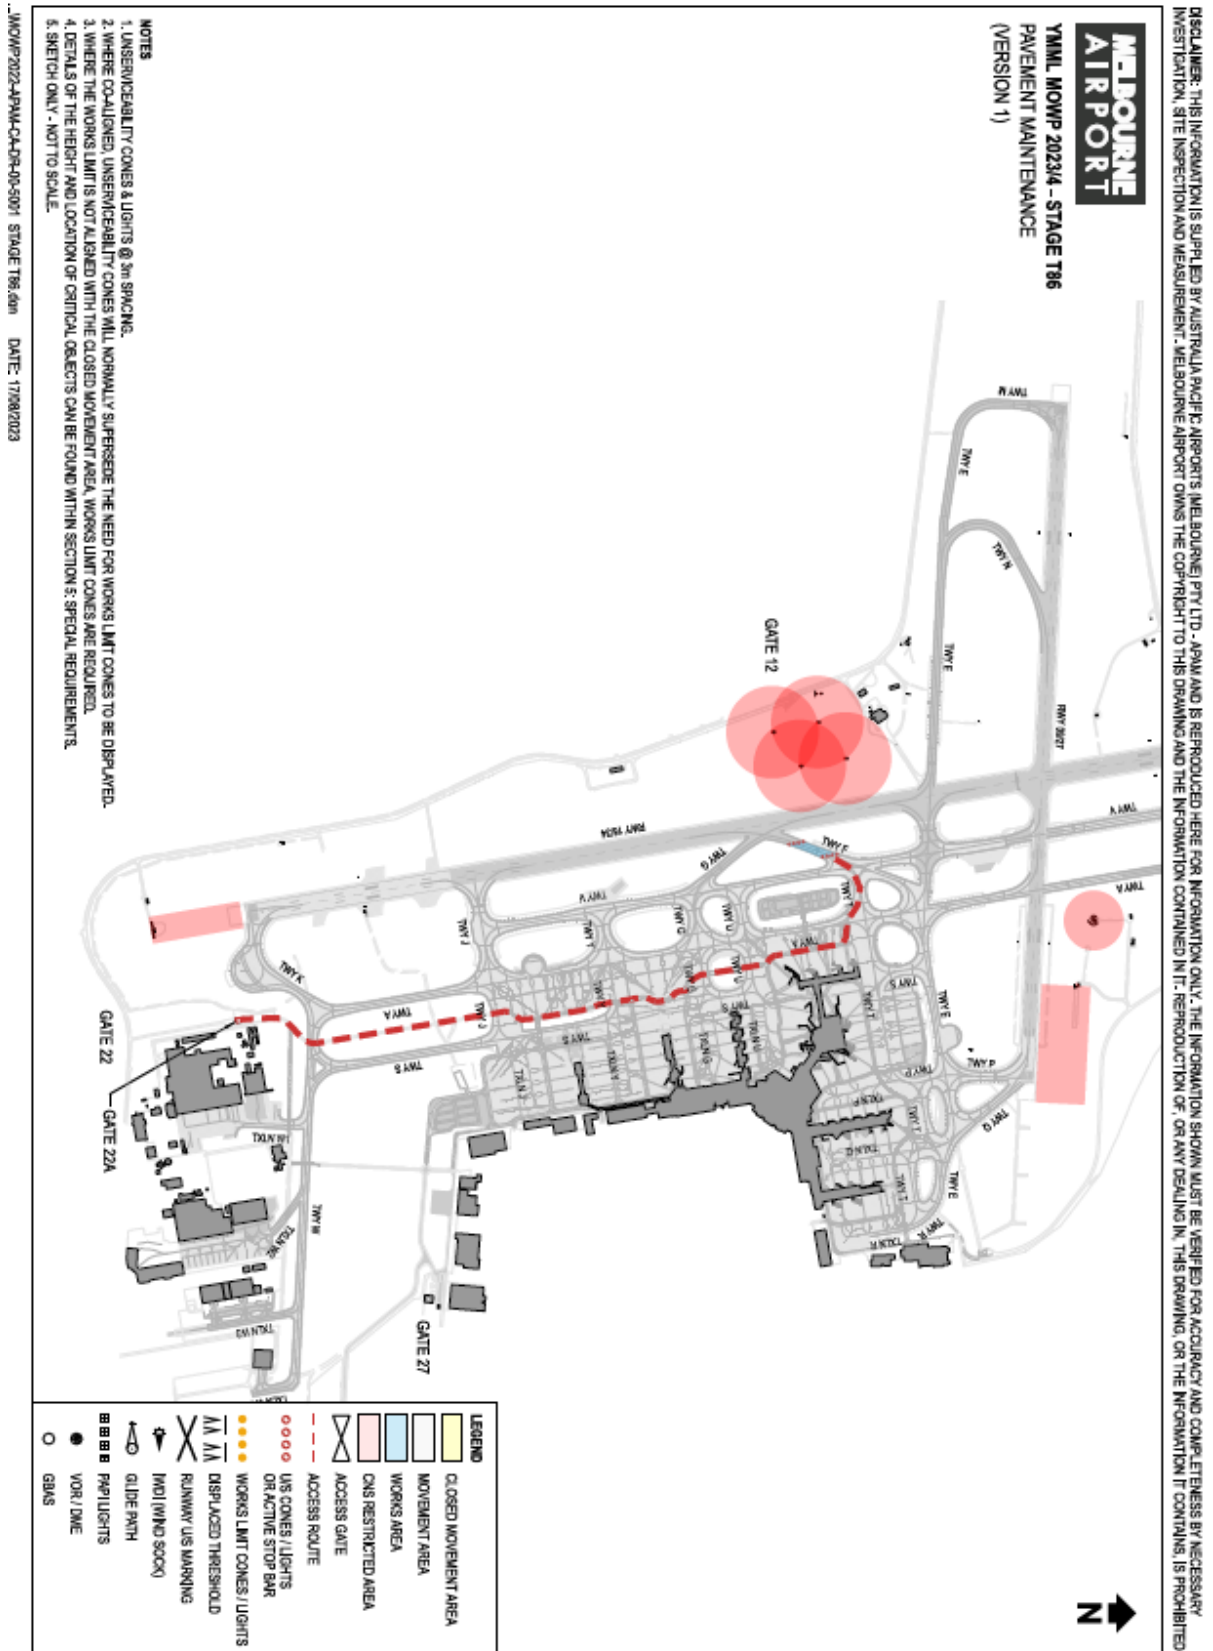


8.92. Stage T87

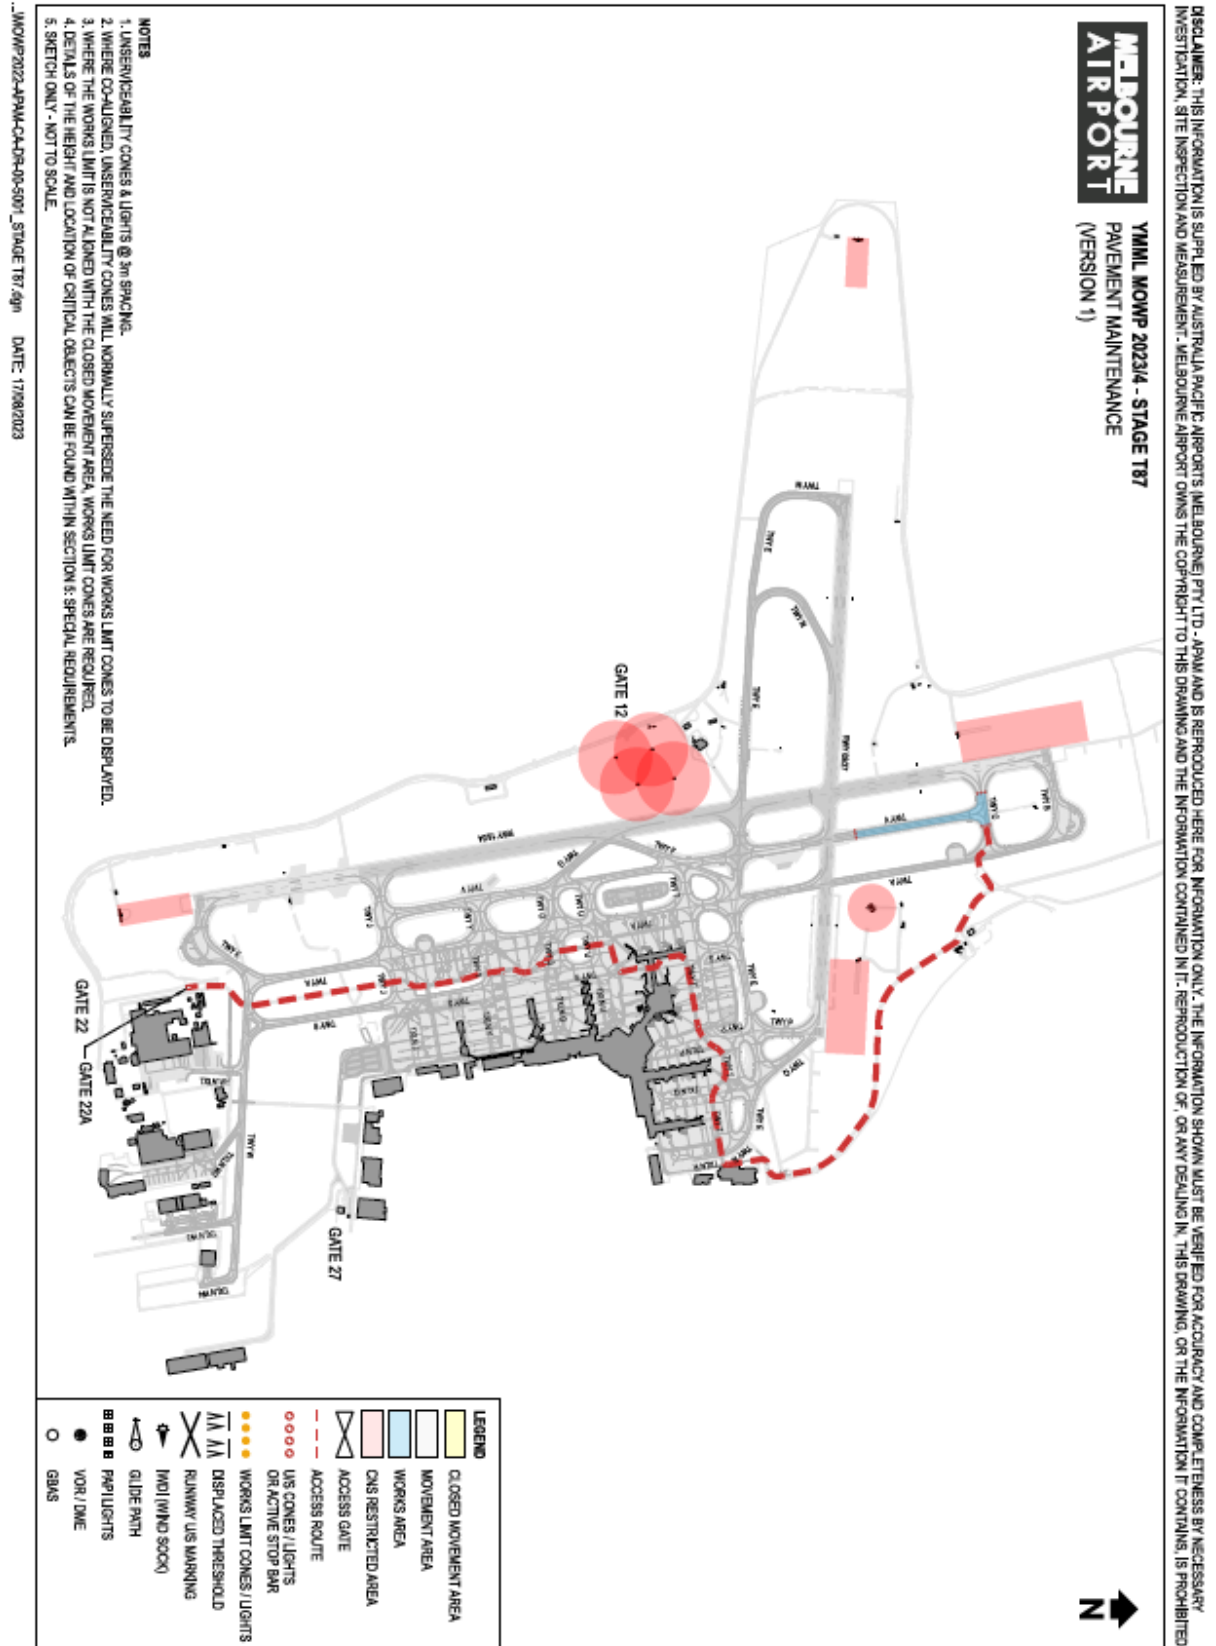


8.93. Stage T88

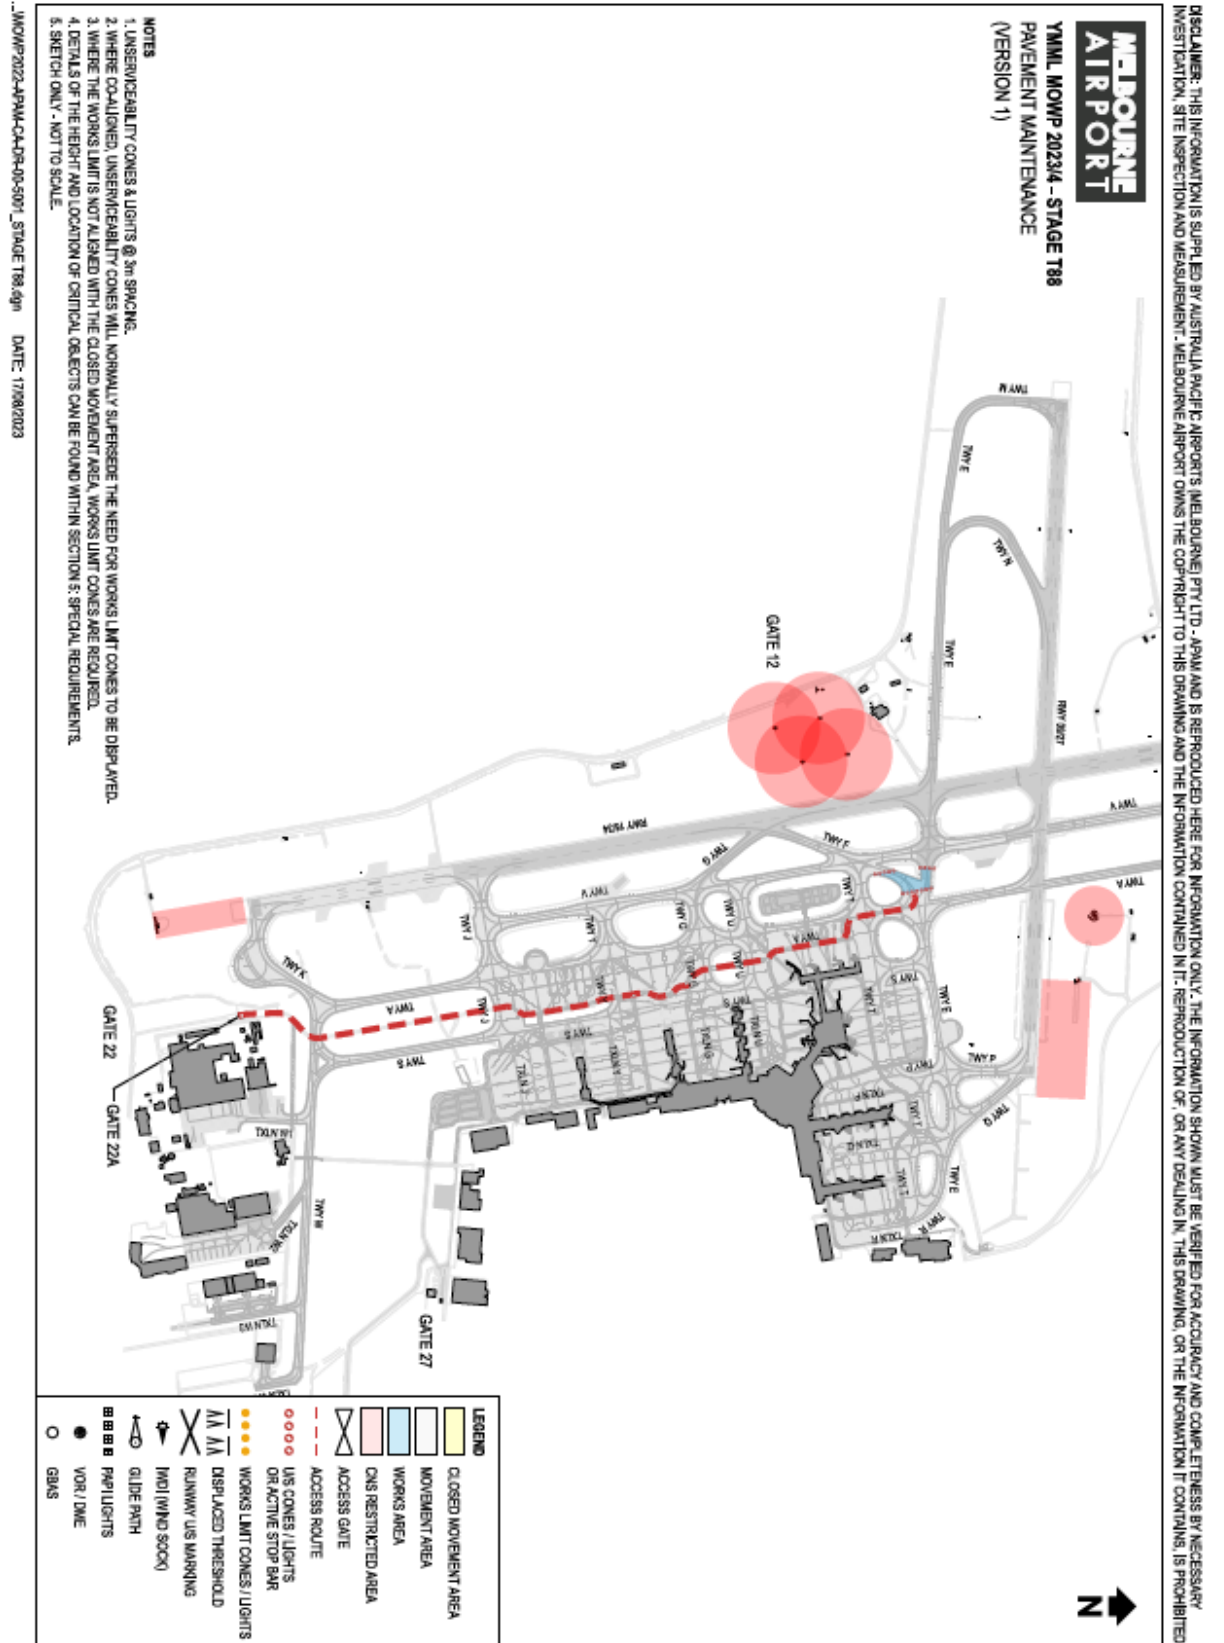

8.94. Stage T89

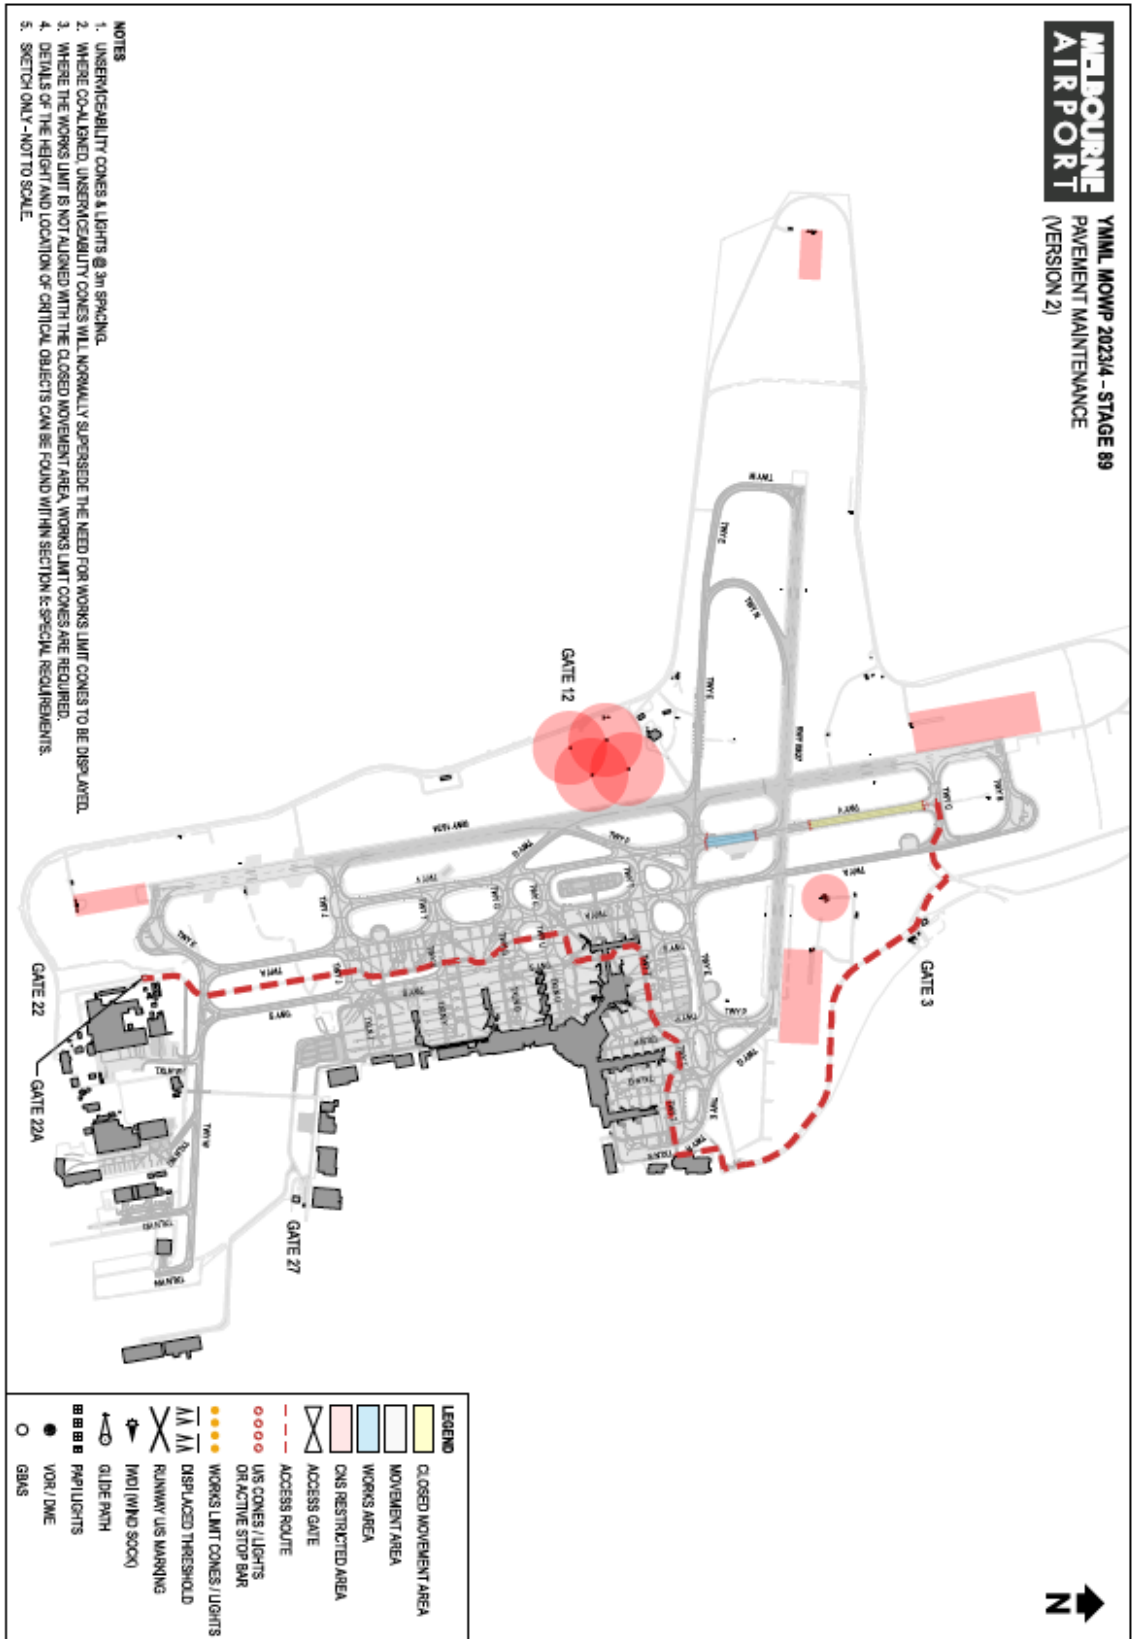

8.95. Stage T90

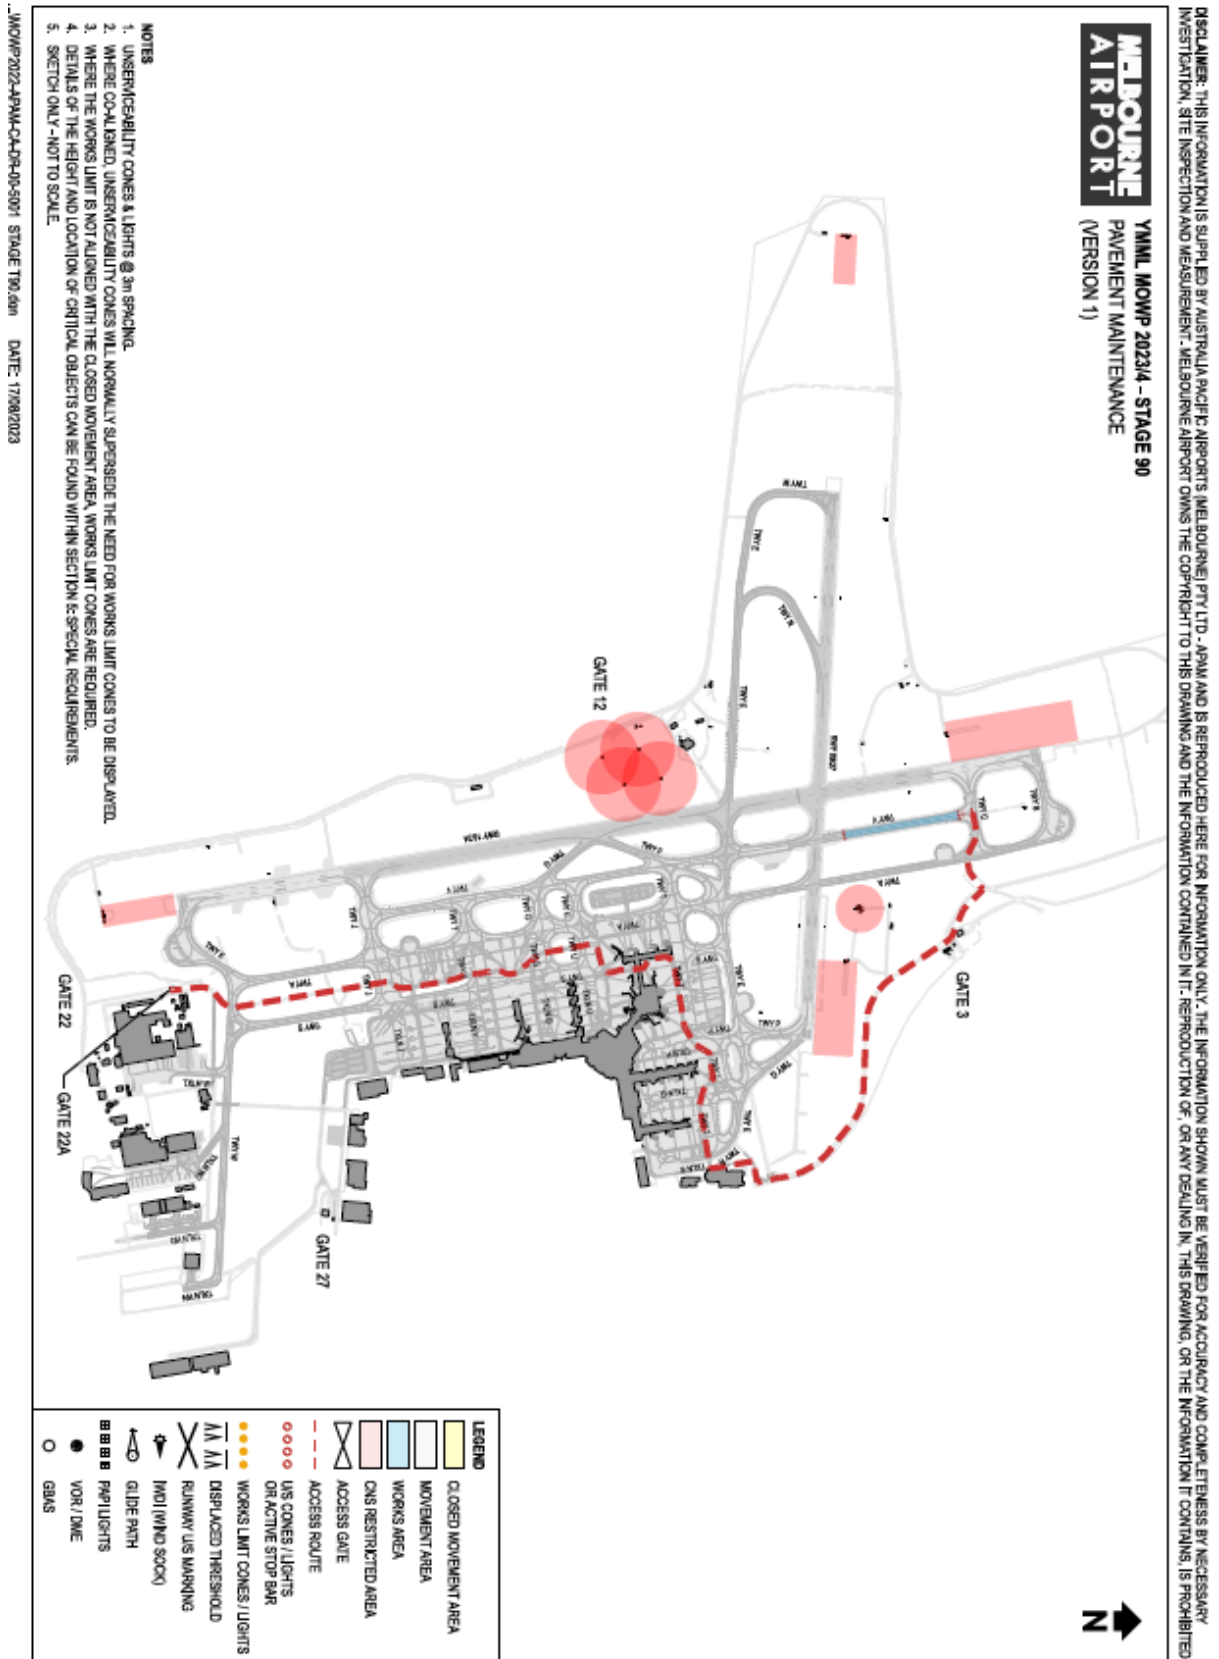

9. Distribution List

This MOWP will be distributed to the organisations and agencies listed below:

Air Asia	Etihad Airways	Royal Brunei Airlines
Air Asia X	Etihad Navigation	Scoot
Air Canada	Express Freighters Australia	Sharp Airlines
Air China	Fiji Airways	Sichuan Airlines
Air India	Garuda Indonesia	Singapore Airlines
Air New Zealand	Hainan Airlines	Skytanking
Air North	Heston MRO	Skytraders
Air Services	ISS Security	Sri Lankin Airlines
Air Vanuatu	Japan Airlines	Tasman Cargo
Airwork Flight Operations	Jepperson Australia Pty Ltd	Team Global Express
Atlas Air	Jet City Pty Ltd	Thai Airways International
Bamboo	Jetstar	Tianjin Airlines
Batik	Kalitta Air	United Airlines
Bejing Capital Airlines	Lufthansa Systems Flight Nav Inc	Victorian Police Air Wing
Bonza	Malaysia Airlines	Vietjet
Bureau of Meteorology	Malindo Air	Vietnam Airlines
Cathay Pacific	Melbourne Airport Precinct (MAP)	Virgin Australia
Cebu Pacific	Melbourne Airport	Viva Energy
China Airlines	Menzies Aviation Group	Xiamen Airlines
China Eastern Airlines	Oceania Aviation	
China Southern Airlines	Pel-air Aviation	
Civil Aviation Safety Authority	Philippine Airlines	
Department of Defence	Pionair	
DHL	Polar-Air/ Atlas	
Dnata Airport Services	Qantas Airways Limited	
Dnata	Qantas Link	
Emirates	Qatar Airways	
Essendon Fields	Regional Express	

The distribution list for this MOWP is maintained by the Airfield Operations and Works Coordinator.

9.1. Further Information

For further information with regards to this **Method of Working Plan**, please contact:

[Airfield Operations & Works Coordinators](#)
